REMT

REQUEST FOR INFORMATION

PROJECT	:	CADANGAN PEMBINAAN BALAI BOMBA DAN PENYELAMAT BEAUFORT SABAH					
ISSUED TO	:	KIA			ISSUED DATE	:	29.12.2020
ATTENTION	:	AR. NOOR IZWAN RAHIM			RF Info No.	:	RF Info/BOMBA/ 04
DESIGNATION	:	PRINCIPL					
C.C	:						
This RFI will Constitute	:	☐ Variation Oder	☐ Time Extension		☐ N/A	PIC Siganture	

INFORMATION REQUIRED :

1. Confirmation of finish floor level.

→ ± 9.85M finish level for porch area.
C & S drawing.

→ ± 0.00M at Archt drawing.

Date Required : ASAP

ISSUED BY
Name : RONNY BIN LESA
SITE AGENT
REMT UTAMA SDN. BHD.
Designation :

Acknowledgement of Receipt :
Name Ar. Noor Izwan Bin Rahim Date 30 December 2020

ATTACHMENT/RESPONSE :

For the floor finish level (FFL), please follow as per C&S drawing.

But you are responsible to make sure the drop from 'Ruang Lobi' to 'Anjung' is 50mm fall slope as per 'Cadangan Penambahbaikan Rekabentuk' drawing from us which has been agreed and approved by JBPM and USB KPKT.

AFK should provide to you their revised drawing pertaining to this different level between 'Ruang Lobi' and 'Anjung'.

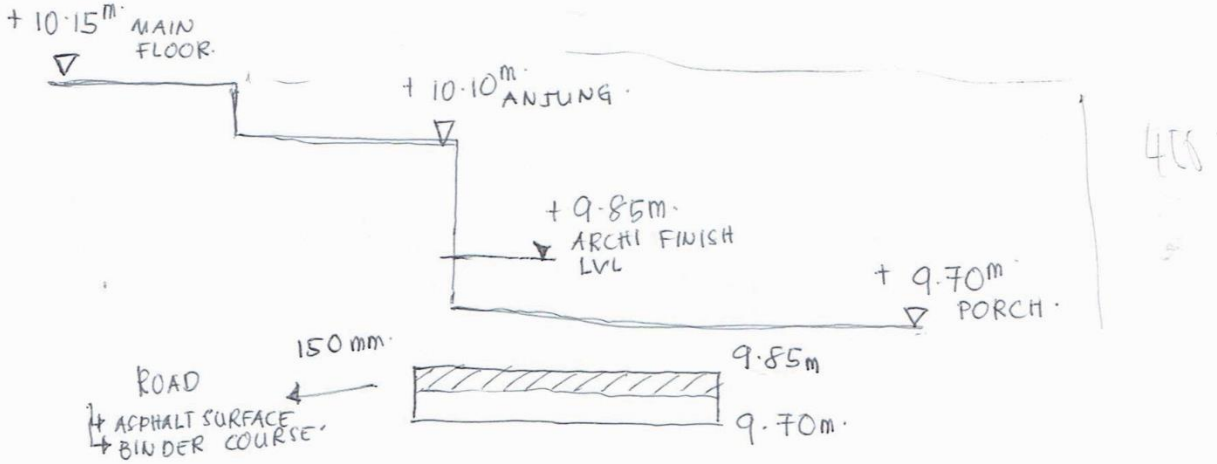
C.C : Aktif FA Konsult Sdn Bhd

Signature :
Name : Ar. Noor Izwan b. Rahim
Position : ARKITEK
No Pendaftaran LAM : A/N 157
Date : 30 December 2020

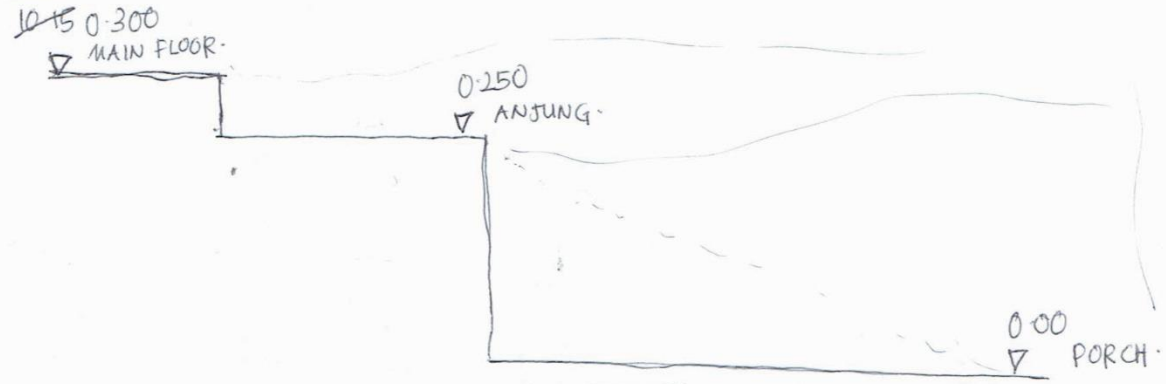
LEMBAGA ARKITEK MALAYSIA

noor izwan architect SP/N 157
Company Stamp

C&S.


+ 10.15m MAIN FLOOR.
+ 10.10m ANJUNG.
+ 9.85m. ARCHI FINISH LVL
+ 9.70m PORCH.
150 mm.
ROAD
ASPHALT SURFACE
BINDER COURSE.
9.85m
9.70m.

ARCHI.


~~10.15~~ 0.300
MAIN FLOOR.
0.250
ANJUNG.
0.00
PORCH.
