REMT

RFIT

REQUEST FOR INSPECTION AND TESTING

PROJECT :	CADANGAN PEMBINAAN BALAI BOMBA DAN PENYELAMAT BEAUFORT SABAH	PROJECT NO :	BOMBA-BEAUFORT
TO :	NCA	REF NO :	RFIT/BOMBA/21/10
ATTN. :	Syahril mohd. Ariffine.		

The following works / tests are ready for inspection / will be conducted at 2.00pm (time) on 11.3.2021 (date).

DESCRIPTION OF WORKS

Location : Rumah Sampah.

Nature of Work : inspection for brick wall guide line.

Sketches (if required) :

(Note : Where required, include details of materials, labour and plant / equipment to be used).

Submitted by		Received by COW / RE
Signature :	Site Agent	Signature :
Name :	Ronny Lesa RONNY BIN LESA SITE AGENT REMT UTAMA SDN. BHD.	Name :
Time/Date :	10.3.2021	Time/Date : 11/03/2021

c.c. 1 3

2 4

INSPECTION/TEST RESPONSE

☑	Inspection / Test acceptable / passed. Work are allowed to proceed.	Remarks /Remedial Works:
☐	Remedial works listed on the right to be completed but no further inspection required.	
☐	Remedial works listed on the right to be completed and re- inspection required on _____ (date) at _____ (time)	

Signature : (COW/RE)

Date : 11/03/2021

RE-INSPECTION/RE-TEST RESPONSE :

☐	Re-inspection / Re- test acceptable / passed. Work are allowed to proceed.	Remarks /Remedial Works:
☐	Further Remedial works listed on the right to be completed but no further inspection required.	


Signature : (COW/RE)

Date :


RFI : 10.

B(k wall guide line.


ck wall




1 PELAN LANTAI (RUMAH SAMPAH)
SCALE 1:100




6 PANDANGAN SISI
SCALE 1:100




6 PANDANGAN BELAKANG
SCALE 1:100



2 PELAN BUMBUNG
SCALE 1:100



3 KERATAN A - A
SCALE 1:100



4 PANDANGAN HADAPAN
SCALE 1:100

NOTA :

1. Lukisan Arkitek adalah indikatif tersahaja.
2. Semua ukuran mesti disemak dahulu tapak binaan, mana2 ukuran yang disebutkan tahap perlu diperiksa, sebagai pemberitahuan. Kontraktor bertanggung jawab kepada kerja kerja binaan dan struktur untuk berpuashati dgn Pihak Berkuasa Tempatan dan Pihak2 Utiliti berkenaan & Jabatan. Segala perbezaan tapak bina hendaklah dimaklum kepada Pegawai Penguasa.
3. Bahan binaan dinding mesti bertaraf dan berkualiti.

PETUNJUK

LANTAI

KOD	KETERANGAN
SC	100mm tbl. lantai konkrit bertetulang siap 150mm tbl. lapisan kerja yang rata bawah tanah (Rujukan)
LS	kerja simen 1/4 'water proofing' jenis 'cementitious' yg berkesan

DINDING

KOD	KETERANGAN
BT	200mm tbl. dinding konkrit tpg. 20mm tbl. kerja simen pada kedua permukaan atau seperti yang ditentukan.
BB	150mm tbl. dinding bata/batu dgn. 20mm tbl. kerja simen pada kedua permukaan atau seperti yang ditentukan.
CT	kerangka utk kerja cuaca (waterproof), pintu dan semua kerja ditutupi pihak kontrak. (Cara selaras mengikut Bahan Penyelia)


BUMBUNG


Kemasan Siling
SC - Skim coat

BUMBUNG

Kerangka bumbung

Kemasan bumbung

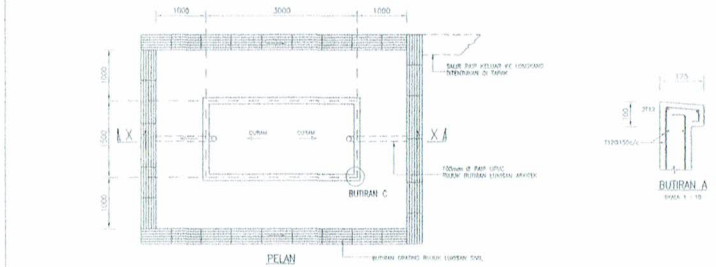



LUKISAN PEMBINAAN

Pelanggan

KEMENTERIAN PERUMAHAN DAN KERAJAAN TEMPATAN

Penulis Bangunan / Pengguna

JABATAN BOMBA DAN PENYELAMAT MALAYSIA

Agensi Pelaksana

KEMENTERIAN PERUMAHAN DAN KERAJAAN TEMPATAN
KPKT

Tajuk Projek

CADANGAN PEMBINAAN PROJEK
BALAI BOMBA DAN PENYELAMAT BEAUFORT, SABAH.

UNTUK TETUAN JABATAN BOMBA DAN PENYELAMAT MALAYSIA

Arkitek

Ar. Noor Izwar Rahim
ARKITEK
No. Pendaftaran LAM : AN 157

Juruterа Awam & Struktur

Juruterа Mekanikal & Elektrikal

Juru Ukur Bahan

Tajuk Lukisan

KOLAM AIR LATIHAN & RUMAH SAMPAH

PELAN LANTAI
KERATAN
PANDANGAN
BUTIRAN
