REMT UTAMA SDN BHD 409864-W

Engineering And Contracting

Ground Floor, Lot 20
Grace Square, Jln Pantai Sembulan,
P. O. Box 14722,
88100 Kota Kinabalu, Sabah.
Tel: 088-257308
Fax: 088-260869

E-mail: remt.utama.sb@gmail.com

Date : *10th December 2019*
Our Ref : *RUSB/AD.C-AKT (BOMBA.BFORT) (las)/1.1.2/19-002*

Noor Izwan Architect,
K-2-7, Block K, Lorong Metro 4,
Metro Town, Jalan Lintas,
88300 Kota Kinabalu,
Sabah
Attention : Ar. Noor Izwan Bin Rahim

Dear Sir,

CADANGAN PEMBINAAN PROJEK BALAI BOMBA DAN PENYELAMAT BEAUFORT, SABAH
NO KONTRAK : KPKT/CPPP/JBPM/14/15/2019
- Work Programmed and Organization Chart

Reference is made to the above matter.
We are pleased to submit herewith a copy of the followings for your approval.

(i) Work Programmed
(ii) Organization Chart

We trust the above submission is in order, should you require further clarification please do not hesitate to contact the under signed.

Thank you.

REMT UTAMA SDN BHD
(Syarikat berdaftar TERAJU – Program TeraS)

SHIR ZAMAN BIN FAZUL RAHMAN
GENERAL MANAGER

CC. : **Ir. Mohd Arzahri Bin Abd Rahman**
Director,
Aktif FA Konsult Sdn Bhd
Lot 17 & 19, 2nd Floor, Block C,
Damai Plaza Phase 4,
Jalan Damai, Luyang, 88859 Kota Kinabalu,
Sabah.


: **Ir. Sherman Bin Daim**
Project Director,
Jurutera Perunding Intelek Sdn Bhd,
No.22-2, 2nd Floor, Block D,
Lorong Plaza Kingfisher 6,
Plaza Kingfisher, Kuala Inanam Likas,
88400 Kota Kinabalu,
Sabah.

: **Sr. Kent Pan**
Principal,
PQS Setia Konsult,
Shop No.1-2 , 2nd Floor, Block B,
Damai Plaza Phase 4,
Jalan Damai, Luyang,
88300 Kota Kinabalu,
Sabah.


CADANGAN PEMBINAAN PROJEK BALAI BOMBA DAN PENYELAMAT BEAUFORT, SABAH

NO. KONTRAK : KPKT/CPPP/JBPM/14/15/2019

Carta Organisasi Pengurusan Projek

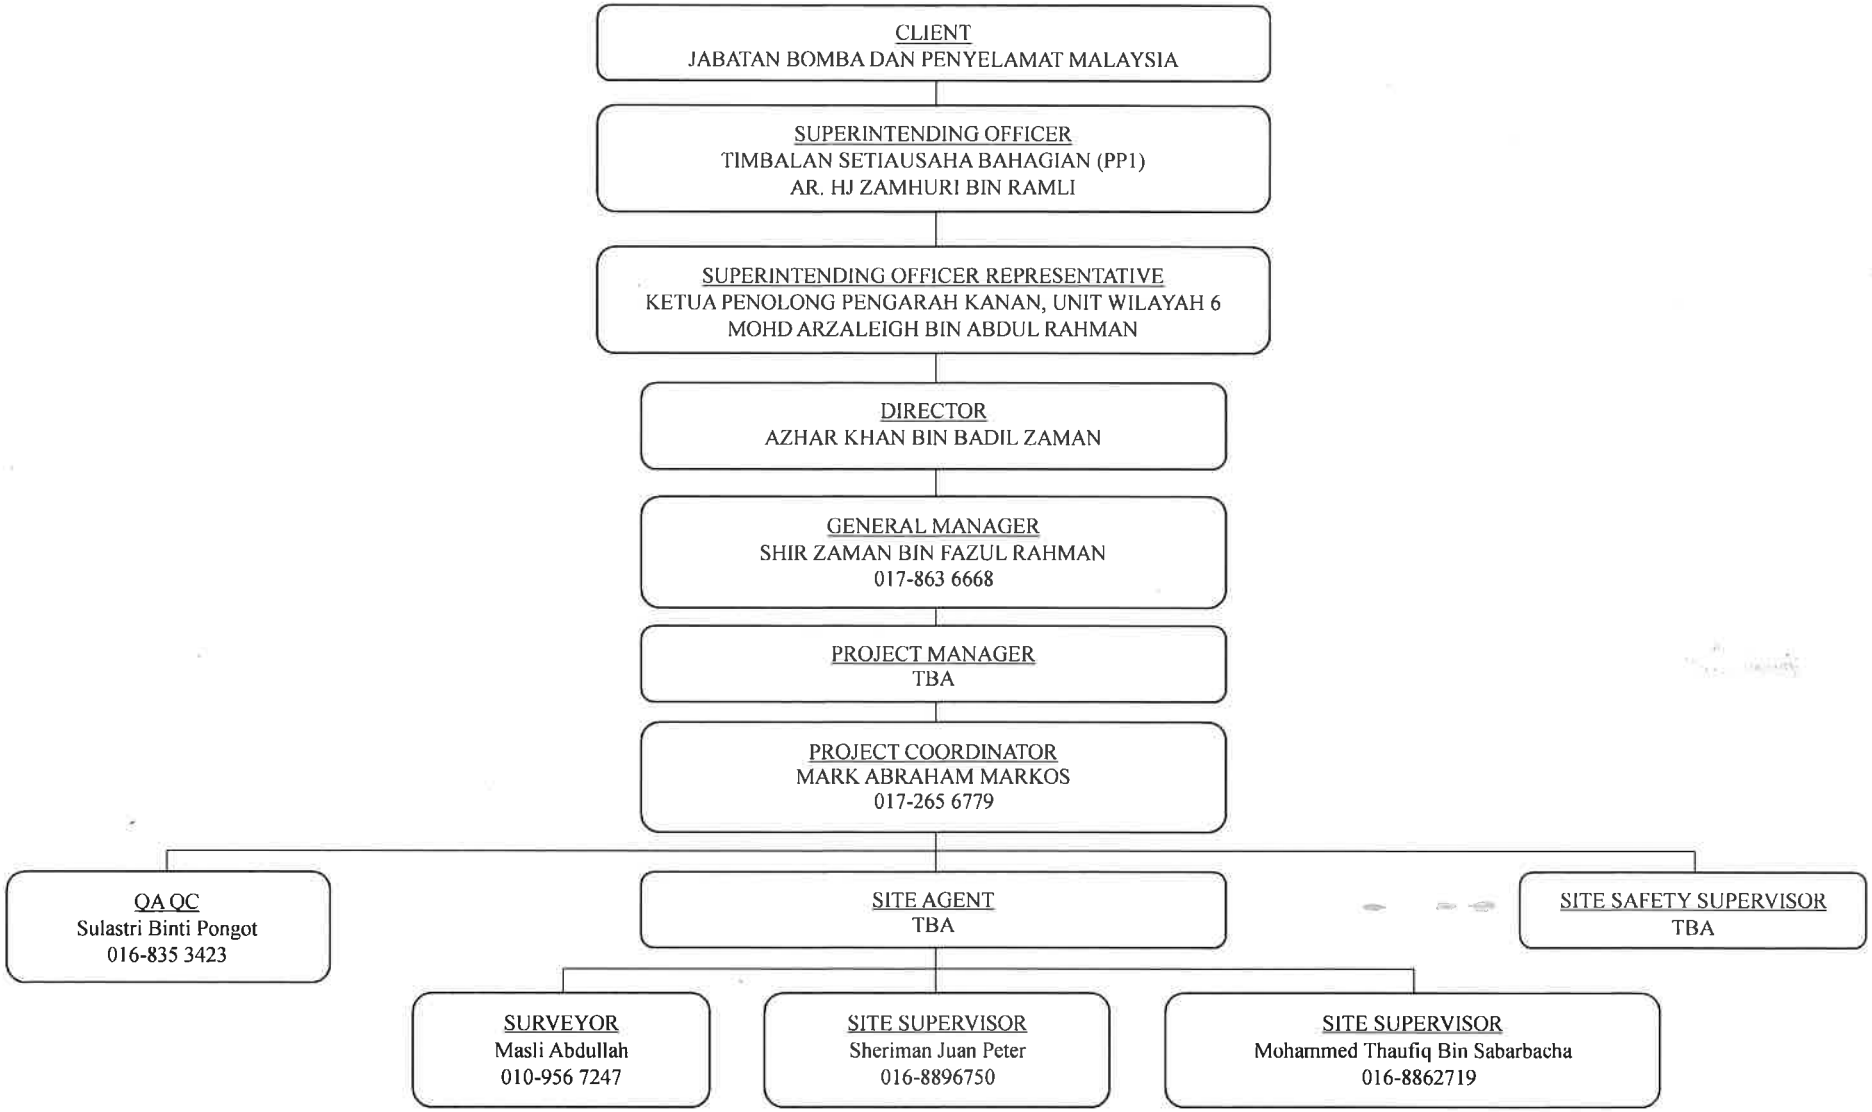


ID	WBS	Task Name	Duration	Start	Finish
1	1	**CADANGAN PEMBINAAN PROJEK BALAI BOMBA DAN PENYELAMAT BEAUFORT, SABAH**	**546 days**	**Tue 12-11-19**	**Mon 10-05-21**
2	1.1	PROJECT START	0 days	Tue 12-11-19	Tue 12-11-19
3	1.2	**PRELIMINARIES**	**546 days**	**Tue 12-11-19**	**Mon 10-05-21**
28	1.3	**SITE PREPARATION, EARTHWORKS AND ASSOCIATED WORKS**	**65 days**	**Tue 12-11-19**	**Wed 15-01-20**
29	1.3.1	Site Clearing	30 days	Tue 12-11-19	Wed 11-12-19
30	1.3.2	Cut and Fill to Formation Level	20 days	Thu 12-12-19	Tue 31-12-19
31	1.3.3	Temporary Earth Drain	15 days	Wed 01-01-20	Wed 15-01-20
32	1.4	**PILING WORKS**	**132 days**	**Tue 26-11-19**	**Sun 05-04-20**
33	1.4.1	Submission of Pile Catalogue, Plant, Equipment and Pile Set Criteria	14 days	Tue 26-11-19	Mon 09-12-19
34	1.4.2	Mobilization of Plant & Equipment	7 days	Wed 01-01-20	Tue 07-01-20
35	1.4.3	Initial Pile Driving for MLT and PDA Test	3 days	Wed 08-01-20	Fri 10-01-20
36	1.4.4	MLT Pile Testing	14 days	Sat 11-01-20	Fri 24-01-20
37	1.4.5	PDA Pile Testing	3 days	Sat 25-01-20	Mon 27-01-20
38	1.4.6	Submission of Pile Testing Report	5 days	Tue 28-01-20	Sat 01-02-20
39	1.4.7	**Supply and Delivery of Piles**	**10 days**	**Sun 02-02-20**	**Tue 11-02-20**
40	1.4.7.1	Menara Latihan	10 days	Sun 02-02-20	Tue 11-02-20
41	1.4.7.2	Entrance Signage	10 days	Sun 02-02-20	Tue 11-02-20
42	1.4.7.3	Entrance Culvert	10 days	Sun 02-02-20	Tue 11-02-20
43	1.4.7.4	Drainage	10 days	Sun 02-02-20	Tue 11-02-20
44	1.4.8	**Pile Driving & Jointing**	**54 days**	**Wed 12-02-20**	**Sun 05-04-20**
45	1.4.8.1	**Menara Latihan (50 Pile Points)**	**21 days**	**Wed 12-02-20**	**Tue 03-03-20**
46	1.4.8.1.1	Pile Points Setting Out	2 days	Wed 12-02-20	Thu 13-02-20
47	1.4.8.1.2	Pile Driving & Jointing	5 days	Fri 14-02-20	Tue 18-02-20
48	1.4.8.1.3	Excavation of Pile caps	3 days	Wed 19-02-20	Fri 21-02-20
49	1.4.8.1.4	Cut off Pile Head	5 days	Sat 22-02-20	Wed 26-02-20
50	1.4.8.1.5	Cut Off piles survey	3 days	Thu 27-02-20	Sat 29-02-20
51	1.4.8.1.6	Submission of Complete Piling Records	3 days	Sun 01-03-20	Tue 03-03-20
52	1.4.8.2	**Entrance Signage (14 Pile Points)**	**20 days**	**Fri 14-02-20**	**Wed 04-03-20**
53	1.4.8.2.1	Pile Points Setting Out	1 day	Fri 14-02-20	Fri 14-02-20
54	1.4.8.2.2	Pile Driving & Jointing	3 days	Sat 22-02-20	Mon 24-02-20
55	1.4.8.2.3	Excavation of Pile caps	2 days	Tue 25-02-20	Wed 26-02-20
56	1.4.8.2.4	Cut off Pile Head	3 days	Thu 27-02-20	Sat 29-02-20
57	1.4.8.2.5	Cut Off piles survey	2 days	Sun 01-03-20	Mon 02-03-20
58	1.4.8.2.6	Submission of Complete Piling Records	2 days	Tue 03-03-20	Wed 04-03-20
59	1.4.8.3	**Entrance Culvert (60 Pile Points)**	**33 days**	**Sat 15-02-20**	**Wed 18-03-20**
60	1.4.8.3.1	Pile Points Setting Out	3 days	Sat 15-02-20	Mon 17-02-20
61	1.4.8.3.2	Pile Driving & Jointing	6 days	Tue 25-02-20	Sun 01-03-20
62	1.4.8.3.3	Excavation of Pile caps	5 days	Mon 02-03-20	Fri 06-03-20
63	1.4.8.3.4	Cut off Pile Head	7 days	Sat 07-03-20	Fri 13-03-20
64	1.4.8.3.5	Cut Off piles survey	3 days	Sat 14-03-20	Mon 16-03-20
65	1.4.8.3.6	Submission of Complete Piling Records	2 days	Tue 17-03-20	Wed 18-03-20
66	1.4.8.4	**Drainage (64 Pile Points)**	**39 days**	**Tue 18-02-20**	**Fri 27-03-20**
67	1.4.8.4.1	Pile Points Setting Out	3 days	Tue 18-02-20	Thu 20-02-20
68	1.4.8.4.2	Pile Driving & Jointing	7 days	Mon 02-03-20	Sun 08-03-20
69	1.4.8.4.3	Excavation of Pile caps	6 days	Mon 09-03-20	Sat 14-03-20
70	1.4.8.4.4	Cut off Pile Head	8 days	Sun 15-03-20	Sun 22-03-20
71	1.4.8.4.5	Cut Off piles survey	3 days	Mon 23-03-20	Wed 25-03-20
72	1.4.8.4.6	Submission of Complete Piling Records	2 days	Thu 26-03-20	Fri 27-03-20
73	1.4.8.5	**Piling As Built Drawings**	**9 days**	**Sat 28-03-20**	**Sun 05-04-20**
74	1.4.8.5.1	Preparation and Endorsement of Piling As Built Survey	7 days	Sat 28-03-20	Fri 03-04-20
75	1.4.8.5.2	Submission of piling As Built Survey	2 days	Sat 04-04-20	Sun 05-04-20
76	1.5	**BUILDING WORKS**	**453 days**	**Thu 16-01-20**	**Mon 12-04-21**
77	1.5.1	**BANGUNAN BALAI BOMBA**	**372 days**	**Thu 16-01-20**	**Thu 21-01-21**
78	1.5.1.1	**Structural Works**	**134 days**	**Thu 16-01-20**	**Thu 28-05-20**
79	1.5.1.1.1	**Pad Footings and RC Stump**	**39 days**	**Thu 16-01-20**	**Sun 23-02-20**
80	1.5.1.1.1.1	Building Setting out & Survey	3 days	Thu 16-01-20	Sat 18-01-20
81	1.5.1.1.1.2	Excavation of Pad Footings	7 days	Sun 19-01-20	Sat 25-01-20
82	1.5.1.1.1.3	Lean Concrete	3 days	Sun 26-01-20	Tue 28-01-20
83	1.5.1.1.1.4	Installation of Formwork and Reinforcement Bar to Pad Footings/Pile Caps and Stump	14 days	Sun 26-01-20	Sat 08-02-20
84	1.5.1.1.1.5	Concreting Works of Pad Footings/Pile Caps	7 days	Sun 09-02-20	Sat 15-02-20
85	1.5.1.1.1.6	Installation of Stumps F/works & Rebars	3 days	Sun 16-02-20	Tue 18-02-20
86	1.5.1.1.1.7	Concreting Works for Stumps	2 days	Wed 19-02-20	Thu 20-02-20
87	1.5.1.1.1.8	Backfilling & Compaction	3 days	Fri 21-02-20	Sun 23-02-20
88	1.5.1.1.2	**Ground Beam Structures**	**22 days**	**Mon 24-02-20**	**Mon 16-03-20**
89	1.5.1.1.2.1	Anti Termite Treatment	1 day	Mon 24-02-20	Mon 24-02-20
90	1.5.1.1.2.2	Lean Concrete	3 days	Tue 25-02-20	Thu 27-02-20
91	1.5.1.1.2.3	Installation of F/works and Rebars for Ground Beam	10 days	Fri 28-02-20	Sun 08-03-20
92	1.5.1.1.2.4	Concreting Works for Fround Beams	5 days	Mon 09-03-20	Fri 13-03-20
93	1.5.1.1.2.5	Backfilling and Compaction	3 days	Sat 14-03-20	Mon 16-03-20
94	1.5.1.1.3	**Ground Slab**	**13 days**	**Tue 17-03-20**	**Sun 29-03-20**
95	1.5.1.1.3.1	Anti Termite Treatment	1 day	Tue 17-03-20	Tue 17-03-20
96	1.5.1.1.3.2	Installation of F/works	2 days	Wed 18-03-20	Thu 19-03-20
97	1.5.1.1.3.3	Damp Proof Membrane	2 days	Fri 20-03-20	Sat 21-03-20

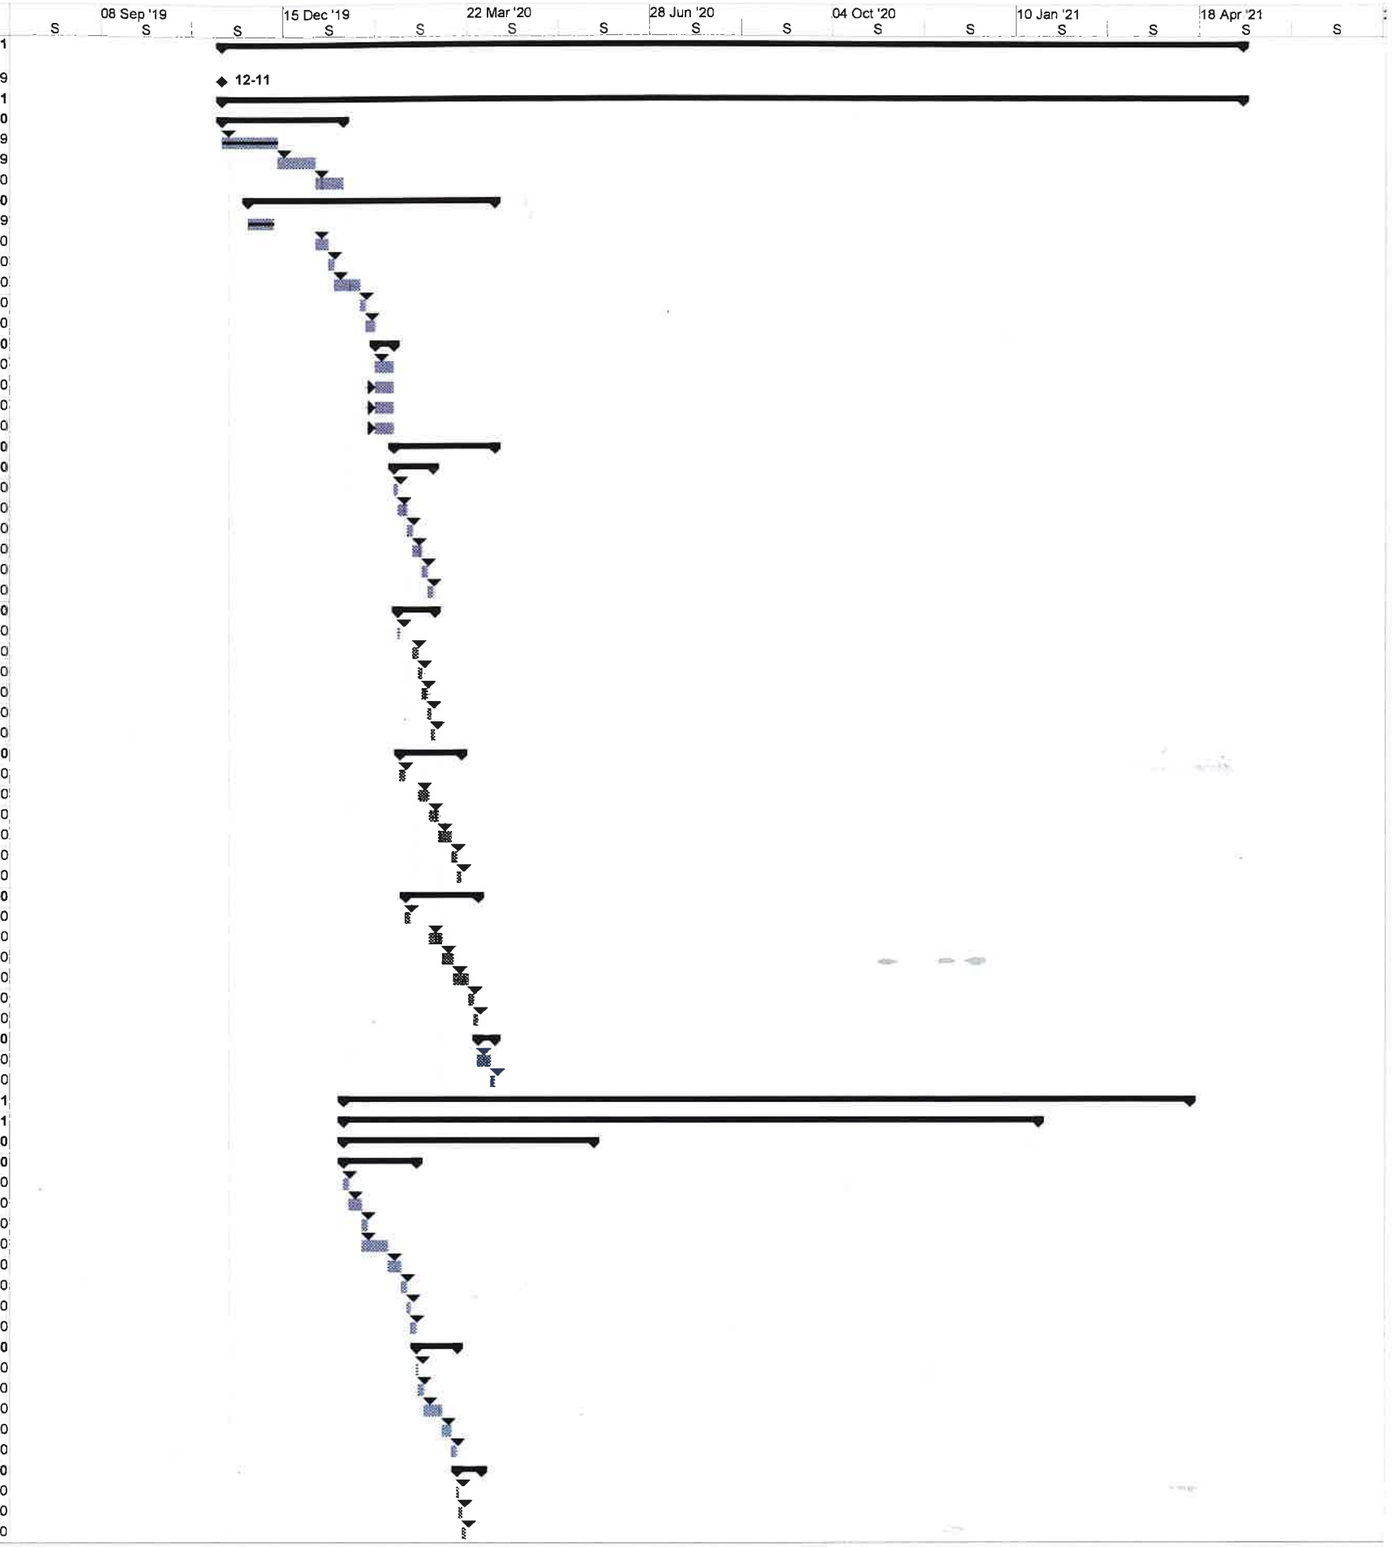

Project: CPM Slp Recovery Ver. 8.0
Date: Tue 10-12-19

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Progress | Deadline


ID	WBS	Task Name	Duration	Start	Finish
98	1.5.1.1.3.4	Installation of Re-bars	5 days	Sun 22-03-20	Thu 26-03-20
99	1.5.1.1.3.5	Concreting of Ground Slab	3 days	Fri 27-03-20	Sun 29-03-20
100	**1.5.1.1.4**	**Apron Slab**	**7 days**	**Mon 30-03-20**	**Sun 05-04-20**
101	1.5.1.1.4.1	Anti Termite Treatment	1 day	Mon 30-03-20	Mon 30-03-20
102	1.5.1.1.4.2	Installation of F/works	1 day	Tue 31-03-20	Tue 31-03-20
103	1.5.1.1.4.3	Damp Proof Membrane	1 day	Wed 01-04-20	Wed 01-04-20
104	1.5.1.1.4.4	Installation of Re-bars	2 days	Thu 02-04-20	Fri 03-04-20
105	1.5.1.1.4.5	Concreting of Apron Slab	2 days	Sat 04-04-20	Sun 05-04-20
106	**1.5.1.1.5**	**Ramp Slab**	**8 days**	**Mon 06-04-20**	**Mon 13-04-20**
107	1.5.1.1.5.1	Anti Termite Treatment	1 day	Mon 06-04-20	Mon 06-04-20
108	1.5.1.1.5.2	Installation of F/works	3 days	Tue 07-04-20	Thu 09-04-20
109	1.5.1.1.5.3	Damp Proof Membrane	1 day	Fri 10-04-20	Fri 10-04-20
110	1.5.1.1.5.4	Installation of Re-bars	2 days	Sat 11-04-20	Sun 12-04-20
111	1.5.1.1.5.5	Concreting of Ramp Slab	1 day	Mon 13-04-20	Mon 13-04-20
112	**1.5.1.1.6**	**Ground Floor - 1st Floor Columns**	**9 days**	**Tue 14-04-20**	**Wed 22-04-20**
113	1.5.1.1.6.1	Installation of Formworks and Rebars	7 days	Tue 14-04-20	Mon 20-04-20
114	1.5.1.1.6.2	Concreting Works	2 days	Tue 21-04-20	Wed 22-04-20
115	**1.5.1.1.7**	**1st Floor Slab**	**12 days**	**Thu 23-04-20**	**Mon 04-05-20**
116	1.5.1.1.7.1	Installation of F/works & Rebars	10 days	Thu 23-04-20	Sat 02-05-20
117	1.5.1.1.7.2	Concreting Works	2 days	Sun 03-05-20	Mon 04-05-20
118	**1.5.1.1.8**	**RC Staircase**	**9 days**	**Tue 05-05-20**	**Wed 13-05-20**
119	1.5.1.1.8.1	Installation of F/works & Re-Bars	7 days	Tue 05-05-20	Mon 11-05-20
120	1.5.1.1.8.2	Concreting Works	2 days	Tue 12-05-20	Wed 13-05-20
121	**1.5.1.1.9**	**1st Floor to Roof Beam Columns**	**9 days**	**Tue 05-05-20**	**Wed 13-05-20**
122	1.5.1.1.9.1	Installation of Formworks and Rebars	7 days	Tue 05-05-20	Mon 11-05-20
123	1.5.1.1.9.2	Concreting Works	2 days	Tue 12-05-20	Wed 13-05-20
124	**1.5.1.1.10**	**RC Roof Beams, RC Flat Roof and Hoods**	**15 days**	**Thu 14-05-20**	**Thu 28-05-20**
125	1.5.1.1.10.1	Installation of F/works & Rebars	12 days	Thu 14-05-20	Mon 25-05-20
126	1.5.1.1.10.2	Concreting Works	3 days	Tue 26-05-20	Thu 28-05-20
127	**1.5.1.2**	**Installation of Roofing System**	**41 days**	**Fri 29-05-20**	**Wed 08-07-20**
128	1.5.1.2.1	Installation of Roof Trusses, Rafters, Battens, Purlins and all necessary Structural Items	20 days	Fri 29-05-20	Wed 17-06-20
129	1.5.1.2.2	Intallation of Roof Covering; including Aluminium Foil Insulation, Chicken Wire Mesh, Facia Board, Gutter and other necessary finishes.	14 days	Thu 18-06-20	Wed 01-07-20
130	1.5.1.2.3	Rainwater Downpipes (RWDP)	7 days	Thu 02-07-20	Wed 08-07-20
131	**1.5.1.3**	**Architectural Works**	**111 days**	**Thu 02-07-20**	**Tue 20-10-20**
132	1.5.1.3.1	Internal and External Brickwall (Bricklaying and Plastering Works)	45 days	Thu 02-07-20	Sat 15-08-20
133	1.5.1.3.2	Internal and External Floor Finishes.	14 days	Sun 16-08-20	Sat 29-08-20
134	1.5.1.3.3	Installation of Doors Windows and Ironmongeries	14 days	Sun 30-08-20	Sat 12-09-20
135	1.5.1.3.4	External and Internal Wall Finishes	14 days	Sun 13-09-20	Sat 26-09-20
136	1.5.1.3.5	Internal Ceiling Finishes	14 days	Sun 27-09-20	Sat 10-10-20
137	1.5.1.3.6	External Ceiling Finishes	10 days	Sun 11-10-20	Tue 20-10-20
138	1.5.1.3.7	Installation of Sanitary Fittings and Appliances	10 days	Sun 11-10-20	Tue 20-10-20
139	**1.5.1.4**	**Electrical Works**	**237 days**	**Thu 23-04-20**	**Tue 15-12-20**
140	**1.5.1.4.1**	**Electrical Services for Internal Wiring**	**195 days**	**Thu 23-04-20**	**Tue 03-11-20**
141	1.5.1.4.1.1	Installation of Conduits as Specified	120 days	Thu 23-04-20	Thu 20-08-20
142	1.5.1.4.1.2	Installation of Internal Cables	14 days	Sun 13-09-20	Sat 26-09-20
143	1.5.1.4.1.3	Installation of Electrical accessories and Finishes (Lightings, Fans Etc)	14 days	Wed 21-10-20	Tue 03-11-20
144	1.5.1.4.2	Telephone Services for Internal works	7 days	Wed 04-11-20	Tue 10-11-20
145	1.5.1.4.3	Lightning Protection System	7 days	Wed 11-11-20	Tue 17-11-20
146	1.5.1.4.4	Extra Low Voltage System	14 days	Wed 18-11-20	Tue 01-12-20
147	1.5.1.4.5	Generating Set System	14 days	Wed 02-12-20	Tue 15-12-20
148	**1.5.1.5**	**Mechanical Works**	**152 days**	**Sun 16-08-20**	**Thu 14-01-21**
149	1.5.1.5.1	Internal Cold WaterPlumbing Services	55 days	Sun 16-08-20	Fri 09-10-20
150	1.5.1.5.2	Internal Sanitary plumbing Services	55 days	Sun 16-08-20	Fri 09-10-20
151	1.5.1.5.3	Air Conditioning and mechanical System	14 days	Wed 16-12-20	Tue 29-12-20
152	1.5.1.5.4	Fire Protection Services	14 days	Wed 30-12-20	Tue 12-01-21
153	1.5.1.5.5	Motorized Roller Shutter	2 days	Wed 13-01-21	Thu 14-01-21
154	1.5.1.6	Testing & Commisioning	7 days	Fri 15-01-21	Thu 21-01-21
155	**1.5.2**	**MENARA LATIHAN**	**366 days**	**Wed 04-03-20**	**Thu 04-03-21**
156	**1.5.2.1**	**Structural Works**	**249 days**	**Wed 04-03-20**	**Sat 07-11-20**
157	**1.5.2.1.1**	**Pile Caps and RC Stump**	**35 days**	**Wed 04-03-20**	**Tue 07-04-20**
158	1.5.2.1.1.1	Lean Concrete	3 days	Wed 04-03-20	Fri 06-03-20
159	1.5.2.1.1.2	Installation of Formwork and Reinforcement Bar to Pile Caps	14 days	Sat 07-03-20	Fri 20-03-20
160	1.5.2.1.1.3	Concreting Works of Pad Footings/Pile Caps	7 days	Sat 21-03-20	Fri 27-03-20
161	1.5.2.1.1.4	Installation of Stumps F/works & Rebars	4 days	Sat 28-03-20	Tue 31-03-20
162	1.5.2.1.1.5	Concreting Works for Stumps	2 days	Wed 01-04-20	Thu 02-04-20
163	1.5.2.1.1.6	Backfilling & Compaction	5 days	Fri 03-04-20	Tue 07-04-20
164	**1.5.2.1.2**	**Ground Beam Structures**	**18 days**	**Wed 08-04-20**	**Sat 25-04-20**
165	1.5.2.1.2.1	Anti Termite Treatment	1 day	Wed 08-04-20	Wed 08-04-20
166	1.5.2.1.2.2	Lean Concrete	2 days	Thu 09-04-20	Fri 10-04-20
167	1.5.2.1.2.3	Installation of F/works and Rebars for Ground Beam	10 days	Sat 11-04-20	Mon 20-04-20
168	1.5.2.1.2.4	Concreting Works for Ground Beams	3 days	Tue 21-04-20	Thu 23-04-20
169	1.5.2.1.2.5	Backfilling and Compaction	2 days	Fri 24-04-20	Sat 25-04-20
170	**1.5.2.1.3**	**Ground Slab**	**11 days**	**Sun 26-04-20**	**Wed 06-05-20**

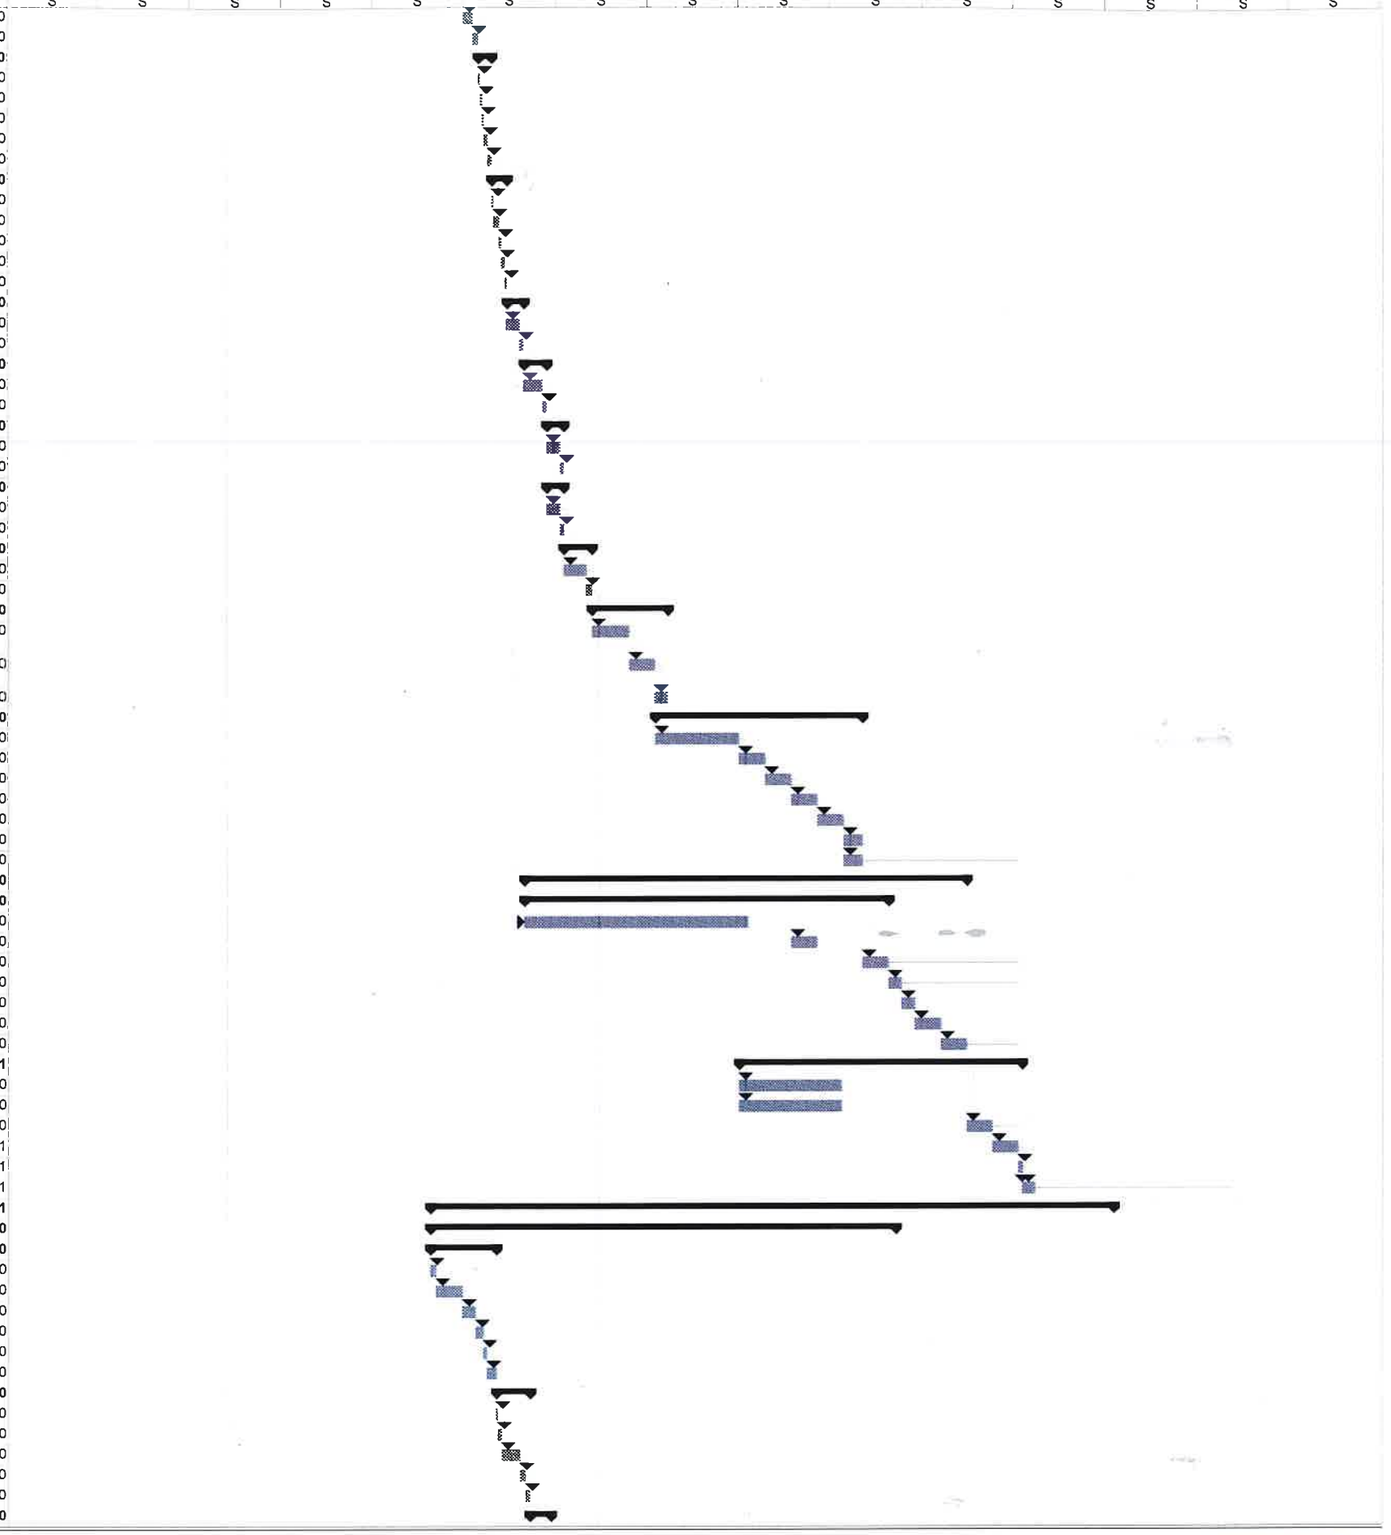

Project: CPM Slp Recovery Ver. 8.0
Date: Tue 10-12-19

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Progress | Deadline


ID	WBS	Task Name	Duration	Start	Finish
171	1.5.2.1.3.1	Anti Termite Treatment	1 day	Sun 26-04-20	Sun 26-04-20
172	1.5.2.1.3.2	Installation of F/works	2 days	Mon 27-04-20	Tue 28-04-20
173	1.5.2.1.3.3	Damp Proof Membrane	2 days	Wed 29-04-20	Thu 30-04-20
174	1.5.2.1.3.4	Installation of Re-bars	4 days	Fri 01-05-20	Mon 04-05-20
175	1.5.2.1.3.5	Concreting of Ground Slab	2 days	Tue 05-05-20	Wed 06-05-20
176	**1.5.2.1.4**	**Apron Slab**	**10 days**	**Thu 07-05-20**	**Sat 16-05-20**
177	1.5.2.1.4.1	Anti Termite Treatment	1 day	Thu 07-05-20	Thu 07-05-20
178	1.5.2.1.4.2	Installation of F/works	2 days	Fri 08-05-20	Sat 09-05-20
179	1.5.2.1.4.3	Damp Proof Membrane	1 day	Sun 10-05-20	Sun 10-05-20
180	1.5.2.1.4.4	Installation of Re-bars	4 days	Mon 11-05-20	Thu 14-05-20
181	1.5.2.1.4.5	Concreting of Apron Slab	2 days	Fri 15-05-20	Sat 16-05-20
182	**1.5.2.1.5**	**Ground Floor - 1st Floor Columns**	**9 days**	**Sun 17-05-20**	**Mon 25-05-20**
183	1.5.2.1.5.1	Installation of Formworks and Rebars	7 days	Sun 17-05-20	Sat 23-05-20
184	1.5.2.1.5.2	Concreting Works	2 days	Sun 24-05-20	Mon 25-05-20
185	**1.5.2.1.6**	**1st Floor R.C Beam & Floor Slab**	**12 days**	**Tue 26-05-20**	**Sat 06-06-20**
186	1.5.2.1.6.1	Installation of F/works & Rebars	10 days	Tue 26-05-20	Thu 04-06-20
187	1.5.2.1.6.2	Concreting Works	2 days	Fri 05-06-20	Sat 06-06-20
188	**1.5.2.1.7**	**RC Staircase (GF -1st FL)**	**8 days**	**Sun 07-06-20**	**Sun 14-06-20**
189	1.5.2.1.7.1	Installation of F/works & Re-Bars	7 days	Sun 07-06-20	Sat 13-06-20
190	1.5.2.1.7.2	Concreting of RC Staircase	1 day	Sun 14-06-20	Sun 14-06-20
191	**1.5.2.1.8**	**1st Floor - 2nd Floor Columns**	**9 days**	**Mon 15-06-20**	**Tue 23-06-20**
192	1.5.2.1.8.1	Installation of Formworks and Rebars	7 days	Mon 15-06-20	Sun 21-06-20
193	1.5.2.1.8.2	Concreting Works	2 days	Mon 22-06-20	Tue 23-06-20
194	**1.5.2.1.9**	**2nd Floor R.C Beam & Slab**	**12 days**	**Wed 24-06-20**	**Sun 05-07-20**
195	1.5.2.1.9.1	Installation of F/works & Rebars	10 days	Wed 24-06-20	Fri 03-07-20
196	1.5.2.1.9.2	Concreting Works	2 days	Sat 04-07-20	Sun 05-07-20
197	**1.5.2.1.10**	**RC Staircase (1st -2nd FL)**	**8 days**	**Mon 06-07-20**	**Mon 13-07-20**
198	1.5.2.1.10.1	Installation of F/works & Re-Bars	7 days	Mon 06-07-20	Sun 12-07-20
199	1.5.2.1.10.2	Concreting of RC Staircase	1 day	Mon 13-07-20	Mon 13-07-20
200	**1.5.2.1.11**	**2nd Floor - 3rd Floor Columns**	**9 days**	**Tue 14-07-20**	**Wed 22-07-20**
201	1.5.2.1.11.1	Installation of Formworks and Rebars	7 days	Tue 14-07-20	Mon 20-07-20
202	1.5.2.1.11.2	Concreting Works	2 days	Tue 21-07-20	Wed 22-07-20
203	**1.5.2.1.12**	**3rd Floor R.C Beam & Slab**	**12 days**	**Thu 23-07-20**	**Mon 03-08-20**
204	1.5.2.1.12.1	Installation of F/works & Rebars	10 days	Thu 23-07-20	Sat 01-08-20
205	1.5.2.1.12.2	Concreting Works	2 days	Sun 02-08-20	Mon 03-08-20
206	**1.5.2.1.13**	**RC Staircase (2nd -3rd FL)**	**8 days**	**Tue 04-08-20**	**Tue 11-08-20**
207	1.5.2.1.13.1	Installation of F/works & Re-Bars	7 days	Tue 04-08-20	Mon 10-08-20
208	1.5.2.1.13.2	Concreting of RC Staircase	1 day	Tue 11-08-20	Tue 11-08-20
209	**1.5.2.1.14**	**3rd Floor - 4th Floor Columns**	**9 days**	**Wed 12-08-20**	**Thu 20-08-20**
210	1.5.2.1.14.1	Installation of Formworks and Rebars	7 days	Wed 12-08-20	Tue 18-08-20
211	1.5.2.1.14.2	Concreting Works	2 days	Wed 19-08-20	Thu 20-08-20
212	**1.5.2.1.15**	**4th Floor R.C Beam & Slab**	**12 days**	**Fri 21-08-20**	**Tue 01-09-20**
213	1.5.2.1.15.1	Installation of F/works & Rebars	10 days	Fri 21-08-20	Sun 30-08-20
214	1.5.2.1.15.2	Concreting Works	2 days	Mon 31-08-20	Tue 01-09-20
215	**1.5.2.1.16**	**RC Staircase (3rd -4th FL)**	**8 days**	**Wed 02-09-20**	**Wed 09-09-20**
216	1.5.2.1.16.1	Installation of F/works & Re-Bars	7 days	Wed 02-09-20	Tue 08-09-20
217	1.5.2.1.16.2	Concreting of RC Staircase	1 day	Wed 09-09-20	Wed 09-09-20
218	**1.5.2.1.17**	**4th Floor - 5th Floor Columns**	**9 days**	**Thu 10-09-20**	**Fri 18-09-20**
219	1.5.2.1.17.1	Installation of Formworks and Rebars	7 days	Thu 10-09-20	Wed 16-09-20
220	1.5.2.1.17.2	Concreting Works	2 days	Thu 17-09-20	Fri 18-09-20
221	**1.5.2.1.18**	**5th Floor R.C Beam & Slab**	**12 days**	**Sat 19-09-20**	**Wed 30-09-20**
222	1.5.2.1.18.1	Installation of F/works & Rebars	10 days	Sat 19-09-20	Mon 28-09-20
223	1.5.2.1.18.2	Concreting Works	2 days	Tue 29-09-20	Wed 30-09-20
224	**1.5.2.1.19**	**RC Staircase (4th -5th FL)**	**8 days**	**Thu 01-10-20**	**Thu 08-10-20**
225	1.5.2.1.19.1	Installation of F/works & Re-Bars	7 days	Thu 01-10-20	Wed 07-10-20
226	1.5.2.1.19.2	Concreting of RC Staircase	1 day	Thu 08-10-20	Thu 08-10-20
227	**1.5.2.1.20**	**5th Floor - Roof Level Columns**	**9 days**	**Fri 09-10-20**	**Sat 17-10-20**
228	1.5.2.1.20.1	Installation of Formworks and Rebars	7 days	Fri 09-10-20	Thu 15-10-20
229	1.5.2.1.20.2	Concreting Works	2 days	Fri 16-10-20	Sat 17-10-20
230	**1.5.2.1.21**	**Roof R.C Beam & Slab**	**12 days**	**Sun 18-10-20**	**Thu 29-10-20**
231	1.5.2.1.21.1	Installation of F/works & Rebars	10 days	Sun 18-10-20	Tue 27-10-20
232	1.5.2.1.21.2	Concreting Works	2 days	Wed 28-10-20	Thu 29-10-20
233	**1.5.2.1.22**	**RC Staircase (5th -Roof Level)**	**9 days**	**Fri 30-10-20**	**Sat 07-11-20**
234	1.5.2.1.22.1	Installation of F/works & Re-Bars	7 days	Fri 30-10-20	Thu 05-11-20
235	1.5.2.1.22.2	Concreting of RC Staircase	2 days	Fri 06-11-20	Sat 07-11-20
236	**1.5.2.2**	**Architectural Works**	**100 days**	**Sun 08-11-20**	**Mon 15-02-21**
237	1.5.2.2.1	Brickwall	30 days	Sun 08-11-20	Mon 07-12-20
238	1.5.2.2.2	External Doors and windows	14 days	Tue 08-12-20	Mon 21-12-20
239	1.5.2.2.3	Internal finishes	21 days	Tue 22-12-20	Mon 11-01-21
240	1.5.2.2.4	External Finishes	21 days	Tue 12-01-21	Mon 01-02-21
241	1.5.2.2.5	Wall Climbing Sytem	14 days	Tue 02-02-21	Mon 15-02-21
242	1.5.2.3	Electrical Works	14 days	Tue 16-02-21	Mon 01-03-21
243	1.5.2.4	Mechanical Works	14 days	Tue 16-02-21	Mon 01-03-21
244	1.5.2.5	Testing & Commisioning	3 days	Tue 02-03-21	Thu 04-03-21

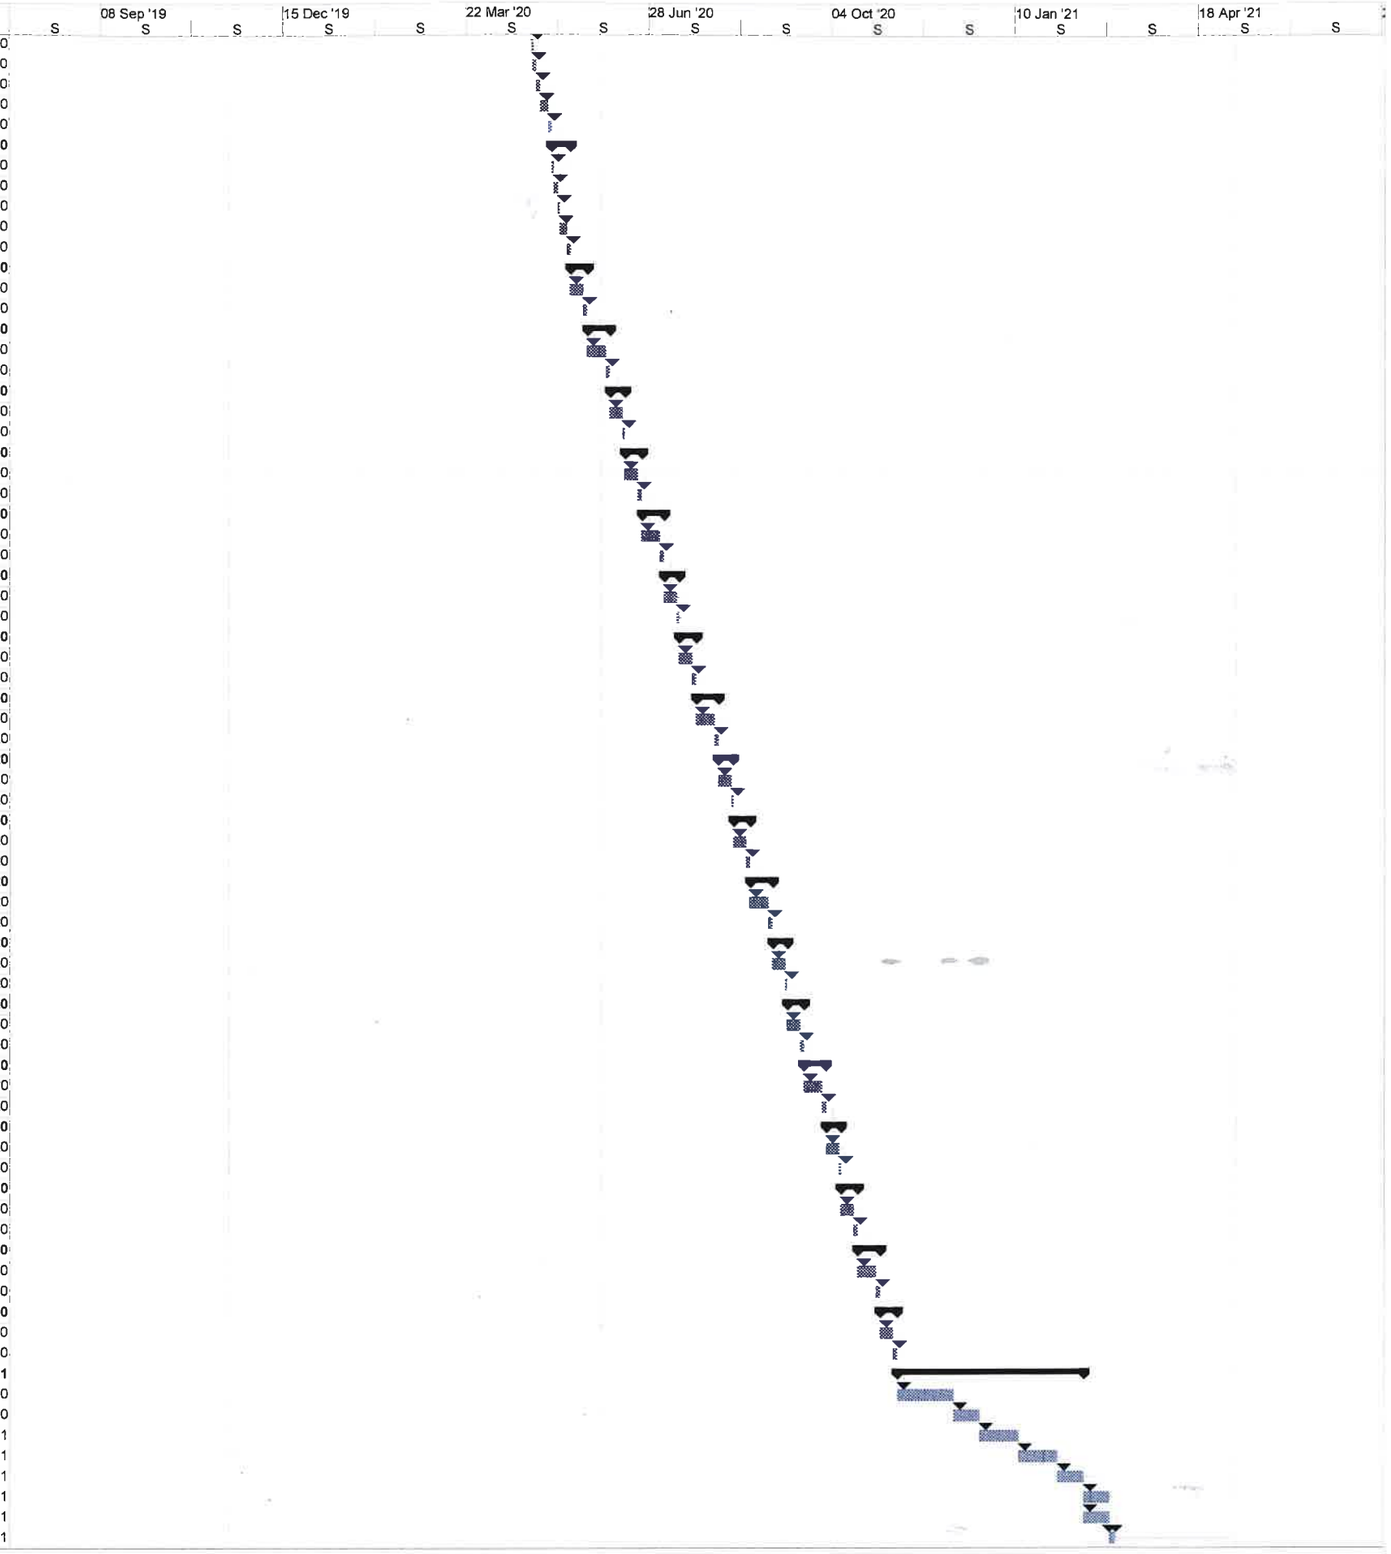

Project: CPM Slp Recovery Ver. 8.0
Date: Tue 10-12-19

Task | Summary | External Milestone | Inactive Milestone | Duration-only | Start-only | External Milestone
Split | Project Summary | Inactive Task | Inactive Summary | Manual Summary Rollup | Finish-only | Progress
Milestone | External Tasks | Inactive Milestone | Manual Task | Manual Summary | External Tasks | Deadline


ID	WBS	Task Name	Duration	Start	Finish
245	**1.5.3**	**BANGUNAN STOR LOGISTIK**	**46 days**	**Fri 22-01-21**	**Mon 08-03-21**
246	**1.5.3.1**	**Structural**	**24 days**	**Fri 22-01-21**	**Sun 14-02-21**
247	**1.5.3.1.1**	**Pad Footings, Pile Caps and RC Stump**	**9 days**	**Fri 22-01-21**	**Sat 30-01-21**
248	1.5.3.1.1.1	Excavations	1 day	Fri 22-01-21	Fri 22-01-21
249	1.5.3.1.1.2	Lean Concrete	1 day	Sat 23-01-21	Sat 23-01-21
250	1.5.3.1.1.3	Installation of Formwork and Reinforcement Bar to Pad Footings/Pile Caps and Stum	2 days	Sun 24-01-21	Mon 25-01-21
251	1.5.3.1.1.4	Concreting Works of Pad Footings	2 days	Tue 26-01-21	Wed 27-01-21
252	1.5.3.1.1.5	Installation of Stumps F/works & Rebars	1 day	Thu 28-01-21	Thu 28-01-21
253	1.5.3.1.1.6	Concreting Works for Stumps	1 day	Fri 29-01-21	Fri 29-01-21
254	1.5.3.1.1.7	Backfilling & Compaction	1 day	Sat 30-01-21	Sat 30-01-21
255	**1.5.3.1.2**	**Ground Beam Structures**	**6 days**	**Sun 31-01-21**	**Fri 05-02-21**
256	1.5.3.1.2.1	Anti Termite Treatment	1 day	Sun 31-01-21	Sun 31-01-21
257	1.5.3.1.2.2	Lean Concrete	1 day	Mon 01-02-21	Mon 01-02-21
258	1.5.3.1.2.3	Installation of F/works and Rebars for Ground Beam	2 days	Tue 02-02-21	Wed 03-02-21
259	1.5.3.1.2.4	Concreting Works for Fround Beams	1 day	Thu 04-02-21	Thu 04-02-21
260	1.5.3.1.2.5	Backfilling and Compaction	1 day	Fri 05-02-21	Fri 05-02-21
261	**1.5.3.1.3**	**Ground Slab**	**5 days**	**Sat 06-02-21**	**Wed 10-02-21**
262	1.5.3.1.3.1	Anti Termite Treatment	1 day	Sat 06-02-21	Sat 06-02-21
263	1.5.3.1.3.2	Installation of F/works	1 day	Sun 07-02-21	Sun 07-02-21
264	1.5.3.1.3.3	Damp Proof Membrane	1 day	Mon 08-02-21	Mon 08-02-21
265	1.5.3.1.3.4	Installation of Re-bars	1 day	Tue 09-02-21	Tue 09-02-21
266	1.5.3.1.3.5	Concreting of Ground Slab	1 day	Wed 10-02-21	Wed 10-02-21
267	**1.5.3.1.4**	**Ground Floor - Roof Beam Columns**	**2 days**	**Thu 11-02-21**	**Fri 12-02-21**
268	1.5.3.1.4.1	Installation of Formworks and Rebars	1 day	Thu 11-02-21	Thu 11-02-21
269	1.5.3.1.4.2	Concreting Works	1 day	Fri 12-02-21	Fri 12-02-21
270	**1.5.3.1.5**	**RC Roof Beams**	**2 days**	**Sat 13-02-21**	**Sun 14-02-21**
271	1.5.3.1.5.1	Installation of F/works & Rebars	1 day	Sat 13-02-21	Sat 13-02-21
272	1.5.3.1.5.2	Concreting Works	1 day	Sun 14-02-21	Sun 14-02-21
273	**1.5.3.2**	**Installation of Roofing System**	**5 days**	**Mon 15-02-21**	**Fri 19-02-21**
274	1.5.3.2.1	Installation of Roof Trusses, Rafters, Battens, Purlins and all necessary Structural Items	2 days	Mon 15-02-21	Tue 16-02-21
275	1.5.3.2.2	Intallation of Roof Covering; including Aluminium Foil Insulation, Chicken Wire Mesh, Fa	2 days	Wed 17-02-21	Thu 18-02-21
276	1.5.3.2.3	Rainwater Downpipes (RWDP)	1 day	Fri 19-02-21	Fri 19-02-21
277	**1.5.3.3**	**Architectural Works**	**10 days**	**Sat 20-02-21**	**Mon 01-03-21**
278	1.5.3.3.1	Internal and External Brickwall (Bricklaying and Plastering Works)	2 days	Sat 20-02-21	Sun 21-02-21
279	1.5.3.3.2	Internal and External Floor Finishes.	1 day	Mon 22-02-21	Mon 22-02-21
280	1.5.3.3.3	Installation of Doors Windows and Ironmongeries	1 day	Tue 23-02-21	Tue 23-02-21
281	1.5.3.3.4	External and Internal Wall Finishes	2 days	Wed 24-02-21	Thu 25-02-21
282	1.5.3.3.5	Internal Ceiling Finishes	2 days	Fri 26-02-21	Sat 27-02-21
283	1.5.3.3.6	External Ceiling Finishes	2 days	Sun 28-02-21	Mon 01-03-21
284	**1.5.3.4**	**Electrical & Mechanical Services**	**6 days**	**Tue 02-03-21**	**Sun 07-03-21**
285	1.5.3.4.1	Electrical Services	3 days	Tue 02-03-21	Thu 04-03-21
286	1.5.3.4.2	Mechanical Services	3 days	Fri 05-03-21	Sun 07-03-21
287	1.5.3.5	Testing & Commisioning	1 day	Mon 08-03-21	Mon 08-03-21
288	**1.5.4**	**BANGUNAN RUMAH PAM**	**48 days**	**Fri 29-05-20**	**Wed 15-07-20**
289	**1.5.4.1**	**Structural**	**26 days**	**Fri 29-05-20**	**Tue 23-06-20**
290	**1.5.4.1.1**	**Pad Footings & RC Stump**	**9 days**	**Fri 29-05-20**	**Sat 06-06-20**
291	1.5.4.1.1.1	Excavation	1 day	Fri 29-05-20	Fri 29-05-20
292	1.5.4.1.1.2	Lean Concrete	1 day	Sat 30-05-20	Sat 30-05-20
293	1.5.4.1.1.3	Installation of Formwork and Reinforcement Bar to Pad Footings/Pile Caps and Stum	3 days	Sun 31-05-20	Tue 02-06-20
294	1.5.4.1.1.4	Concreting Works of Pad Footings/Pile Caps	1 day	Wed 03-06-20	Wed 03-06-20
295	1.5.4.1.1.5	Installation of Stumps F/works & Rebars	1 day	Thu 04-06-20	Thu 04-06-20
296	1.5.4.1.1.6	Concreting Works for Stumps	1 day	Fri 05-06-20	Fri 05-06-20
297	1.5.4.1.1.7	Backfilling & Compaction	1 day	Sat 06-06-20	Sat 06-06-20
298	**1.5.4.1.2**	**Ground Beam Structures**	**6 days**	**Sun 07-06-20**	**Fri 12-06-20**
299	1.5.4.1.2.1	Anti Termite Treatment	1 day	Sun 07-06-20	Sun 07-06-20
300	1.5.4.1.2.2	Lean Concrete	1 day	Mon 08-06-20	Mon 08-06-20
301	1.5.4.1.2.3	Installation of F/works and Rebars for Ground Beam	2 days	Tue 09-06-20	Wed 10-06-20
302	1.5.4.1.2.4	Concreting Works for Fround Beams	1 day	Thu 11-06-20	Thu 11-06-20
303	1.5.4.1.2.5	Backfilling and Compaction	1 day	Fri 12-06-20	Fri 12-06-20
304	**1.5.4.1.3**	**Ground Slab**	**5 days**	**Sat 13-06-20**	**Wed 17-06-20**
305	1.5.4.1.3.1	Anti Termite Treatment	1 day	Sat 13-06-20	Sat 13-06-20
306	1.5.4.1.3.2	Installation of F/works	1 day	Sun 14-06-20	Sun 14-06-20
307	1.5.4.1.3.3	Damp Proof Membrane	1 day	Mon 15-06-20	Mon 15-06-20
308	1.5.4.1.3.4	Installation of Re-bars	1 day	Tue 16-06-20	Tue 16-06-20
309	1.5.4.1.3.5	Concreting of Ground Slab	1 day	Wed 17-06-20	Wed 17-06-20
310	**1.5.4.1.4**	**Ground Floor - Roof Beam Columns**	**3 days**	**Thu 18-06-20**	**Sat 20-06-20**
311	1.5.4.1.4.1	Installation of Formworks and Rebars	2 days	Thu 18-06-20	Fri 19-06-20
312	1.5.4.1.4.2	Concreting Works	1 day	Sat 20-06-20	Sat 20-06-20
313	**1.5.4.1.5**	**RC Roof Beams**	**3 days**	**Sun 21-06-20**	**Tue 23-06-20**
314	1.5.4.1.5.1	Installation of F/works & Rebars	2 days	Sun 21-06-20	Mon 22-06-20
315	1.5.4.1.5.2	Concreting Works	1 day	Tue 23-06-20	Tue 23-06-20
316	**1.5.4.2**	**Installation of Roofing System**	**5 days**	**Wed 24-06-20**	**Sun 28-06-20**
317	1.5.4.2.1	Installation of Roof Trusses, Rafters, Battens, Purlins and all necessary Structural Items	2 days	Wed 24-06-20	Thu 25-06-20
318	1.5.4.2.2	Intallation of Roof Covering; including Aluminium Foil Insulation, Chicken Wire Mesh, Fa	2 days	Fri 26-06-20	Sat 27-06-20

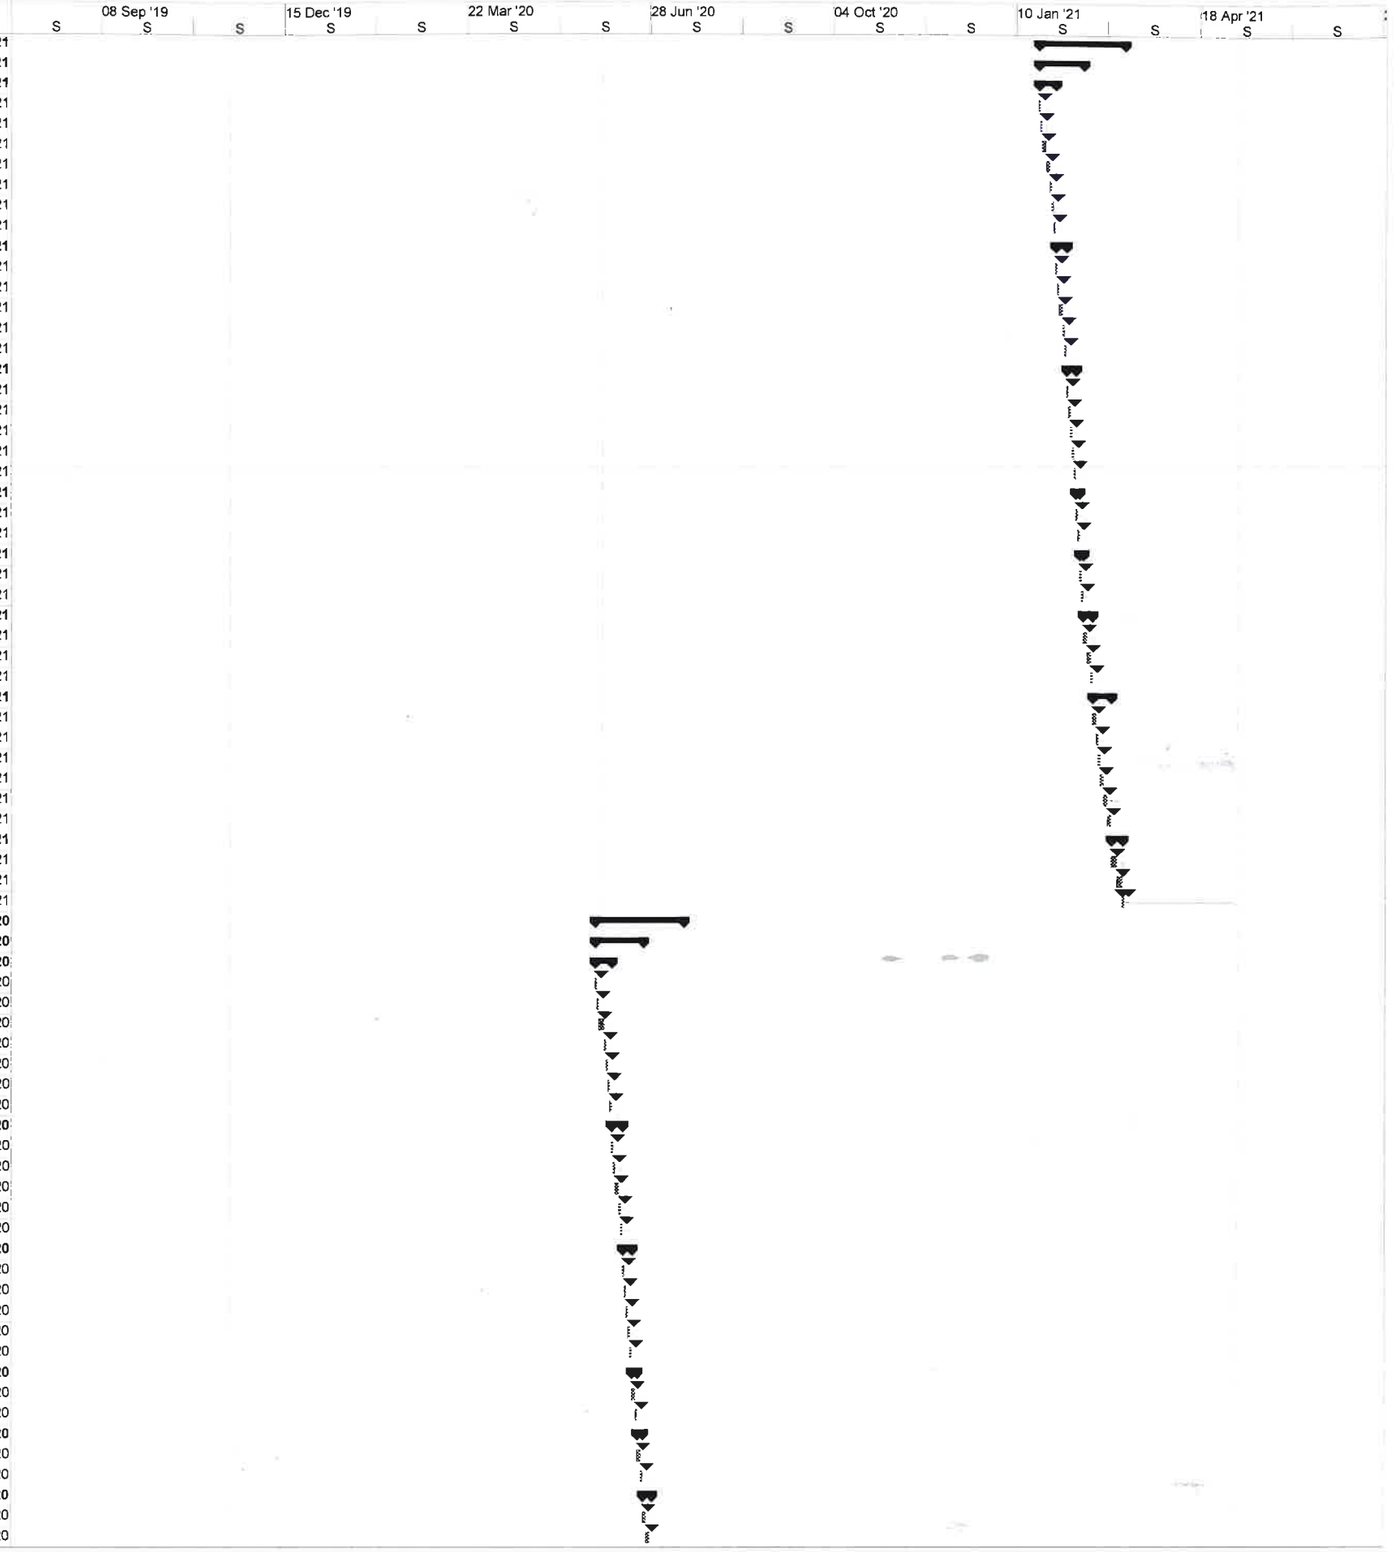

Project: CPM Slp Recovery Ver 8.0
Date: Tue 10-12-19

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Progress | Deadline


ID	WBS	Task Name	Duration	Start	Finish
319	1.5.4.2.3	Rainwater Downpipes (RWDP)	1 day	Sun 28-06-20	Sun 28-06-20
320	**1.5.4.3**	**Architectural Works**	**10 days**	**Mon 29-06-20**	**Wed 08-07-20**
321	1.5.4.3.1	Internal and External Brickwall (Bricklaying and Plastering Works)	2 days	Mon 29-06-20	Tue 30-06-20
322	1.5.4.3.2	Internal and External Floor Finishes.	1 day	Wed 01-07-20	Wed 01-07-20
323	1.5.4.3.3	Installation of Doors Windows and Ironmongeries	1 day	Thu 02-07-20	Thu 02-07-20
324	1.5.4.3.4	External and Internal Wall Finishes	2 days	Fri 03-07-20	Sat 04-07-20
325	1.5.4.3.5	Internal Ceiling Finishes	2 days	Sun 05-07-20	Mon 06-07-20
326	1.5.4.3.6	External Ceiling Finishes	2 days	Tue 07-07-20	Wed 08-07-20
327	**1.5.4.4**	**Electrical & Mechanical Services**	**6 days**	**Thu 09-07-20**	**Tue 14-07-20**
328	1.5.4.4.1	Electrical Services	3 days	Thu 09-07-20	Sat 11-07-20
329	1.5.4.4.2	Mechanical Services	3 days	Sun 12-07-20	Tue 14-07-20
330	1.5.4.5	Testing & Commisioning	1 day	Wed 15-07-20	Wed 15-07-20
331	**1.5.5**	**BANGUNAN PENCAWANG SESB**	**148 days**	**Thu 16-07-20**	**Thu 10-12-20**
332	**1.5.5.1**	**Structural**	**49 days**	**Thu 16-07-20**	**Wed 02-09-20**
333	**1.5.5.1.1**	**Pad Footings, Pile Caps and RC Stump**	**12 days**	**Thu 16-07-20**	**Mon 27-07-20**
334	1.5.5.1.1.1	Excavations	2 days	Thu 16-07-20	Fri 17-07-20
335	1.5.5.1.1.2	Lean Concrete	1 day	Sat 18-07-20	Sat 18-07-20
336	1.5.5.1.1.3	Installation of Formwork and Reinforcement Bar to Pad Footings/Pile Caps and Stum	5 days	Sun 19-07-20	Thu 23-07-20
337	1.5.5.1.1.4	Concreting Works of Pad Footings/Pile Caps	1 day	Fri 24-07-20	Fri 24-07-20
338	1.5.5.1.1.5	Installation of Stumps F/works & Rebars	1 day	Sat 25-07-20	Sat 25-07-20
339	1.5.5.1.1.6	Concreting Works for Stumps	1 day	Sun 26-07-20	Sun 26-07-20
340	1.5.5.1.1.7	Backfilling & Compaction	1 day	Mon 27-07-20	Mon 27-07-20
341	**1.5.5.1.2**	**Ground Beam Structures**	**12 days**	**Tue 28-07-20**	**Sat 08-08-20**
342	1.5.5.1.2.1	Anti Termite Treatment	1 day	Tue 28-07-20	Tue 28-07-20
343	1.5.5.1.2.2	Lean Concrete	1 day	Wed 29-07-20	Wed 29-07-20
344	1.5.5.1.2.3	Installation of F/works and Rebars for Ground Beam	7 days	Thu 30-07-20	Wed 05-08-20
345	1.5.5.1.2.4	Concreting Works for Ground Beams	2 days	Thu 06-08-20	Fri 07-08-20
346	1.5.5.1.2.5	Backfilling and Compaction	1 day	Sat 08-08-20	Sat 08-08-20
347	**1.5.5.1.3**	**Ground Slab**	**9 days**	**Sun 09-08-20**	**Mon 17-08-20**
348	1.5.5.1.3.1	Anti Termite Treatment	1 day	Sun 09-08-20	Sun 09-08-20
349	1.5.5.1.3.2	Installation of F/works	2 days	Mon 10-08-20	Tue 11-08-20
350	1.5.5.1.3.3	Damp Proof Membrane	1 day	Wed 12-08-20	Wed 12-08-20
351	1.5.5.1.3.4	Installation of Re-bars	3 days	Thu 13-08-20	Sat 15-08-20
352	1.5.5.1.3.5	Concreting of Ground Slab	2 days	Sun 16-08-20	Mon 17-08-20
353	**1.5.5.1.4**	**Ground Floor - Roof Beam Columns**	**7 days**	**Tue 18-08-20**	**Mon 24-08-20**
354	1.5.5.1.4.1	Installation of Formworks and Rebars	5 days	Tue 18-08-20	Sat 22-08-20
355	1.5.5.1.4.2	Concreting Works	2 days	Sun 23-08-20	Mon 24-08-20
356	**1.5.5.1.5**	**RC Roof Beams**	**9 days**	**Tue 25-08-20**	**Wed 02-09-20**
357	1.5.5.1.5.1	Installation of F/works & Rebars	7 days	Tue 25-08-20	Mon 31-08-20
358	1.5.5.1.5.2	Concreting Works	2 days	Tue 01-09-20	Wed 02-09-20
359	**1.5.5.2**	**Installation of Roofing System**	**14 days**	**Thu 03-09-20**	**Wed 16-09-20**
360	1.5.5.2.1	Installation of Roof Trusses, Rafters, Battens, Purlins and all necessary Structural Items	7 days	Thu 03-09-20	Wed 09-09-20
361	1.5.5.2.2	Intallation of Roof Covering; including Aluminium Foil Insulation, Chicken Wire Mesh, Fa	5 days	Thu 10-09-20	Mon 14-09-20
362	1.5.5.2.3	Rainwater Downpipes (RWDP)	2 days	Tue 15-09-20	Wed 16-09-20
363	**1.5.5.3**	**Architectural Works**	**37 days**	**Thu 17-09-20**	**Fri 23-10-20**
364	1.5.5.3.1	Internal and External Brickwall (Bricklaying and Plastering Works)	10 days	Thu 17-09-20	Sat 26-09-20
365	1.5.5.3.2	Internal and External Floor Finishes.	5 days	Sun 27-09-20	Thu 01-10-20
366	1.5.5.3.3	Installation of Doors Windows and Ironmongeries	4 days	Fri 02-10-20	Mon 05-10-20
367	1.5.5.3.4	External and Internal Wall Finishes	7 days	Tue 06-10-20	Mon 12-10-20
368	1.5.5.3.5	Internal Ceiling Finishes	7 days	Tue 13-10-20	Mon 19-10-20
369	1.5.5.3.6	External Ceiling Finishes	4 days	Tue 20-10-20	Fri 23-10-20
370	**1.5.5.4**	**Electrical & Mechanical Services**	**44 days**	**Sat 24-10-20**	**Sun 06-12-20**
371	1.5.5.4.1	Electrical Services	30 days	Sat 24-10-20	Sun 22-11-20
372	1.5.5.4.2	Mechanical Services	14 days	Mon 23-11-20	Sun 06-12-20
373	1.5.5.5	Testing & Commisioning	4 days	Mon 07-12-20	Thu 10-12-20
374	**1.5.6**	**TEMPAT LETAK KERETA BERBUMBUNG**	**35 days**	**Fri 11-12-20**	**Thu 14-01-21**
375	1.5.6.1	Structural Works	14 days	Fri 11-12-20	Thu 24-12-20
376	1.5.6.2	Architectural & Roofing Works	14 days	Fri 25-12-20	Thu 07-01-21
377	1.5.6.3	Electrical Works	7 days	Fri 08-01-21	Thu 14-01-21
378	**1.5.7**	**RUMAH PEMBUANGAN SAMPAH**	**35 days**	**Tue 09-03-21**	**Mon 12-04-21**
379	1.5.7.1	Structural Works	14 days	Tue 09-03-21	Mon 22-03-21
380	1.5.7.2	Architectural & Roofing Works	14 days	Tue 23-03-21	Mon 05-04-21
381	1.5.7.3	Electrical & Mechanical Works	7 days	Tue 06-04-21	Mon 12-04-21
382	**1.6**	**KERJA-KERJA DI SEKITAR BANGUNAN**	**151 days**	**Fri 11-12-20**	**Mon 10-05-21**
383	**1.6.1**	**Kerja-Kerja Jalan, Padang Kawad serta Kerja-Kerja Berkaitan**	**98 days**	**Fri 15-01-21**	**Thu 22-04-21**
384	**1.6.1.1**	**Jalanraya/ Road infrastructures**	**49 days**	**Fri 15-01-21**	**Thu 04-03-21**
385	1.6.1.1.1	Subgrade	14 days	Fri 15-01-21	Thu 28-01-21
386	1.6.1.1.2	Road Kerb	14 days	Fri 29-01-21	Thu 11-02-21
387	1.6.1.1.3	Road Base	14 days	Fri 12-02-21	Thu 25-02-21
388	1.6.1.1.4	Laying of Premix	7 days	Fri 26-02-21	Thu 04-03-21
389	**1.6.1.2**	**Marching Field/ Padang Kawad**	**49 days**	**Fri 05-03-21**	**Thu 22-04-21**
390	1.6.1.2.1	Subgrade	14 days	Fri 05-03-21	Thu 18-03-21
391	1.6.1.2.2	Road Kerb	14 days	Fri 19-03-21	Thu 01-04-21
392	1.6.1.2.3	Road Base	14 days	Fri 02-04-21	Thu 15-04-21

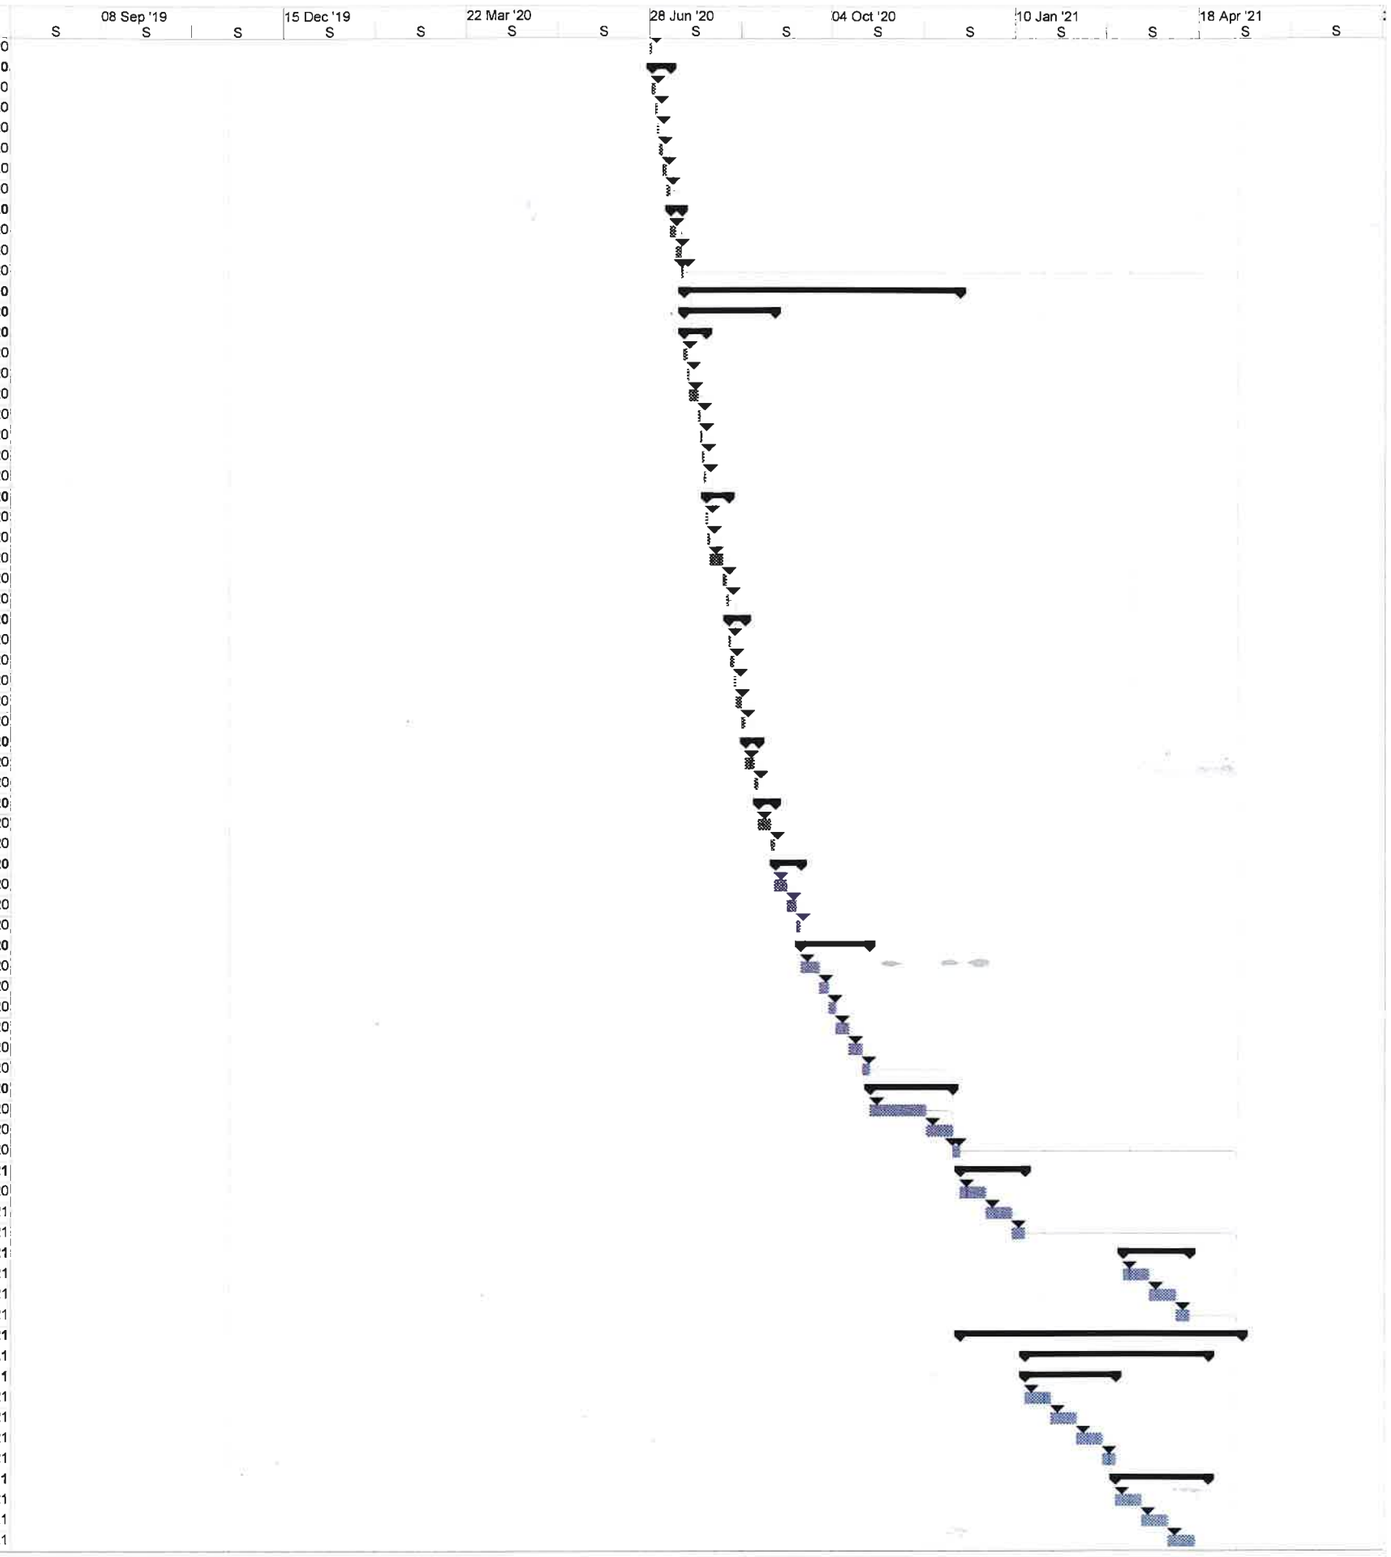

Project: CPM Slp Recovery Ver. 8.0
Date: Tue 10-12-19

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Progress | Deadline

ID	WBS	Task Name	Duration	Start	Finish
393	1.6.1.2.4	Laying of Premix	7 days	Fri 16-04-21	Thu 22-04-21
394	**1.6.2**	**Sistem Saliran Permukaan**	**63 days**	**Tue 09-03-21**	**Mon 10-05-21**
395	1.6.2.1	Surface Drainage System	60 days	Tue 09-03-21	Fri 07-05-21
396	1.6.2.2	Testing & Commisioning	3 days	Sat 08-05-21	Mon 10-05-21
397	**1.6.3**	**Sistem Retikulasi Air**	**63 days**	**Tue 09-03-21**	**Mon 10-05-21**
398	1.6.3.1	Water Reticulation System	60 days	Tue 09-03-21	Fri 07-05-21
399	1.6.3.2	Tseting Commisioning	3 days	Sat 08-05-21	Mon 10-05-21
400	**1.6.4**	**Sistem Kumbahan**	**123 days**	**Fri 11-12-20**	**Mon 12-04-21**
401	1.6.4.1	Sewerage Manholes	60 days	Fri 11-12-20	Mon 08-02-21
402	1.6.4.2	Sewerage Piping System	60 days	Tue 09-02-21	Fri 09-04-21
403	1.6.4.3	Testing & Commisioning	3 days	Sat 10-04-21	Mon 12-04-21
404	**1.6.5**	**Flag Pole**	**14 days**	**Fri 23-04-21**	**Thu 06-05-21**
405	1.6.5.1	Flag Pole	14 days	Fri 23-04-21	Thu 06-05-21
406	**1.6.6**	**Fencing**	**54 days**	**Fri 26-02-21**	**Tue 20-04-21**
407	1.6.6.1	Fencing	30 days	Fri 26-02-21	Sat 27-03-21
408	1.6.6.2	Decorative Fencing	14 days	Sun 28-03-21	Sat 10-04-21
409	1.6.6.3	Gate	10 days	Sun 11-04-21	Tue 20-04-21
410	**1.6.7**	**Kerja-Kerja Penanaman Rumput**	**20 days**	**Sun 11-04-21**	**Fri 30-04-21**
411	1.6.7.1	Turfing Works	20 days	Sun 11-04-21	Fri 30-04-21
412	**1.6.8**	**Pembinaan Kolah Air**	**14 days**	**Fri 16-04-21**	**Thu 29-04-21**
413	1.6.8.1	Kolah Air	14 days	Fri 16-04-21	Thu 29-04-21
414	**1.7**	**WANG PERUNTUKAN SEMENTARA**	**546 days**	**Tue 12-11-19**	**Mon 10-05-21**
415	1.7.1	Contribution to Local Authority	546 days	Tue 12-11-19	Mon 10-05-21
416	1.7.2	Contribution for Loose Furnitures	109 days	Fri 22-01-21	Mon 10-05-21
417	1.7.3	Contribution for Landscape	109 days	Fri 22-01-21	Mon 10-05-21
418	1.7.4	Contribution for Signages	109 days	Fri 22-01-21	Mon 10-05-21
419	1.7.5	Contribution for OFF Site Works	109 days	Fri 22-01-21	Mon 10-05-21
420	1.8	PROJECT FINISH	0 days	Mon 10-05-21	Mon 10-05-21

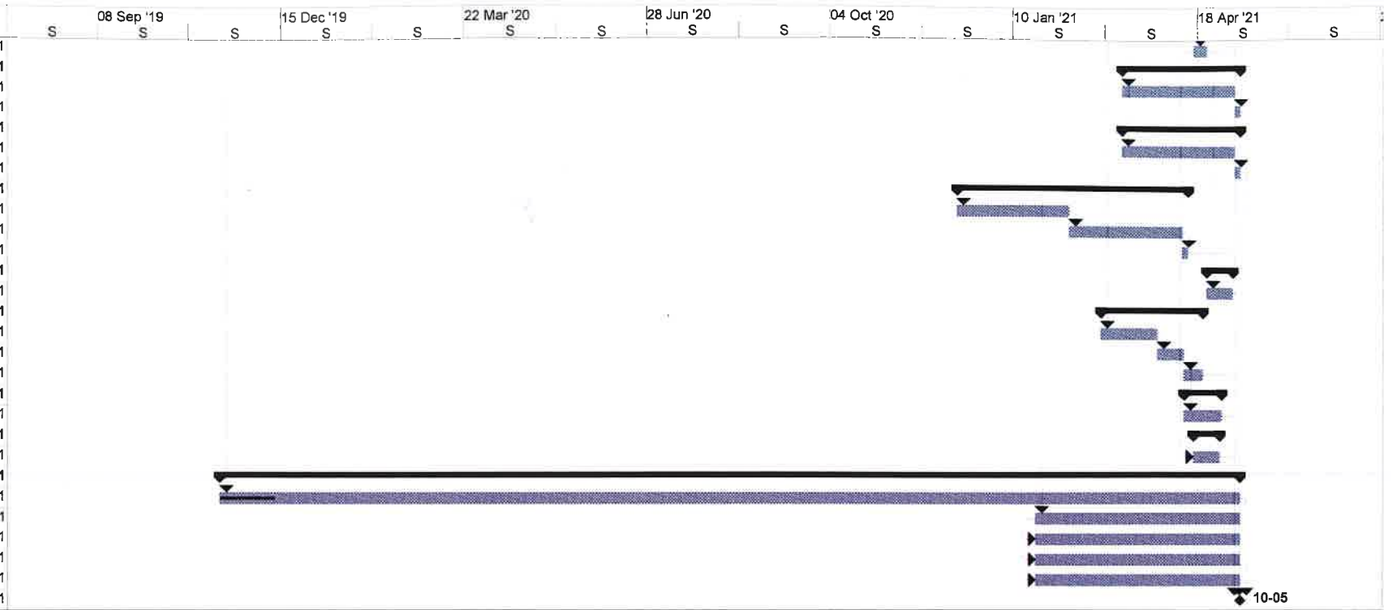

Project: CPM Slp Recovery Ver. 8.0
Date: Tue 10-12-19

Task	Summary	External Milestone	Inactive Milestone	Duration-only	Start-only	External Milestone
Split	Project Summary	Inactive Task	Inactive Summary	Manual Summary Rollup	Finish-only	Progress
Milestone	External Tasks	Inactive Milestone	Manual Task	Manual Summary	External Tasks	Deadline
