

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
1		**CADANGAN PEMBINAAN PROJEK BALAI BOMBA DAN PENYELAMAT BEAUFORT, SABAH**	**390 days**	**Tue 12-11-19**	**Wed 01-09-21**	**Tue 12-11-19**	**Wed 01-09-21**	**$6,305,978.26**
2		PROJECT START	0 days	Tue 12-11-19	Tue 12-11-19	Tue 12-11-19	Tue 12-11-19	$0.00
3		**PRELIMINARIES**	**308 days**	**Tue 12-11-19**	**Mon 10-05-21**	**Tue 12-11-19**	**Mon 10-05-21**	**$303,180.00**
4		**Provisions In Condition of Contract PWD Form 203 (Rev.1/2010)**	**308 days**	**Tue 12-11-19**	**Mon 10-05-21**	**Tue 12-11-19**	**Mon 10-05-21**	**$303,180.00**
317		**SITE PREPARATION, EARTHWORKS AND ASSOCIATED WORKS**	**309 days**	**Wed 11-12-19**	**Wed 09-06-21**	**Wed 11-12-19**	**Wed 09-06-21**	**$1,817,866.00**
318		Site Clearing	25 days	Wed 11-12-19	Tue 14-01-20	Wed 11-12-19	Tue 14-01-20	$35,812.00
319		Temporary Access Complete with Washbay	7 days	Wed 15-01-20	Thu 23-01-20	Wed 15-01-20	Thu 23-01-20	$14,500.00
320		Earthwork: Cut and Fill to Formation Level	30 days	Fri 24-01-20	Thu 05-03-20	Fri 24-01-20	Thu 05-03-20	$69,750.00
321		Temporary Earth Drain	14 days	Fri 06-03-20	Fri 17-07-20	Fri 06-03-20	Fri 17-07-20	$19,475.00
322		**Geotechnical Work**	**57 days**	**Fri 06-03-20**	**Wed 16-09-20**	**Fri 06-03-20**	**Wed 16-09-20**	**$318,461.00**
323		**PVD & Drainage Blanket**	**26 days**	**Fri 06-03-20**	**Tue 04-08-20**	**Fri 06-03-20**	**Tue 04-08-20**	**$171,061.00**
324		Plant & Equipment	3 days	Fri 06-03-20	Tue 10-03-20	Fri 06-03-20	Tue 10-03-20	$15,000.00
325		Setting out for Prefabricated Vertical Drain	2 days	Wed 11-03-20	Thu 12-03-20	Wed 11-03-20	Thu 12-03-20	$6,241.00
326		Supply and Install Pre-Fabricated Vertical Drain	14 days	Fri 13-03-20	Fri 24-07-20	Fri 13-03-20	Fri 24-07-20	$99,840.00
327		Construction of 500mm Drainage Blanket	7 days	Mon 27-07-20	Tue 04-08-20	Mon 27-07-20	Tue 04-08-20	$49,980.00
328		**Surcharging**	**31 days**	**Wed 05-08-20**	**Wed 16-09-20**	**Wed 05-08-20**	**Wed 16-09-20**	**$147,400.00**
329		Supply , lay, spread and compact of suitable materials as surcharge fill	3 days	Wed 05-08-20	Fri 07-08-20	Wed 05-08-20	Fri 07-08-20	$35,250.00
330		Excavate and remove surcharge materials as directed	14 days	Mon 10-08-20	Thu 27-08-20	Mon 10-08-20	Thu 27-08-20	$21,150.00
331		Supply and lay approved geotextile between drainage blanket and suitable fill	7 days	Fri 28-08-20	Mon 07-09-20	Fri 28-08-20	Mon 07-09-20	$42,000.00
332		Supply and lay approved geotextile between drainage blanket and surcharge fill	7 days	Tue 08-09-20	Wed 16-09-20	Tue 08-09-20	Wed 16-09-20	$49,000.00
333		**Marching Field & Roadworks**	**190 days**	**Thu 17-09-20**	**Wed 09-06-21**	**Thu 17-09-20**	**Wed 09-06-21**	**$617,514.00**
334		Preparation of Subgrade Layer	39 days	Thu 17-09-20	Tue 10-11-20	Thu 17-09-20	Tue 10-11-20	$30,064.00
335		Contruction/Laying of Road Base	40 days	Wed 11-11-20	Tue 05-01-21	Wed 11-11-20	Tue 05-01-21	$222,040.00
336		Installation of Road Kerb	30 days	Wed 06-01-21	Tue 16-02-21	Wed 06-01-21	Tue 16-02-21	$24,270.00
337		Testing; FDT, CBR, MDT	7 days	Wed 17-02-21	Thu 25-02-21	Wed 17-02-21	Thu 25-02-21	$2,500.00
338		Asphalt Finishes Layer	30 days	Fri 26-02-21	Thu 08-04-21	Fri 26-02-21	Thu 08-04-21	$307,440.00
339		Road Marking	30 days	Fri 09-04-21	Thu 20-05-21	Fri 09-04-21	Thu 20-05-21	$29,400.00
340		Road Signboard	14 days	Fri 21-05-21	Wed 09-06-21	Fri 21-05-21	Wed 09-06-21	$1,800.00
341		**Sistem Saliran Permukaan**	**160 days**	**Thu 17-09-20**	**Wed 28-04-21**	**Thu 17-09-20**	**Wed 28-04-21**	**$330,280.00**
342		Reinforced Concrete Drain	60 days	Thu 17-09-20	Wed 09-12-20	Thu 17-09-20	Wed 09-12-20	$198,620.00
343		Culvert Construction	30 days	Thu 10-12-20	Wed 20-01-21	Thu 10-12-20	Wed 20-01-21	$95,000.00
344		Sump	30 days	Thu 21-01-21	Wed 03-03-21	Thu 21-01-21	Wed 03-03-21	$16,500.00
345		MS Grating for Sump and Grating	20 days	Thu 04-03-21	Wed 31-03-21	Thu 04-03-21	Wed 31-03-21	$16,660.00
346		Work to Existing Drain	20 days	Thu 01-04-21	Wed 28-04-21	Thu 01-04-21	Wed 28-04-21	$3,500.00
347		**Sistem Retikulasi Air**	**116 days**	**Thu 10-12-20**	**Thu 20-05-21**	**Thu 10-12-20**	**Thu 20-05-21**	**$75,177.00**
348		Excavation and Laying of 150mm MSSL Pipes including bedding and surrounding	39 days	Thu 10-12-20	Tue 02-02-21	Thu 10-12-20	Tue 02-02-21	$30,488.00
349		Pillar Hydrant & Bulk Meter	20 days	Wed 03-02-21	Tue 02-03-21	Wed 03-02-21	Tue 02-03-21	$7,500.00
350		Valve Chambers including Accessories and Equipment	20 days	Wed 03-03-21	Tue 30-03-21	Wed 03-03-21	Tue 30-03-21	$3,750.00
351		Balancing Tank	30 days	Wed 31-03-21	Tue 11-05-21	Wed 31-03-21	Tue 11-05-21	$22,500.00
352		Tightness Test, Flushing and Dissenfecting Test	7 days	Wed 12-05-21	Thu 20-05-21	Wed 12-05-21	Thu 20-05-21	$10,939.00

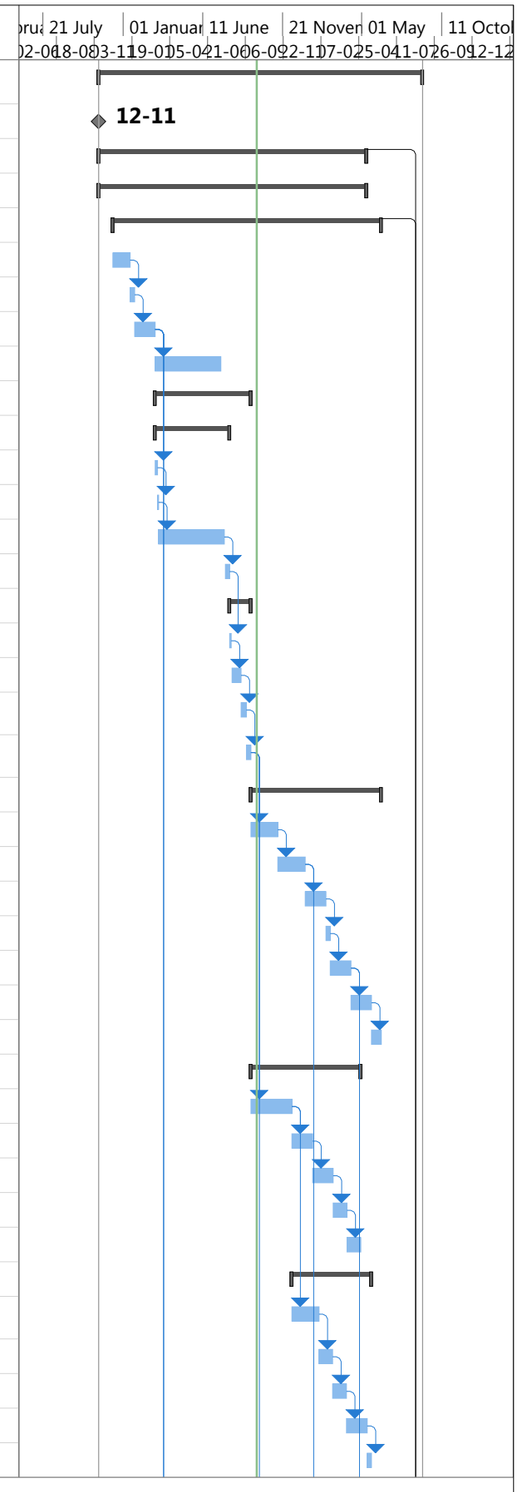

Project: Project1
Date: Tue 29-09-20

Task	Project Summary	Manual Task	Start-only	Deadline	
Split	Inactive Task	Duration-only	Finish-only	Progress	
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress	
Summary	Inactive Summary	Manual Summary	External Milestone		


ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
353		**Sistem Saliran Kumbahan**	**137 days**	**Thu 17-09-20**	**Fri 26-03-21**	**Thu 17-09-20**	**Fri 26-03-21**	**$50,760.00**
354		Excavation of Pipe Trenches, Laying of Bedding and Laying of 150mm UPVC Pipe, jointingand other accessories.	60 days	Thu 17-09-20	Wed 09-12-20	Thu 17-09-20	Wed 09-12-20	$13,160.00
355		Construction of Manholes	40 days	Thu 10-12-20	Wed 03-02-21	Thu 10-12-20	Wed 03-02-21	$7,600.00
356		Construction of Septic Tank	30 days	Thu 04-02-21	Wed 17-03-21	Thu 04-02-21	Wed 17-03-21	$25,000.00
357		Testing	7 days	Thu 18-03-21	Fri 26-03-21	Thu 18-03-21	Fri 26-03-21	$5,000.00
358		**Fencing, Decorative Fencing and Gates**	**107 days**	**Wed 06-01-21**	**Thu 03-06-21**	**Wed 06-01-21**	**Thu 03-06-21**	**$286,137.00**
359		Construction of Sliding and Double Swing Gate including RC Colums	13 days	Wed 06-01-21	Fri 22-01-21	Wed 06-01-21	Fri 22-01-21	$30,500.00
360		Boundary Fencing	60 days	Mon 25-01-21	Fri 16-04-21	Mon 25-01-21	Fri 16-04-21	$158,406.00
361		**Flag Pole**	**14 days**	**Mon 19-04-21**	**Thu 06-05-21**	**Mon 19-04-21**	**Thu 06-05-21**	**$18,600.00**
362		Flag Pole	14 days	Mon 19-04-21	Thu 06-05-21	Mon 19-04-21	Thu 06-05-21	$18,600.00
363		**Kolah Air**	**14 days**	**Fri 07-05-21**	**Wed 26-05-21**	**Fri 07-05-21**	**Wed 26-05-21**	**$17,607.00**
364		Kolah Air	14 days	Fri 07-05-21	Wed 26-05-21	Fri 07-05-21	Wed 26-05-21	$17,607.00
365		**Turfing**	**40 days**	**Fri 09-04-21**	**Thu 03-06-21**	**Fri 09-04-21**	**Thu 03-06-21**	**$61,024.00**
366		Turfing Work	40 days	Fri 09-04-21	Thu 03-06-21	Fri 09-04-21	Thu 03-06-21	$61,024.00
367		**PILING WORKS**	**113 days**	**Fri 20-12-19**	**Thu 17-09-20**	**Fri 20-12-19**	**Thu 17-09-20**	**$141,905.91**
368		Submission of Pile Catalogue, Plant, Equipment and Pile Set Criteria	1 day	Fri 20-12-19	Fri 20-12-19	Fri 20-12-19	Fri 20-12-19	$0.00
369		Mobilization of Plant & Equipment	3 days	Fri 06-03-20	Tue 10-03-20	Fri 06-03-20	Tue 10-03-20	$23,250.00
370		Initial Pile Driving for MLT	1 day	Wed 11-03-20	Wed 11-03-20	Wed 11-03-20	Wed 11-03-20	$0.00
371		MLT Pile Testing (1 Nos)	7 days	Thu 12-03-20	Tue 14-07-20	Thu 12-03-20	Tue 14-07-20	$18,600.00
372		Submission of Pile Testing Report	2 days	Wed 15-07-20	Thu 16-07-20	Wed 15-07-20	Thu 16-07-20	$0.00
373		**Supply and Delivery of Piles**	**8 days**	**Fri 17-07-20**	**Tue 28-07-20**	**Fri 17-07-20**	**Tue 28-07-20**	**$62,058.90**
374		Menara Latihan	2 days	Fri 17-07-20	Mon 20-07-20	Fri 17-07-20	Mon 20-07-20	$19,065.00
375		Entrance Signage	2 days	Tue 21-07-20	Wed 22-07-20	Tue 21-07-20	Wed 22-07-20	$4,361.70
376		Entrance Culvert	2 days	Thu 23-07-20	Fri 24-07-20	Thu 23-07-20	Fri 24-07-20	$18,693.00
377		Drainage	2 days	Mon 27-07-20	Tue 28-07-20	Mon 27-07-20	Tue 28-07-20	$19,939.20
378		**Pile Driving & Jointing**	**37 days**	**Wed 29-07-20**	**Thu 17-09-20**	**Wed 29-07-20**	**Thu 17-09-20**	**$37,997.01**
379		**Menara Latihan (50 Pile Points)**	**12 days**	**Wed 29-07-20**	**Thu 13-08-20**	**Wed 29-07-20**	**Thu 13-08-20**	**$8,742.00**
380		Pile Points Setting Out	1 day	Wed 29-07-20	Wed 29-07-20	Wed 29-07-20	Wed 29-07-20	$0.00
381		Pile Driving& Jointing	5 days	Thu 30-07-20	Wed 05-08-20	Thu 30-07-20	Wed 05-08-20	$7,347.00
382		Excavation of Pile caps	3 days	Thu 06-08-20	Mon 10-08-20	Thu 06-08-20	Mon 10-08-20	$0.00
383		Cut off Pile Head	3 days	Tue 11-08-20	Thu 13-08-20	Tue 11-08-20	Thu 13-08-20	$1,395.00
384		**Entrance Signage (7 Pile Points)**	**12 days**	**Thu 30-07-20**	**Fri 14-08-20**	**Thu 30-07-20**	**Fri 14-08-20**	**$1,647.03**
385		Pile Points Setting Out	1 day	Thu 30-07-20	Thu 30-07-20	Thu 30-07-20	Thu 30-07-20	$0.00
386		Pile Driving& Jointing	3 days	Thu 06-08-20	Mon 10-08-20	Thu 06-08-20	Mon 10-08-20	$1,451.73
387		Excavation of Pile caps	2 days	Tue 11-08-20	Wed 12-08-20	Tue 11-08-20	Wed 12-08-20	$0.00
388		Cut off Pile Head	2 days	Thu 13-08-20	Fri 14-08-20	Thu 13-08-20	Fri 14-08-20	$195.30
389		**Entrance Culvert (30 Pile Points)**	**22 days**	**Fri 31-07-20**	**Mon 31-08-20**	**Fri 31-07-20**	**Mon 31-08-20**	**$7,058.70**
390		Pile Points Setting Out	1 day	Fri 31-07-20	Fri 31-07-20	Fri 31-07-20	Fri 31-07-20	$0.00
391		Pile Driving& Jointing	6 days	Tue 11-08-20	Tue 18-08-20	Tue 11-08-20	Tue 18-08-20	$6,221.70
392		Excavation of Pile caps	4 days	Wed 19-08-20	Mon 24-08-20	Wed 19-08-20	Mon 24-08-20	$0.00
393		Cut off Pile Head	5 days	Tue 25-08-20	Mon 31-08-20	Tue 25-08-20	Mon 31-08-20	$837.00

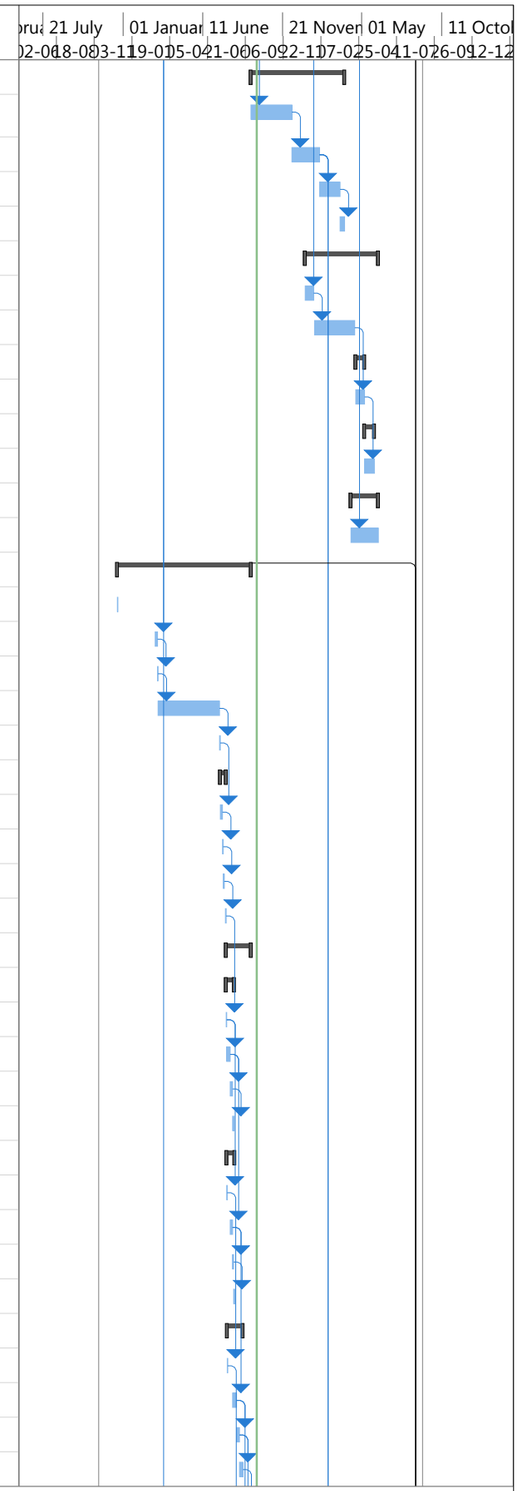

Project: Project1
Date: Tue 29-09-20

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress


ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
394		**Drainage (32 Pile Points)**	**26 days**	**Mon 03-08-20**	**Mon 07-09-20**	**Mon 03-08-20**	**Mon 07-09-20**	**$7,529.28**
395		Pile Points Setting Out	1 day	Mon 03-08-20	Mon 03-08-20	Mon 03-08-20	Mon 03-08-20	$0.00
396		Pile Driving& Jointing	6 days	Wed 19-08-20	Wed 26-08-20	Wed 19-08-20	Wed 26-08-20	$6,636.48
397		Excavation of Pile caps	4 days	Tue 25-08-20	Fri 28-08-20	Tue 25-08-20	Fri 28-08-20	$0.00
398		Cut off Pile Head	5 days	Tue 01-09-20	Mon 07-09-20	Tue 01-09-20	Mon 07-09-20	$892.80
399		**Piling As Built Drawings**	**8 days**	**Tue 08-09-20**	**Thu 17-09-20**	**Tue 08-09-20**	**Thu 17-09-20**	**$13,020.00**
400		PDA Test (1 No)	1 day	Tue 08-09-20	Tue 08-09-20	Tue 08-09-20	Tue 08-09-20	$1,860.00
401		Preparation and Endorsement of Piling As Built Survey	7 days	Tue 08-09-20	Wed 16-09-20	Tue 08-09-20	Wed 16-09-20	$0.00
402		Submission of Piling Record	3 days	Tue 08-09-20	Thu 10-09-20	Tue 08-09-20	Thu 10-09-20	$1,860.00
403		Submission of piling As Built Survey	1 day	Thu 17-09-20	Thu 17-09-20	Thu 17-09-20	Thu 17-09-20	$9,300.00
404		**BUILDING WORKS**	**307 days**	**Fri 06-03-20**	**Wed 01-09-21**	**Fri 06-03-20**	**Wed 01-09-21**	**$2,045,721.35**
405		**BANGUNAN BALAI BOMBA**	**297 days**	**Fri 06-03-20**	**Wed 18-08-21**	**Fri 06-03-20**	**Wed 18-08-21**	**$1,488,465.70**
406		**Structural Works**	**193 days**	**Fri 06-03-20**	**Thu 25-03-21**	**Fri 06-03-20**	**Thu 25-03-21**	**$718,874.90**
407		**Pad Footings and RC Stump**	**61 days**	**Fri 06-03-20**	**Tue 22-09-20**	**Fri 06-03-20**	**Tue 22-09-20**	**$198,081.60**
408		Building Setting out& Survey	3 days	Fri 06-03-20	Tue 10-03-20	Fri 06-03-20	Tue 10-03-20	$0.00
409		Excavation of Pad Footings	7 days	Wed 11-03-20	Mon 13-07-20	Wed 11-03-20	Mon 13-07-20	$8,076.00
410		Lean Concrete	4 days	Tue 14-07-20	Fri 17-07-20	Tue 14-07-20	Fri 17-07-20	$2,202.00
411		Installation of Formwork to Pad Footings	14 days	Mon 20-07-20	Thu 06-08-20	Mon 20-07-20	Thu 06-08-20	$15,750.00
412		Installation of Reinforcement Bars to Pad Footings & Stumps	10 days	Fri 07-08-20	Thu 20-08-20	Fri 07-08-20	Thu 20-08-20	$54,393.60
413		Concreting Works of Pad Footings	7 days	Fri 21-08-20	Mon 31-08-20	Fri 21-08-20	Mon 31-08-20	$110,334.00
414		Installation of Stumps F/works	5 days	Tue 01-09-20	Mon 07-09-20	Tue 01-09-20	Mon 07-09-20	$3,700.00
415		Concreting Works for Stumps	4 days	Tue 08-09-20	Fri 11-09-20	Tue 08-09-20	Fri 11-09-20	$3,626.00
416		Backfilling& Compaction	7 days	Mon 14-09-20	Tue 22-09-20	Mon 14-09-20	Tue 22-09-20	$0.00
417		**Ground Beam Structures**	**47 days**	**Wed 23-09-20**	**Thu 26-11-20**	**Wed 23-09-20**	**Thu 26-11-20**	**$99,444.00**
418		Excavation of Ground Beam	4 days	Wed 23-09-20	Mon 28-09-20	Wed 23-09-20	Mon 28-09-20	$696.00
419		Lean Concrete	7 days	Tue 29-09-20	Wed 07-10-20	Tue 29-09-20	Wed 07-10-20	$672.00
420		Installation of Ground Beam F/works	14 days	Thu 08-10-20	Tue 27-10-20	Thu 08-10-20	Tue 27-10-20	$20,950.00
421		Installation of Ground Beam Rebars	10 days	Wed 28-10-20	Tue 10-11-20	Wed 28-10-20	Tue 10-11-20	$51,744.00
422		Concreting Works for Ground Beams	7 days	Wed 11-11-20	Thu 19-11-20	Wed 11-11-20	Thu 19-11-20	$25,382.00
423		Backfilling and Compaction	5 days	Fri 20-11-20	Thu 26-11-20	Fri 20-11-20	Thu 26-11-20	$0.00
424		**Ground Slab**	**18 days**	**Fri 27-11-20**	**Tue 22-12-20**	**Fri 27-11-20**	**Tue 22-12-20**	**$82,635.70**
425		Excavation of Ground Slab	2 days	Fri 27-11-20	Mon 30-11-20	Fri 27-11-20	Mon 30-11-20	$864.00
426		Anti Termite Treatment	2 days	Tue 01-12-20	Wed 02-12-20	Tue 01-12-20	Wed 02-12-20	$2,980.00
427		Installation of F/works	3 days	Thu 03-12-20	Mon 07-12-20	Thu 03-12-20	Mon 07-12-20	$1,552.00
428		Damp Proof Membrane	2 days	Tue 08-12-20	Wed 09-12-20	Tue 08-12-20	Wed 09-12-20	$3,105.00
429		Lean Concrete	1 day	Thu 10-12-20	Thu 10-12-20	Thu 10-12-20	Thu 10-12-20	$2,454.70
430		Installation of Re-bars	5 days	Fri 11-12-20	Thu 17-12-20	Fri 11-12-20	Thu 17-12-20	$29,204.00
431		Concreting of Ground Slab	3 days	Fri 18-12-20	Tue 22-12-20	Fri 18-12-20	Tue 22-12-20	$42,476.00
432		**Apron Slab**	**13 days**	**Wed 23-12-20**	**Fri 08-01-21**	**Wed 23-12-20**	**Fri 08-01-21**	**$6,791.00**
433		Excavation for Apron Slab	3 days	Wed 23-12-20	Fri 25-12-20	Wed 23-12-20	Fri 25-12-20	$104.00
434		Installation of F/works	3 days	Mon 28-12-20	Wed 30-12-20	Mon 28-12-20	Wed 30-12-20	$0.00

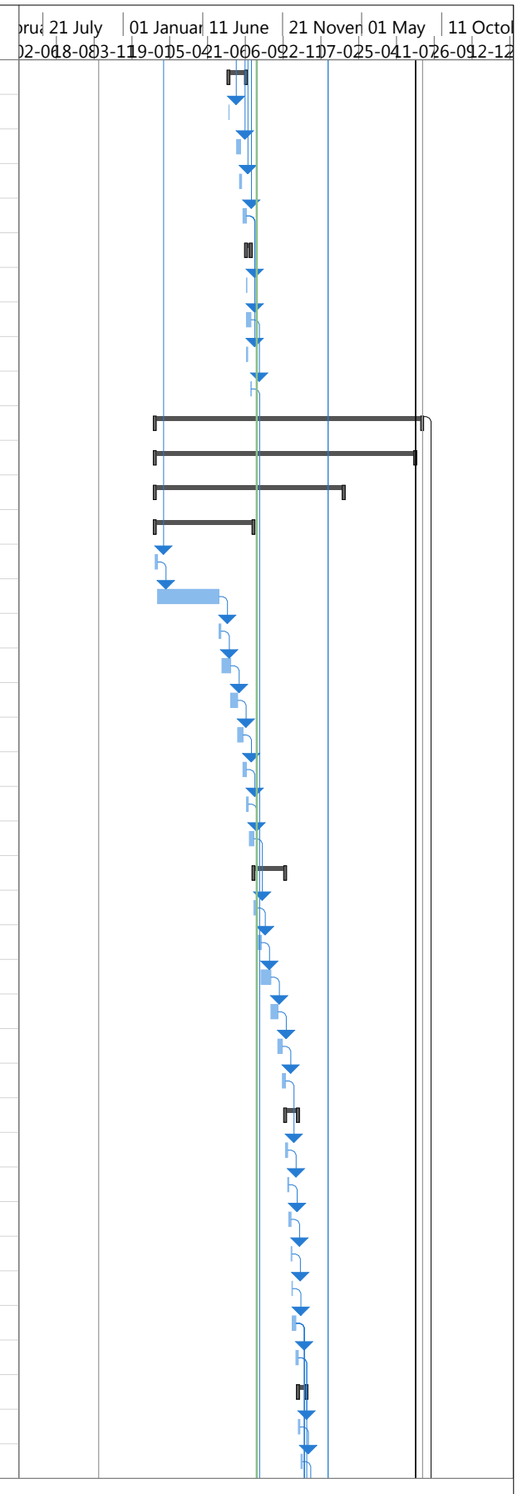

Project: Project1
Date: Tue 29-09-20

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone


ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
435		Lean Concrete	2 days	Thu 31-12-20	Fri 01-01-21	Thu 31-12-20	Fri 01-01-21	$450.00
436		Installation of Re-bars	3 days	Mon 04-01-21	Wed 06-01-21	Mon 04-01-21	Wed 06-01-21	$1,575.00
437		Concreting of Apron Slab	2 days	Thu 07-01-21	Fri 08-01-21	Thu 07-01-21	Fri 08-01-21	$4,662.00
438		**Ramp Slab**	**6 days**	**Mon 11-01-21**	**Mon 18-01-21**	**Mon 11-01-21**	**Mon 18-01-21**	**$3,968.00**
439		Installation of F/works	3 days	Mon 11-01-21	Wed 13-01-21	Mon 11-01-21	Wed 13-01-21	$50.00
440		Installation of Re-bars	2 days	Thu 14-01-21	Fri 15-01-21	Thu 14-01-21	Fri 15-01-21	$546.00
441		Concreting of Ramp Slab	1 day	Mon 18-01-21	Mon 18-01-21	Mon 18-01-21	Mon 18-01-21	$3,372.00
442		**Ground Floor - 1st Floor Columns**	**13 days**	**Wed 23-12-20**	**Fri 08-01-21**	**Wed 23-12-20**	**Fri 08-01-21**	**$53,756.20**
443		Installation of Formworks	5 days	Wed 23-12-20	Tue 29-12-20	Wed 23-12-20	Tue 29-12-20	$14,850.00
444		Installation of Reinforcement Bars	5 days	Wed 30-12-20	Tue 05-01-21	Wed 30-12-20	Tue 05-01-21	$23,107.20
445		Concreting Works	3 days	Wed 06-01-21	Fri 08-01-21	Wed 06-01-21	Fri 08-01-21	$15,799.00
446		**1st Floor Beam & Slab**	**22 days**	**Mon 11-01-21**	**Tue 09-02-21**	**Mon 11-01-21**	**Tue 09-02-21**	**$84,145.00**
447		Installation of F/works for Beam & Slab	10 days	Mon 11-01-21	Fri 22-01-21	Mon 11-01-21	Fri 22-01-21	$17,708.00
448		Installation of Rebars for Beam & Slab	7 days	Mon 25-01-21	Tue 02-02-21	Mon 25-01-21	Tue 02-02-21	$18,781.00
449		Concreting Works for Beam & Slab	5 days	Wed 03-02-21	Tue 09-02-21	Wed 03-02-21	Tue 09-02-21	$47,656.00
450		**RC Staircase**	**32 days**	**Wed 10-02-21**	**Thu 25-03-21**	**Wed 10-02-21**	**Thu 25-03-21**	**$21,551.60**
451		Installation of F/works	5 days	Wed 10-02-21	Tue 16-02-21	Wed 10-02-21	Tue 16-02-21	$3,063.00
452		Instalation of Rebars	5 days	Wed 17-02-21	Tue 23-02-21	Wed 17-02-21	Tue 23-02-21	$3,302.40
453		Concreting Works	2 days	Wed 24-02-21	Thu 25-02-21	Wed 24-02-21	Thu 25-02-21	$4,092.20
454		Staircase Finishing Work including Railling work	20 days	Fri 26-02-21	Thu 25-03-21	Fri 26-02-21	Thu 25-03-21	$11,094.00
455		**1st Floor to Roof Beam Columns**	**13 days**	**Wed 10-02-21**	**Fri 26-02-21**	**Wed 10-02-21**	**Fri 26-02-21**	**$53,756.20**
456		Installation of Formworks	5 days	Wed 10-02-21	Tue 16-02-21	Wed 10-02-21	Tue 16-02-21	$14,850.00
457		Installation of Rebars	5 days	Wed 17-02-21	Tue 23-02-21	Wed 17-02-21	Tue 23-02-21	$23,107.20
458		Concreting Works	3 days	Wed 24-02-21	Fri 26-02-21	Wed 24-02-21	Fri 26-02-21	$15,799.00
459		**RC Roof Beams, RC Flat Roof and Hoods**	**18 days**	**Mon 01-03-21**	**Wed 24-03-21**	**Mon 01-03-21**	**Wed 24-03-21**	**$114,745.60**
460		Installation of F/works	7 days	Mon 01-03-21	Tue 09-03-21	Mon 01-03-21	Tue 09-03-21	$31,700.00
461		Installation of Rebars	7 days	Wed 10-03-21	Thu 18-03-21	Wed 10-03-21	Thu 18-03-21	$40,569.60
462		Concreting Works	4 days	Fri 19-03-21	Wed 24-03-21	Fri 19-03-21	Wed 24-03-21	$42,476.00
463		**Installation of Roofing System**	**27 days**	**Thu 25-03-21**	**Fri 30-04-21**	**Thu 25-03-21**	**Fri 30-04-21**	**$153,530.00**
464		Installation of Roof Trusses, Rafters, Battens, Purlins and all necessary Structural Items	10 days	Thu 25-03-21	Wed 07-04-21	Thu 25-03-21	Wed 07-04-21	$63,200.00
465		Intallation of Roof Covering; including Aluminium Foil Insulation, Chicken Wire Mesh, Facia Board, Gutter and other necessary finishes.	10 days	Thu 08-04-21	Wed 21-04-21	Thu 08-04-21	Wed 21-04-21	$85,370.00
466		Rainwater Downpipes (RWDP)	7 days	Thu 22-04-21	Fri 30-04-21	Thu 22-04-21	Fri 30-04-21	$4,960.00
467		**Architectural Works**	**105 days**	**Thu 25-03-21**	**Wed 18-08-21**	**Thu 25-03-21**	**Wed 18-08-21**	**$616,060.80**
468		**External Wall**	**22 days**	**Thu 25-03-21**	**Fri 23-04-21**	**Thu 25-03-21**	**Fri 23-04-21**	**$57,569.20**
469		Stiffeners	7 days	Thu 25-03-21	Fri 02-04-21	Thu 25-03-21	Fri 02-04-21	$7,179.20
470		External Wall (1 Brick, Half Brick Including Parapet Wall including all sundries)	15 days	Mon 05-04-21	Fri 23-04-21	Mon 05-04-21	Fri 23-04-21	$50,390.00
471		**External Doors & Windows**	**31 days**	**Mon 26-04-21**	**Mon 07-06-21**	**Mon 26-04-21**	**Mon 07-06-21**	**$60,716.00**
472		**External Doors**	**28 days**	**Mon 26-04-21**	**Wed 02-06-21**	**Mon 26-04-21**	**Wed 02-06-21**	**$11,731.00**
473		Lintols	3 days	Mon 26-04-21	Wed 28-04-21	Mon 26-04-21	Wed 28-04-21	$260.00
474		Door Frames	7 days	Thu 29-04-21	Fri 07-05-21	Thu 29-04-21	Fri 07-05-21	$550.00
475		Door Panels	7 days	Mon 10-05-21	Tue 18-05-21	Mon 10-05-21	Tue 18-05-21	$1,920.00

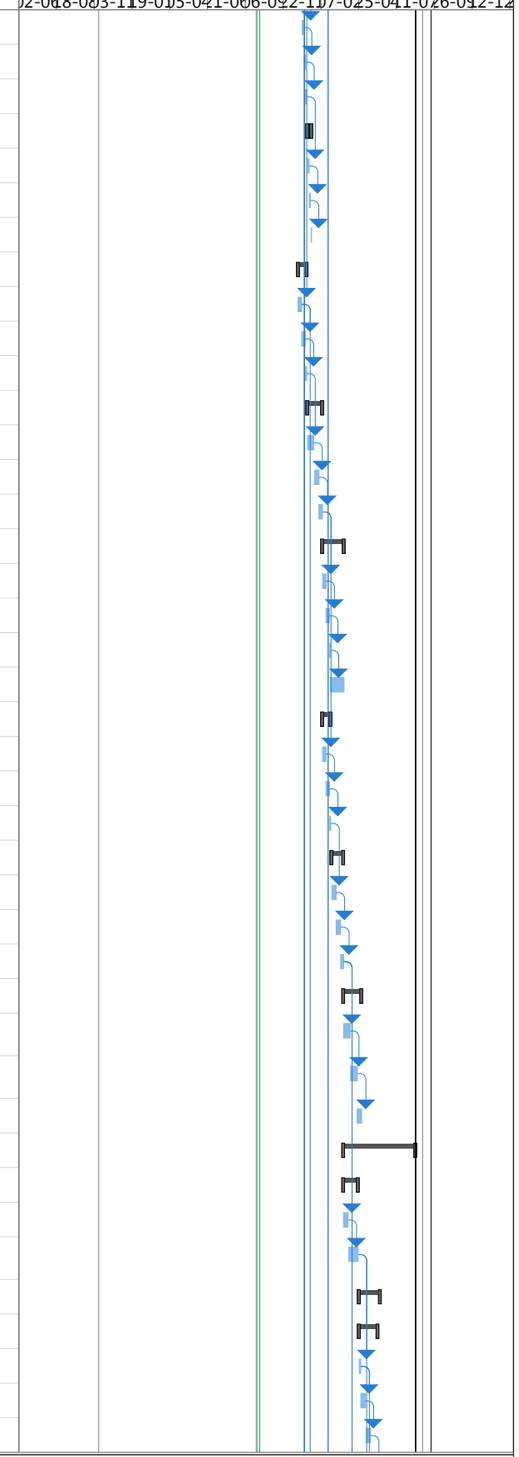

Project: Project1
Date: Tue 29-09-20

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress


ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
476		Ironmongeries including Door Finishes	5 days	Wed 19-05-21	Tue 25-05-21	Wed 19-05-21	Tue 25-05-21	$3,823.00
477		Automatic Roller Shutter	4 days	Wed 26-05-21	Mon 31-05-21	Wed 26-05-21	Mon 31-05-21	$4,300.00
478		Aluminium Sliding Doors & Gate	2 days	Tue 01-06-21	Wed 02-06-21	Tue 01-06-21	Wed 02-06-21	$878.00
479		**External Windows**	**28 days**	**Thu 29-04-21**	**Mon 07-06-21**	**Thu 29-04-21**	**Mon 07-06-21**	**$48,985.00**
480		Lintols	7 days	Thu 29-04-21	Fri 07-05-21	Thu 29-04-21	Fri 07-05-21	$2,420.00
481		Intallation of Aluminium Window Frames and Panels	21 days	Mon 10-05-21	Mon 07-06-21	Mon 10-05-21	Mon 07-06-21	$46,565.00
482		**Internal Walls& Partition**	**40 days**	**Thu 25-03-21**	**Wed 19-05-21**	**Thu 25-03-21**	**Wed 19-05-21**	**$75,057.00**
483		Installation of Brickwall (1Brick & Half Brick including Mild Steel Railing, Toilet Cubicle System c/w Sundries)	40 days	Thu 25-03-21	Wed 19-05-21	Thu 25-03-21	Wed 19-05-21	$75,057.00
484		**Internal Doors & Windows**	**29 days**	**Thu 20-05-21**	**Tue 29-06-21**	**Thu 20-05-21**	**Tue 29-06-21**	**$48,794.00**
485		**Internal Doors**	**29 days**	**Thu 20-05-21**	**Tue 29-06-21**	**Thu 20-05-21**	**Tue 29-06-21**	**$40,560.00**
486		Lintols and Heelstone	5 days	Thu 20-05-21	Wed 26-05-21	Thu 20-05-21	Wed 26-05-21	$880.00
487		Door Frames	7 days	Thu 27-05-21	Fri 04-06-21	Thu 27-05-21	Fri 04-06-21	$3,960.00
488		Door Panels	7 days	Mon 07-06-21	Tue 15-06-21	Mon 07-06-21	Tue 15-06-21	$18,700.00
489		Ironmongeries including Door Finishes	10 days	Wed 16-06-21	Tue 29-06-21	Wed 16-06-21	Tue 29-06-21	$17,020.00
490		**Internal Windows**	**12 days**	**Thu 20-05-21**	**Fri 04-06-21**	**Thu 20-05-21**	**Fri 04-06-21**	**$8,234.00**
491		Lintols	5 days	Thu 20-05-21	Wed 26-05-21	Thu 20-05-21	Wed 26-05-21	$560.00
492		Installation of Window Frames and Panels	7 days	Thu 27-05-21	Fri 04-06-21	Thu 27-05-21	Fri 04-06-21	$7,674.00
493		**Internal Wall Finishes**	**24 days**	**Thu 20-05-21**	**Tue 22-06-21**	**Thu 20-05-21**	**Tue 22-06-21**	**$59,045.00**
494		Plastering of Walls & Columns	14 days	Thu 20-05-21	Tue 08-06-21	Thu 20-05-21	Tue 08-06-21	$24,272.00
495		Wall Tiles	3 days	Wed 09-06-21	Fri 11-06-21	Wed 09-06-21	Fri 11-06-21	$9,825.00
496		Internal Wall Painting Finishes	7 days	Mon 14-06-21	Tue 22-06-21	Mon 14-06-21	Tue 22-06-21	$24,948.00
497		**Internal Floor Finishes**	**22 days**	**Wed 09-06-21**	**Thu 08-07-21**	**Wed 09-06-21**	**Thu 08-07-21**	**$103,024.00**
498		Cement Screed	7 days	Wed 09-06-21	Thu 17-06-21	Wed 09-06-21	Thu 17-06-21	$33,912.00
499		Waterproofing	2 days	Fri 18-06-21	Mon 21-06-21	Fri 18-06-21	Mon 21-06-21	$3,803.00
500		Floor Tiles Finishes including skirting	7 days	Tue 22-06-21	Wed 30-06-21	Tue 22-06-21	Wed 30-06-21	$41,169.00
501		Carpet Tiles including skirting	7 days	Tue 22-06-21	Wed 30-06-21	Tue 22-06-21	Wed 30-06-21	$11,325.00
502		Epoxy Floring	3 days	Thu 01-07-21	Mon 05-07-21	Thu 01-07-21	Mon 05-07-21	$10,725.00
503		Artificial Turfing	1 day	Tue 06-07-21	Tue 06-07-21	Tue 06-07-21	Tue 06-07-21	$1,890.00
504		PreCast Concrete Drain Cover	3 days	Tue 06-07-21	Thu 08-07-21	Tue 06-07-21	Thu 08-07-21	$200.00
505		**Internal Ceiling Finishes**	**19 days**	**Wed 23-06-21**	**Mon 19-07-21**	**Wed 23-06-21**	**Mon 19-07-21**	**$71,838.00**
506		Installation of Aluminium Strip Including all Fittings	7 days	Wed 23-06-21	Thu 01-07-21	Wed 23-06-21	Thu 01-07-21	$29,250.00
507		Installation of Ceiling Board	7 days	Fri 02-07-21	Mon 12-07-21	Fri 02-07-21	Mon 12-07-21	$35,490.00
508		Painting of Intrenal Ceiling	5 days	Tue 13-07-21	Mon 19-07-21	Tue 13-07-21	Mon 19-07-21	$7,098.00
509		**External Finishes**	**34 days**	**Tue 08-06-21**	**Fri 23-07-21**	**Tue 08-06-21**	**Fri 23-07-21**	**$116,882.00**
510		**External Wall**	**20 days**	**Tue 08-06-21**	**Mon 05-07-21**	**Tue 08-06-21**	**Mon 05-07-21**	**$71,140.00**
511		External Plastering to Wall, Columns, Hoods, Beam & Cavity Wall	10 days	Tue 08-06-21	Mon 21-06-21	Tue 08-06-21	Mon 21-06-21	$25,828.00
512		Waterproofong at Top of Hood	5 days	Tue 08-06-21	Mon 14-06-21	Tue 08-06-21	Mon 14-06-21	$21,930.00
513		External Wall Painting Finishes	10 days	Tue 22-06-21	Mon 05-07-21	Tue 22-06-21	Mon 05-07-21	$23,382.00
514		**External Floor Finishes**	**9 days**	**Tue 06-07-21**	**Fri 16-07-21**	**Tue 06-07-21**	**Fri 16-07-21**	**$7,792.00**
515		Cement Screed Finishes	5 days	Tue 06-07-21	Mon 12-07-21	Tue 06-07-21	Mon 12-07-21	$2,748.00
516		External Floor Tiling Finishes	4 days	Tue 13-07-21	Fri 16-07-21	Tue 13-07-21	Fri 16-07-21	$5,044.00

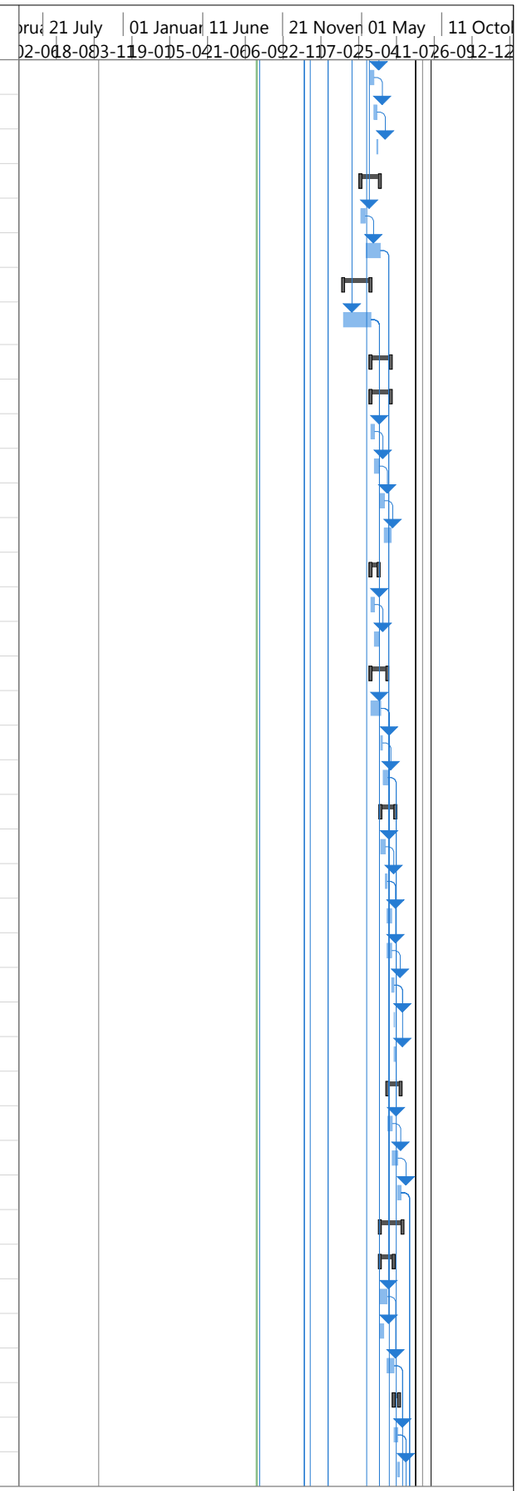

Project: Project1
Date: Tue 29-09-20

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress


ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
517		**External Ceiling Finishes**	**14 days**	**Tue 06-07-21**	**Fri 23-07-21**	**Tue 06-07-21**	**Fri 23-07-21**	**$37,950.00**
518		Installation of External Ceiling Finishes	14 days	Tue 06-07-21	Fri 23-07-21	Tue 06-07-21	Fri 23-07-21	$37,950.00
519		**Installation of Sanitary Appliances**	**15 days**	**Tue 20-07-21**	**Mon 09-08-21**	**Tue 20-07-21**	**Mon 09-08-21**	**$12,900.00**
520		WC, Cistern, Shower, Taps, Stop Cock, Wash Basins, Sink, Bidet, Handicap Rail, All Accessories and Testing Required	15 days	Tue 20-07-21	Mon 09-08-21	Tue 20-07-21	Mon 09-08-21	$12,900.00
521		**Other Builder's Work**	**22 days**	**Tue 20-07-21**	**Wed 18-08-21**	**Tue 20-07-21**	**Wed 18-08-21**	**$10,235.60**
522		Mass concrete at WC Base	7 days	Tue 20-07-21	Wed 28-07-21	Tue 20-07-21	Wed 28-07-21	$550.00
523		Counter Top & Bench	7 days	Tue 10-08-21	Wed 18-08-21	Tue 10-08-21	Wed 18-08-21	$2,100.00
524		Sliding Pole	7 days	Tue 10-08-21	Wed 18-08-21	Tue 10-08-21	Wed 18-08-21	$7,585.60
525		**MENARA LATIHAN**	**249 days**	**Fri 18-09-20**	**Wed 01-09-21**	**Fri 18-09-20**	**Wed 01-09-21**	**$362,700.00**
526		**Structural Works**	**240 days**	**Fri 18-09-20**	**Thu 19-08-21**	**Fri 18-09-20**	**Thu 19-08-21**	**$245,247.00**
527		**Pile Caps and RC Stump**	**27 days**	**Fri 18-09-20**	**Mon 26-10-20**	**Fri 18-09-20**	**Mon 26-10-20**	**$15,502.34**
528		Excavation of Pile Caps	7 days	Fri 18-09-20	Mon 28-09-20	Fri 18-09-20	Mon 28-09-20	$252.00
529		Lean Concrete	4 days	Tue 29-09-20	Fri 02-10-20	Tue 29-09-20	Fri 02-10-20	$78.00
530		Installation of Formwork	5 days	Mon 05-10-20	Fri 09-10-20	Mon 05-10-20	Fri 09-10-20	$1,950.00
531		Installation of Rebars for Pile Caps and Stump	5 days	Mon 12-10-20	Fri 16-10-20	Mon 12-10-20	Fri 16-10-20	$4,852.34
532		Concreting Works of Pile Caps	2 days	Mon 19-10-20	Tue 20-10-20	Mon 19-10-20	Tue 20-10-20	$6,734.00
533		Installation of Stumps F/work	2 days	Wed 21-10-20	Thu 22-10-20	Wed 21-10-20	Thu 22-10-20	$600.00
534		Concreting Works for Stumps	1 day	Fri 23-10-20	Fri 23-10-20	Fri 23-10-20	Fri 23-10-20	$1,036.00
535		Backfilling& Compaction	1 day	Mon 26-10-20	Mon 26-10-20	Mon 26-10-20	Mon 26-10-20	$0.00
536		**Ground Beam Structures**	**17 days**	**Tue 27-10-20**	**Wed 18-11-20**	**Tue 27-10-20**	**Wed 18-11-20**	**$11,468.00**
537		Excavation of Ground Beam	2 days	Tue 27-10-20	Wed 28-10-20	Tue 27-10-20	Wed 28-10-20	$96.00
538		Lean Concrete	2 days	Thu 29-10-20	Fri 30-10-20	Thu 29-10-20	Fri 30-10-20	$96.00
539		Installation of F/works for Ground Beam	5 days	Mon 02-11-20	Fri 06-11-20	Mon 02-11-20	Fri 06-11-20	$3,450.00
540		Installation of G. Beam Rebars	5 days	Mon 09-11-20	Fri 13-11-20	Mon 09-11-20	Fri 13-11-20	$4,200.00
541		Concreting Works for Ground Beams	2 days	Mon 16-11-20	Tue 17-11-20	Mon 16-11-20	Tue 17-11-20	$3,626.00
542		Backfilling and Compaction	1 day	Wed 18-11-20	Wed 18-11-20	Wed 18-11-20	Wed 18-11-20	$0.00
543		**Ground Slab**	**7 days**	**Thu 19-11-20**	**Fri 27-11-20**	**Thu 19-11-20**	**Fri 27-11-20**	**$8,994.80**
544		Excavation for Ground Slab	1 day	Thu 19-11-20	Thu 19-11-20	Thu 19-11-20	Thu 19-11-20	$72.00
545		Anti Termite Treatment	1 day	Fri 20-11-20	Fri 20-11-20	Fri 20-11-20	Fri 20-11-20	$260.00
546		Installation of F/works	1 day	Mon 23-11-20	Mon 23-11-20	Mon 23-11-20	Mon 23-11-20	$500.00
547		Damp Proof Membrane	1 day	Tue 24-11-20	Tue 24-11-20	Tue 24-11-20	Tue 24-11-20	$260.00
548		Installation of Re-bars	2 days	Wed 25-11-20	Thu 26-11-20	Wed 25-11-20	Thu 26-11-20	$4,276.80
549		Concreting of Ground Slab	1 day	Fri 27-11-20	Fri 27-11-20	Fri 27-11-20	Fri 27-11-20	$3,626.00
550		**Frame**	**144 days**	**Mon 30-11-20**	**Thu 17-06-21**	**Mon 30-11-20**	**Thu 17-06-21**	**$122,211.86**
551		**Ground Floor - 1st Floor Columns**	**8 days**	**Mon 30-11-20**	**Wed 09-12-20**	**Mon 30-11-20**	**Wed 09-12-20**	**$8,965.83**
552		Installation of Formworks and Rebars	7 days	Mon 30-11-20	Tue 08-12-20	Mon 30-11-20	Tue 08-12-20	$4,735.53
553		Concreting Works	1 day	Wed 09-12-20	Wed 09-12-20	Wed 09-12-20	Wed 09-12-20	$4,230.30
554		**1st Floor R.C Beam & Floor Slab**	**8 days**	**Thu 10-12-20**	**Mon 21-12-20**	**Thu 10-12-20**	**Mon 21-12-20**	**$8,858.32**
555		Installation of F/works & Rebars	7 days	Thu 10-12-20	Fri 18-12-20	Thu 10-12-20	Fri 18-12-20	$6,268.32
556		Concreting Works	1 day	Mon 21-12-20	Mon 21-12-20	Mon 21-12-20	Mon 21-12-20	$2,590.00
557		**RC Staircase (GF -1st FL)**	**8 days**	**Tue 22-12-20**	**Thu 31-12-20**	**Tue 22-12-20**	**Thu 31-12-20**	**$3,262.93**

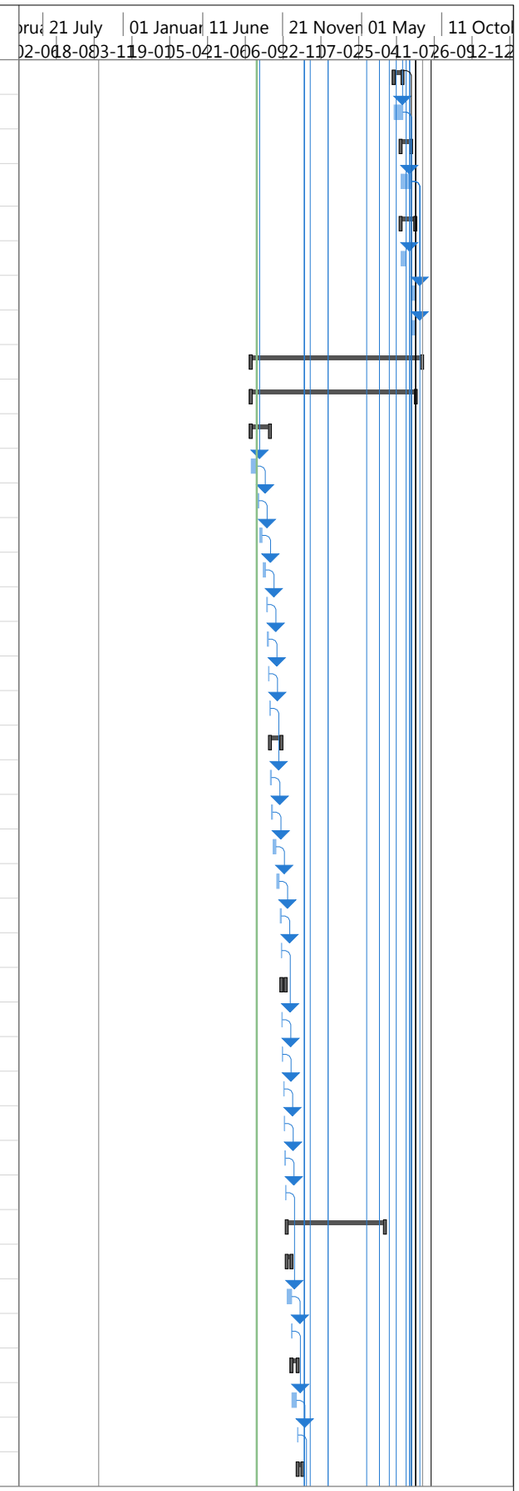

Project: Project1
Date: Tue 29-09-20

Task | Split | Milestone | Summary
Project Summary | Inactive Task | Inactive Milestone | Inactive Summary
Manual Task | Duration-only | Manual Summary Rollup | Manual Summary
Start-only | Finish-only | External Tasks | External Milestone
Deadline | Progress | Manual Progress


ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
558		Installation of F/works & Re-Bars	7 days	Tue 22-12-20	Wed 30-12-20	Tue 22-12-20	Wed 30-12-20	$2,296.00
559		Concreting of RC Staircase	1 day	Thu 31-12-20	Thu 31-12-20	Thu 31-12-20	Thu 31-12-20	$966.93
560		**1st Floor - 2nd Floor Columns**	**8 days**	**Fri 01-01-21**	**Tue 12-01-21**	**Fri 01-01-21**	**Tue 12-01-21**	**$8,965.83**
561		Installation of Formworks and Rebars	7 days	Fri 01-01-21	Mon 11-01-21	Fri 01-01-21	Mon 11-01-21	$4,735.53
562		Concreting Works	1 day	Tue 12-01-21	Tue 12-01-21	Tue 12-01-21	Tue 12-01-21	$4,230.30
563		**2nd Floor R.C Beam & Slab**	**8 days**	**Wed 13-01-21**	**Fri 22-01-21**	**Wed 13-01-21**	**Fri 22-01-21**	**$8,858.32**
564		Installation of F/works & Rebars	7 days	Wed 13-01-21	Thu 21-01-21	Wed 13-01-21	Thu 21-01-21	$6,268.32
565		Concreting Works	1 day	Fri 22-01-21	Fri 22-01-21	Fri 22-01-21	Fri 22-01-21	$2,590.00
566		**RC Staircase (1st -2nd FL)**	**8 days**	**Mon 25-01-21**	**Wed 03-02-21**	**Mon 25-01-21**	**Wed 03-02-21**	**$3,262.93**
567		Installation of F/works & Re-Bars	7 days	Mon 25-01-21	Tue 02-02-21	Mon 25-01-21	Tue 02-02-21	$2,296.00
568		Concreting of RC Staircase	1 day	Wed 03-02-21	Wed 03-02-21	Wed 03-02-21	Wed 03-02-21	$966.93
569		**2nd Floor - 3rd Floor Columns**	**8 days**	**Thu 04-02-21**	**Mon 15-02-21**	**Thu 04-02-21**	**Mon 15-02-21**	**$8,965.53**
570		Installation of Formworks and Rebars	7 days	Thu 04-02-21	Fri 12-02-21	Thu 04-02-21	Fri 12-02-21	$4,735.53
571		Concreting Works	1 day	Mon 15-02-21	Mon 15-02-21	Mon 15-02-21	Mon 15-02-21	$4,230.00
572		**3rd Floor R.C Beam & Slab**	**8 days**	**Tue 16-02-21**	**Thu 25-02-21**	**Tue 16-02-21**	**Thu 25-02-21**	**$8,858.32**
573		Installation of F/works & Rebars	7 days	Tue 16-02-21	Wed 24-02-21	Tue 16-02-21	Wed 24-02-21	$6,268.32
574		Concreting Works	1 day	Thu 25-02-21	Thu 25-02-21	Thu 25-02-21	Thu 25-02-21	$2,590.00
575		**RC Staircase (2nd -3rd FL)**	**8 days**	**Fri 26-02-21**	**Tue 09-03-21**	**Fri 26-02-21**	**Tue 09-03-21**	**$3,262.93**
576		Installation of F/works & Re-Bars	7 days	Fri 26-02-21	Mon 08-03-21	Fri 26-02-21	Mon 08-03-21	$2,296.00
577		Concreting of RC Staircase	1 day	Tue 09-03-21	Tue 09-03-21	Tue 09-03-21	Tue 09-03-21	$966.93
578		**3rd Floor - 4th Floor Columns**	**8 days**	**Wed 10-03-21**	**Fri 19-03-21**	**Wed 10-03-21**	**Fri 19-03-21**	**$8,965.83**
579		Installation of Formworks and Rebars	7 days	Wed 10-03-21	Thu 18-03-21	Wed 10-03-21	Thu 18-03-21	$4,735.53
580		Concreting Works	1 day	Fri 19-03-21	Fri 19-03-21	Fri 19-03-21	Fri 19-03-21	$4,230.30
581		**4th Floor RC Beam & Slab**	**8 days**	**Mon 22-03-21**	**Wed 31-03-21**	**Mon 22-03-21**	**Wed 31-03-21**	**$8,858.32**
582		Installation of Formworks and Rebars	7 days	Mon 22-03-21	Tue 30-03-21	Mon 22-03-21	Tue 30-03-21	$6,268.32
583		Concreting Works	1 day	Wed 31-03-21	Wed 31-03-21	Wed 31-03-21	Wed 31-03-21	$2,590.00
584		**RC Staircase (3rd - 4th FL)**	**8 days**	**Thu 01-04-21**	**Mon 12-04-21**	**Thu 01-04-21**	**Mon 12-04-21**	**$3,262.93**
585		Installation of Formworks and Rebars	7 days	Thu 01-04-21	Fri 09-04-21	Thu 01-04-21	Fri 09-04-21	$2,296.00
586		Concreting Works	1 day	Mon 12-04-21	Mon 12-04-21	Mon 12-04-21	Mon 12-04-21	$966.93
587		**4th Floor - 5th Floor Columns**	**8 days**	**Tue 13-04-21**	**Thu 22-04-21**	**Tue 13-04-21**	**Thu 22-04-21**	**$8,965.83**
588		Installation of Formworks and Rebars	7 days	Tue 13-04-21	Wed 21-04-21	Tue 13-04-21	Wed 21-04-21	$4,735.53
589		Concreting Works	1 day	Thu 22-04-21	Thu 22-04-21	Thu 22-04-21	Thu 22-04-21	$4,230.30
590		**5th Floor R.C Beam & Slab**	**8 days**	**Fri 23-04-21**	**Tue 04-05-21**	**Fri 23-04-21**	**Tue 04-05-21**	**$8,858.32**
591		Installation of F/works & Rebars	7 days	Fri 23-04-21	Mon 03-05-21	Fri 23-04-21	Mon 03-05-21	$6,268.32
592		Concreting Works	1 day	Tue 04-05-21	Tue 04-05-21	Tue 04-05-21	Tue 04-05-21	$2,590.00
593		**RC Staircase (4th -5th Level)**	**8 days**	**Wed 05-05-21**	**Fri 14-05-21**	**Wed 05-05-21**	**Fri 14-05-21**	**$3,262.93**
594		Installation of F/works & Rebars	7 days	Wed 05-05-21	Thu 13-05-21	Wed 05-05-21	Thu 13-05-21	$2,296.00
595		Concreting Works	1 day	Fri 14-05-21	Fri 14-05-21	Fri 14-05-21	Fri 14-05-21	$966.93
596		**5th Floor - Roof Level Columns**	**8 days**	**Mon 17-05-21**	**Wed 26-05-21**	**Mon 17-05-21**	**Wed 26-05-21**	**$8,965.83**
597		Installation of Formworks and Rebars	7 days	Mon 17-05-21	Tue 25-05-21	Mon 17-05-21	Tue 25-05-21	$4,735.53
598		Concreting Works	1 day	Wed 26-05-21	Wed 26-05-21	Wed 26-05-21	Wed 26-05-21	$4,230.30

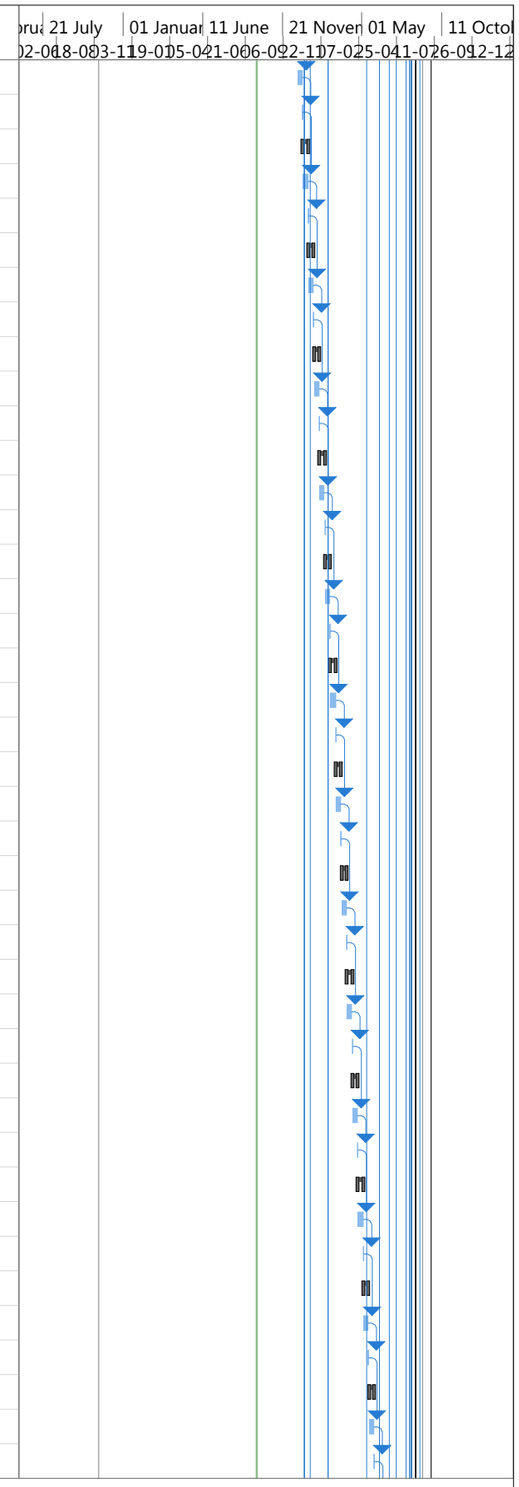

Project: Project1
Date: Tue 29-09-20

Task	Project Summary	Manual Task	Start-only	Deadline	
Split	Inactive Task	Duration-only	Finish-only	Progress	
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress	
Summary	Inactive Summary	Manual Summary	External Milestone		


ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
599		**Roof R.C Beam & Slab**	**8 days**	**Thu 27-05-21**	**Mon 07-06-21**	**Thu 27-05-21**	**Mon 07-06-21**	**$4,548.00**
600		Installation of F/works & Rebars	7 days	Thu 27-05-21	Fri 04-06-21	Thu 27-05-21	Fri 04-06-21	$2,994.00
601		Concreting Works	1 day	Mon 07-06-21	Mon 07-06-21	Mon 07-06-21	Mon 07-06-21	$1,554.00
602		**RC Staircase (5th -Roof Level)**	**8 days**	**Tue 08-06-21**	**Thu 17-06-21**	**Tue 08-06-21**	**Thu 17-06-21**	**$3,262.93**
603		Installation of F/works & Re-Bars	7 days	Tue 08-06-21	Wed 16-06-21	Tue 08-06-21	Wed 16-06-21	$2,296.00
604		Concreting of RC Staircase	1 day	Thu 17-06-21	Thu 17-06-21	Thu 17-06-21	Thu 17-06-21	$966.93
605		**Walls**	**14 days**	**Fri 18-06-21**	**Wed 07-07-21**	**Fri 18-06-21**	**Wed 07-07-21**	**$12,250.00**
606		Installation of Half Brick Wall including Waterproofing and Sundries	14 days	Fri 18-06-21	Wed 07-07-21	Fri 18-06-21	Wed 07-07-21	$12,250.00
607		**External Doors and Windows**	**17 days**	**Thu 08-07-21**	**Fri 30-07-21**	**Thu 08-07-21**	**Fri 30-07-21**	**$18,390.00**
608		Lintols	7 days	Thu 08-07-21	Fri 16-07-21	Thu 08-07-21	Fri 16-07-21	$500.00
609		Installation of Door Frames, Panels, Accessories, Ironmongeries and Finishing	10 days	Mon 19-07-21	Fri 30-07-21	Mon 19-07-21	Fri 30-07-21	$17,890.00
610		**Internal Finishes**	**45 days**	**Fri 18-06-21**	**Thu 19-08-21**	**Fri 18-06-21**	**Thu 19-08-21**	**$28,208.00**
611		**Internal Wall Finishes**	**24 days**	**Thu 08-07-21**	**Tue 10-08-21**	**Thu 08-07-21**	**Tue 10-08-21**	**$7,344.00**
612		Wall Plastering	14 days	Thu 08-07-21	Tue 27-07-21	Thu 08-07-21	Tue 27-07-21	$3,888.00
613		Wall Painting Finishes	10 days	Wed 28-07-21	Tue 10-08-21	Wed 28-07-21	Tue 10-08-21	$3,456.00
614		**Internal Floor Finishes**	**2 days**	**Wed 11-08-21**	**Thu 12-08-21**	**Wed 11-08-21**	**Thu 12-08-21**	**$352.00**
615		Cement Screed	2 days	Wed 11-08-21	Thu 12-08-21	Wed 11-08-21	Thu 12-08-21	$352.00
616		**Internal Ceiling Finishes**	**4 days**	**Fri 13-08-21**	**Wed 18-08-21**	**Fri 13-08-21**	**Wed 18-08-21**	**$616.00**
617		Ceiling Plastering Finishes	2 days	Fri 13-08-21	Mon 16-08-21	Fri 13-08-21	Mon 16-08-21	$308.00
618		Painting of Internal Ceiling	2 days	Tue 17-08-21	Wed 18-08-21	Tue 17-08-21	Wed 18-08-21	$308.00
619		**Staircase Finishes**	**45 days**	**Fri 18-06-21**	**Thu 19-08-21**	**Fri 18-06-21**	**Thu 19-08-21**	**$19,896.00**
620		Plastering Work and Painting Finishes to Staircase	30 days	Fri 18-06-21	Thu 29-07-21	Fri 18-06-21	Thu 29-07-21	$4,970.00
621		Mild Steel Railing	15 days	Fri 30-07-21	Thu 19-08-21	Fri 30-07-21	Thu 19-08-21	$14,926.00
622		**External Finishes**	**20 days**	**Thu 08-07-21**	**Wed 04-08-21**	**Thu 08-07-21**	**Wed 04-08-21**	**$28,222.00**
623		**External Wall Finishes**	**14 days**	**Thu 08-07-21**	**Tue 27-07-21**	**Thu 08-07-21**	**Tue 27-07-21**	**$24,273.00**
624		Wall Plastering, Waterproofing and WallPainting Finishes	14 days	Thu 08-07-21	Tue 27-07-21	Thu 08-07-21	Tue 27-07-21	$24,273.00
625		External Floor Finishes : Cement Screed	3 days	Wed 28-07-21	Fri 30-07-21	Wed 28-07-21	Fri 30-07-21	$1,872.00
626		External Ceiling Finishes: Cement Screed and Painting	3 days	Mon 02-08-21	Wed 04-08-21	Mon 02-08-21	Wed 04-08-21	$2,077.00
627		Wall Climbing System	20 days	Thu 05-08-21	Wed 01-09-21	Thu 05-08-21	Wed 01-09-21	$109,737.00
628		Roof Builder's Work: GI Pipes to Parapet Walls, MS Door & waterproofing Work	5 days	Thu 05-08-21	Wed 11-08-21	Thu 05-08-21	Wed 11-08-21	$7,716.00
629		**RUMAH PAM**	**59 days**	**Mon 02-11-20**	**Thu 21-01-21**	**Mon 02-11-20**	**Thu 21-01-21**	**$42,408.00**
630		**Structural Works**	**48 days**	**Mon 02-11-20**	**Wed 06-01-21**	**Mon 02-11-20**	**Wed 06-01-21**	**$25,175.70**
631		**Pad Footings and RC Stump**	**14 days**	**Mon 02-11-20**	**Thu 19-11-20**	**Mon 02-11-20**	**Thu 19-11-20**	**$9,043.50**
632		Building Setting out&Survey	1 day	Mon 02-11-20	Mon 02-11-20	Mon 02-11-20	Mon 02-11-20	$0.00
633		Excavation of Pad Footings	2 days	Tue 03-11-20	Wed 04-11-20	Tue 03-11-20	Wed 04-11-20	$320.00
634		Lean Concrete	1 day	Thu 05-11-20	Thu 05-11-20	Thu 05-11-20	Thu 05-11-20	$360.00
635		Installation of Formwork to Pad Footings	3 days	Fri 06-11-20	Tue 10-11-20	Fri 06-11-20	Tue 10-11-20	$1,050.00
636		Installation of Reinforcement Bars to Pad Footings& Stumps	3 days	Wed 11-11-20	Fri 13-11-20	Wed 11-11-20	Fri 13-11-20	$2,038.50
637		Concreting Works of Pad Footings	1 day	Mon 16-11-20	Mon 16-11-20	Mon 16-11-20	Mon 16-11-20	$4,500.00
638		Installation of Stumps F/works	1 day	Tue 17-11-20	Tue 17-11-20	Tue 17-11-20	Tue 17-11-20	$550.00
639		Concreting Works for Stumps	1 day	Wed 18-11-20	Wed 18-11-20	Wed 18-11-20	Wed 18-11-20	$225.00

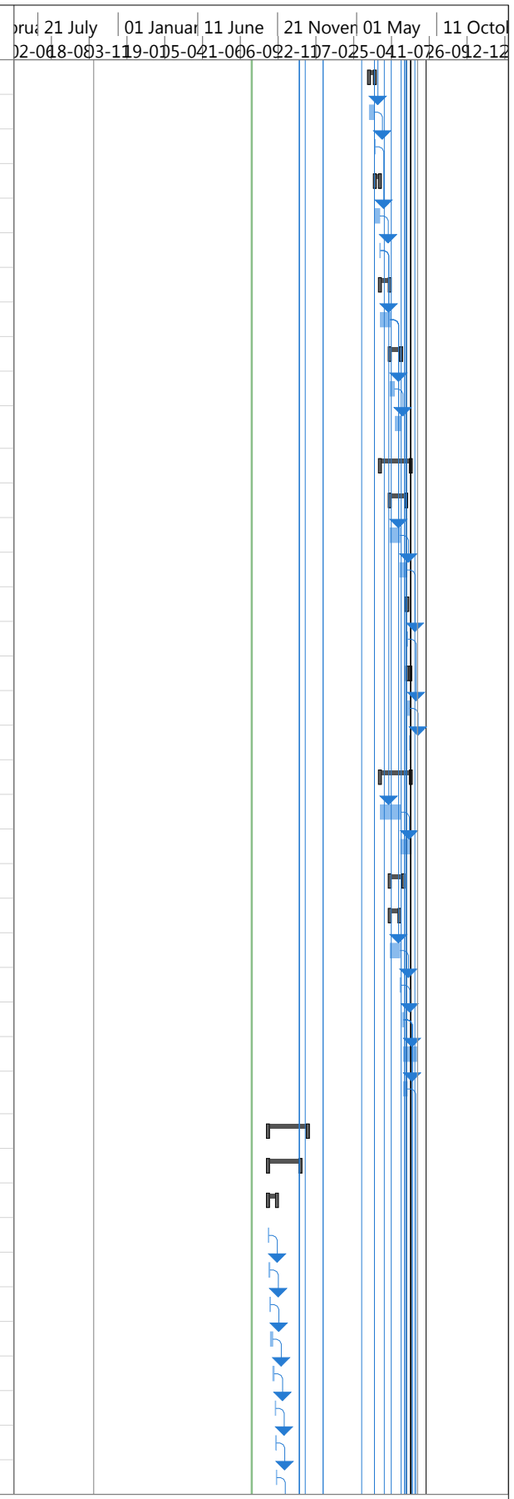

Project: Project1
Date: Tue 29-09-20

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone


ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
640		Backfilling&Compaction	1 day	Thu 19-11-20	Thu 19-11-20	Thu 19-11-20	Thu 19-11-20	$0.00
641		**Ground Beam Structures**	**11 days**	**Fri 20-11-20**	**Fri 04-12-20**	**Fri 20-11-20**	**Fri 04-12-20**	**$3,541.00**
642		Excavation of Ground Beam	2 days	Fri 20-11-20	Mon 23-11-20	Fri 20-11-20	Mon 23-11-20	$24.00
643		Lean Concrete	1 day	Tue 24-11-20	Tue 24-11-20	Tue 24-11-20	Tue 24-11-20	$75.00
644		Installation of Ground Beam F/works	3 days	Wed 25-11-20	Fri 27-11-20	Wed 25-11-20	Fri 27-11-20	$1,350.00
645		Installation of Ground Beam Rebars	3 days	Mon 30-11-20	Wed 02-12-20	Mon 30-11-20	Wed 02-12-20	$1,192.00
646		Concreting Works for Ground Beams	1 day	Thu 03-12-20	Thu 03-12-20	Thu 03-12-20	Thu 03-12-20	$900.00
647		Backfilling and Compaction	1 day	Fri 04-12-20	Fri 04-12-20	Fri 04-12-20	Fri 04-12-20	$0.00
648		**Ground Slab**	**10 days**	**Mon 07-12-20**	**Fri 18-12-20**	**Mon 07-12-20**	**Fri 18-12-20**	**$5,715.07**
649		Excavation of Ground Slab	1 day	Mon 07-12-20	Mon 07-12-20	Mon 07-12-20	Mon 07-12-20	$56.00
650		Anti Termite Treatment	1 day	Tue 08-12-20	Tue 08-12-20	Tue 08-12-20	Tue 08-12-20	$205.00
651		Installation of F/works	1 day	Wed 09-12-20	Wed 09-12-20	Wed 09-12-20	Wed 09-12-20	$210.00
652		Damp Proof Membrane	1 day	Thu 10-12-20	Thu 10-12-20	Thu 10-12-20	Thu 10-12-20	$120.00
653		Lean Concrete	1 day	Fri 11-12-20	Fri 11-12-20	Fri 11-12-20	Fri 11-12-20	$420.00
654		Installation of Re-bars	1 day	Mon 14-12-20	Mon 14-12-20	Mon 14-12-20	Mon 14-12-20	$1,174.50
655		Concreting of Ground Slab	1 day	Tue 15-12-20	Tue 15-12-20	Tue 15-12-20	Tue 15-12-20	$2,700.00
656		Plinth	3 days	Wed 16-12-20	Fri 18-12-20	Wed 16-12-20	Fri 18-12-20	$829.57
657		**Apron Slab & Ramp**	**6 days**	**Wed 16-12-20**	**Wed 23-12-20**	**Wed 16-12-20**	**Wed 23-12-20**	**$1,513.63**
658		Excavation for Apron Slab	1 day	Wed 16-12-20	Wed 16-12-20	Wed 16-12-20	Wed 16-12-20	$16.50
659		Installation of F/works	2 days	Thu 17-12-20	Fri 18-12-20	Thu 17-12-20	Fri 18-12-20	$0.00
660		Lean Concrete	1 day	Mon 21-12-20	Mon 21-12-20	Mon 21-12-20	Mon 21-12-20	$120.00
661		Installation of Re-bars	2 days	Tue 22-12-20	Wed 23-12-20	Tue 22-12-20	Wed 23-12-20	$832.13
662		Concreting of Apron Slab & Ramp	1 day	Tue 22-12-20	Tue 22-12-20	Tue 22-12-20	Tue 22-12-20	$545.00
663		**Columns**	**3 days**	**Wed 16-12-20**	**Fri 18-12-20**	**Wed 16-12-20**	**Fri 18-12-20**	**$1,311.00**
664		Installation of Formworks	1 day	Wed 16-12-20	Wed 16-12-20	Wed 16-12-20	Wed 16-12-20	$600.00
665		Installation of Reinforcement Bars	1 day	Thu 17-12-20	Thu 17-12-20	Thu 17-12-20	Thu 17-12-20	$351.00
666		Concreting Works	1 day	Fri 18-12-20	Fri 18-12-20	Fri 18-12-20	Fri 18-12-20	$360.00
667		**Roof Beams & Hoods**	**5 days**	**Mon 21-12-20**	**Fri 25-12-20**	**Mon 21-12-20**	**Fri 25-12-20**	**$2,991.50**
668		Installation of F/works for Roof Beams	2 days	Mon 21-12-20	Tue 22-12-20	Mon 21-12-20	Tue 22-12-20	$1,250.00
669		Installation of Rebars for Roof Beams	2 days	Wed 23-12-20	Thu 24-12-20	Wed 23-12-20	Thu 24-12-20	$391.50
670		Concreting Works for Roof Beams	1 day	Fri 25-12-20	Fri 25-12-20	Fri 25-12-20	Fri 25-12-20	$1,350.00
671		**RC Gutter**	**8 days**	**Mon 28-12-20**	**Wed 06-01-21**	**Mon 28-12-20**	**Wed 06-01-21**	**$1,060.00**
672		Installation of F/works	2 days	Mon 28-12-20	Tue 29-12-20	Mon 28-12-20	Tue 29-12-20	$250.00
673		Installation of Rebars	2 days	Wed 30-12-20	Thu 31-12-20	Wed 30-12-20	Thu 31-12-20	$252.00
674		Concreting of RC Gutter	2 days	Fri 01-01-21	Mon 04-01-21	Fri 01-01-21	Mon 04-01-21	$360.00
675		Waterproofing and Finishing of RC Gutter	2 days	Tue 05-01-21	Wed 06-01-21	Tue 05-01-21	Wed 06-01-21	$198.00
676		**Installation of Roofing System**	**8 days**	**Thu 07-01-21**	**Mon 18-01-21**	**Thu 07-01-21**	**Mon 18-01-21**	**$4,767.00**
677		Installation of Roof Trusses, Rafters, Battens, Purlins and all necessary Structural Items	3 days	Thu 07-01-21	Mon 11-01-21	Thu 07-01-21	Mon 11-01-21	$2,792.00
678		Intallation of Roof Covering; including Aluminium Foil Insulation, Chicken Wire Mesh, Facia Board, Gutter and other necessary finishes.	3 days	Tue 12-01-21	Thu 14-01-21	Tue 12-01-21	Thu 14-01-21	$1,510.00
679		Rainwater Downpipes (RWDP)	2 days	Fri 15-01-21	Mon 18-01-21	Fri 15-01-21	Mon 18-01-21	$465.00
680		**Architectural Works**	**13 days**	**Tue 05-01-21**	**Thu 21-01-21**	**Tue 05-01-21**	**Thu 21-01-21**	**$12,465.30**

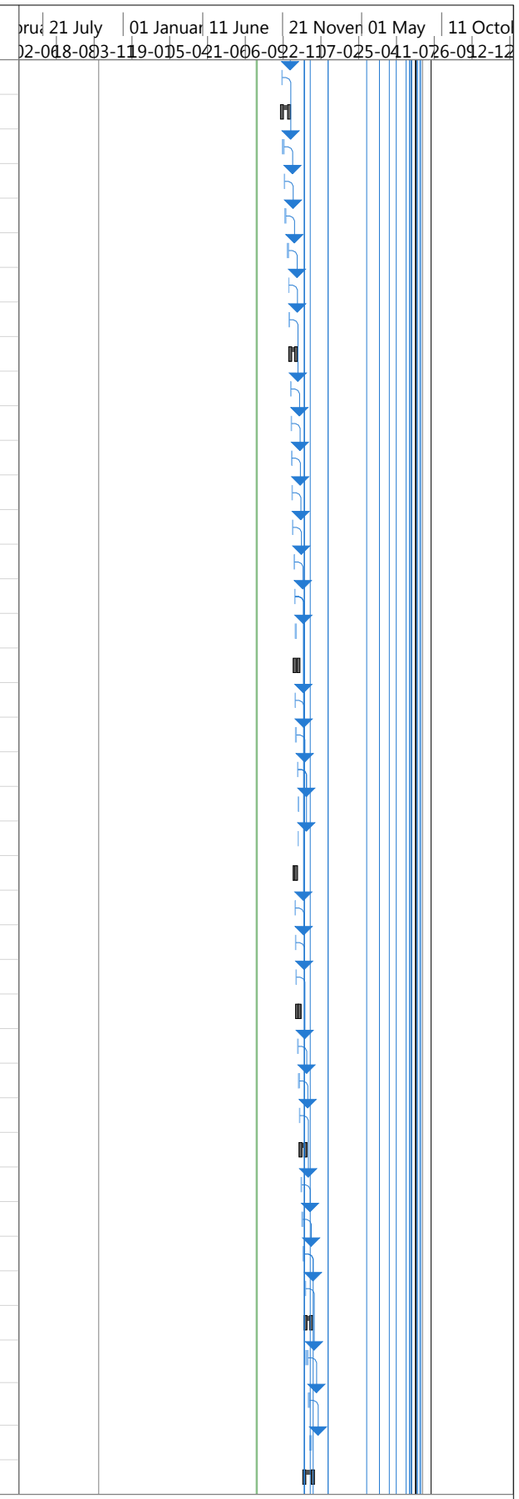

Project: Project1
Date: Tue 29-09-20

Task | Project Summary | Manual Task | Start-only | Deadline
Split | Inactive Task | Duration-only | Finish-only | Progress
Milestone | Inactive Milestone | Manual Summary Rollup | External Tasks | Manual Progress
Summary | Inactive Summary | Manual Summary | External Milestone


ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
681		**External Wall**	**3 days**	**Tue 05-01-21**	**Thu 07-01-21**	**Tue 05-01-21**	**Thu 07-01-21**	**$2,662.30**
682		External Wall (Half Brick Wall including all sundries)	3 days	Tue 05-01-21	Thu 07-01-21	Tue 05-01-21	Thu 07-01-21	$2,662.30
683		**External Doors & Windows**	**4 days**	**Fri 08-01-21**	**Wed 13-01-21**	**Fri 08-01-21**	**Wed 13-01-21**	**$2,110.00**
684		**External Doors**	**4 days**	**Fri 08-01-21**	**Wed 13-01-21**	**Fri 08-01-21**	**Wed 13-01-21**	**$1,265.00**
685		Lintols	1 day	Fri 08-01-21	Fri 08-01-21	Fri 08-01-21	Fri 08-01-21	$50.00
686		Door Frames	1 day	Mon 11-01-21	Mon 11-01-21	Mon 11-01-21	Mon 11-01-21	$0.00
687		Door Panels	1 day	Tue 12-01-21	Tue 12-01-21	Tue 12-01-21	Tue 12-01-21	$1,130.00
688		Ironmongeries including Door Finishes	1 day	Wed 13-01-21	Wed 13-01-21	Wed 13-01-21	Wed 13-01-21	$85.00
689		**External Windows**	**2 days**	**Fri 08-01-21**	**Mon 11-01-21**	**Fri 08-01-21**	**Mon 11-01-21**	**$845.00**
690		Lintols	1 day	Fri 08-01-21	Fri 08-01-21	Fri 08-01-21	Fri 08-01-21	$125.00
691		Intallation of Aluminium Window Frames and Panels	1 day	Mon 11-01-21	Mon 11-01-21	Mon 11-01-21	Mon 11-01-21	$720.00
692		**Internal Wall Finishes**	**5 days**	**Fri 08-01-21**	**Thu 14-01-21**	**Fri 08-01-21**	**Thu 14-01-21**	**$1,568.00**
693		Plastering of Walls& Columns	3 days	Fri 08-01-21	Tue 12-01-21	Fri 08-01-21	Tue 12-01-21	$784.00
694		Internal Wall Painting Finishes	2 days	Wed 13-01-21	Thu 14-01-21	Wed 13-01-21	Thu 14-01-21	$784.00
695		**Internal Floor Finishes**	**2 days**	**Fri 15-01-21**	**Mon 18-01-21**	**Fri 15-01-21**	**Mon 18-01-21**	**$455.00**
696		Cement Screed	2 days	Fri 15-01-21	Mon 18-01-21	Fri 15-01-21	Mon 18-01-21	$455.00
697		**Internal Ceiling Finishes**	**2 days**	**Tue 19-01-21**	**Wed 20-01-21**	**Tue 19-01-21**	**Wed 20-01-21**	**$2,850.00**
698		Plaster ceiling Finishes	1 day	Tue 19-01-21	Tue 19-01-21	Tue 19-01-21	Tue 19-01-21	$1,520.00
699		Painting of Intrenal Ceiling	1 day	Wed 20-01-21	Wed 20-01-21	Wed 20-01-21	Wed 20-01-21	$1,330.00
700		**External Finishes**	**7 days**	**Wed 13-01-21**	**Thu 21-01-21**	**Wed 13-01-21**	**Thu 21-01-21**	**$2,820.00**
701		**External Wall**	**5 days**	**Wed 13-01-21**	**Tue 19-01-21**	**Wed 13-01-21**	**Tue 19-01-21**	**$1,568.00**
702		External Plastering to External Wall	3 days	Wed 13-01-21	Fri 15-01-21	Wed 13-01-21	Fri 15-01-21	$784.00
703		External Wall Painting Finishes	2 days	Mon 18-01-21	Tue 19-01-21	Mon 18-01-21	Tue 19-01-21	$784.00
704		**External Floor Finishes**	**1 day**	**Wed 20-01-21**	**Wed 20-01-21**	**Wed 20-01-21**	**Wed 20-01-21**	**$252.00**
705		Cement Screed Finishes	1 day	Wed 20-01-21	Wed 20-01-21	Wed 20-01-21	Wed 20-01-21	$252.00
706		**External Ceiling Finishes**	**1 day**	**Thu 21-01-21**	**Thu 21-01-21**	**Thu 21-01-21**	**Thu 21-01-21**	**$1,000.00**
707		External Ceiling Finishes	1 day	Thu 21-01-21	Thu 21-01-21	Thu 21-01-21	Thu 21-01-21	$1,000.00
708		**TEMPAT LETAK KERETA BERBUMBUNG**	**29 days**	**Mon 01-03-21**	**Thu 08-04-21**	**Mon 01-03-21**	**Thu 08-04-21**	**$26,598.00**
709		Excavation of Pad Footings	3 days	Mon 01-03-21	Wed 03-03-21	Mon 01-03-21	Wed 03-03-21	$64.00
710		Installation of F/works to Pad Footings including Lean Concrete	3 days	Thu 04-03-21	Mon 08-03-21	Thu 04-03-21	Mon 08-03-21	$670.00
711		Installation of Rebars to Pad Footings & Stumps	3 days	Tue 09-03-21	Thu 11-03-21	Tue 09-03-21	Thu 11-03-21	$1,209.00
712		Concreting of Pad Footings	3 days	Fri 12-03-21	Tue 16-03-21	Fri 12-03-21	Tue 16-03-21	$1,350.00
713		Installation of F/works and Concreting of Stumps	2 days	Wed 17-03-21	Thu 18-03-21	Wed 17-03-21	Thu 18-03-21	$750.00
714		Backfill	1 day	Fri 19-03-21	Fri 19-03-21	Fri 19-03-21	Fri 19-03-21	$6.50
715		Installation of GI Posts	7 days	Mon 22-03-21	Tue 30-03-21	Mon 22-03-21	Tue 30-03-21	$4,362.00
716		Installation of Roofing System	7 days	Wed 31-03-21	Thu 08-04-21	Wed 31-03-21	Thu 08-04-21	$18,186.50
717		**STOR LOGISTIK**	**114 days**	**Tue 01-12-20**	**Fri 07-05-21**	**Tue 01-12-20**	**Fri 07-05-21**	**$83,699.65**
718		**Structural Works**	**82 days**	**Tue 01-12-20**	**Wed 24-03-21**	**Tue 01-12-20**	**Wed 24-03-21**	**$50,165.50**
719		**Pad Footings and RC Stump**	**29 days**	**Tue 01-12-20**	**Fri 08-01-21**	**Tue 01-12-20**	**Fri 08-01-21**	**$11,039.50**
720		Building Setting out&Survey	2 days	Tue 01-12-20	Wed 02-12-20	Tue 01-12-20	Wed 02-12-20	$0.00
721		Excavation of Pad Footings	7 days	Thu 03-12-20	Fri 11-12-20	Thu 03-12-20	Fri 11-12-20	$504.00

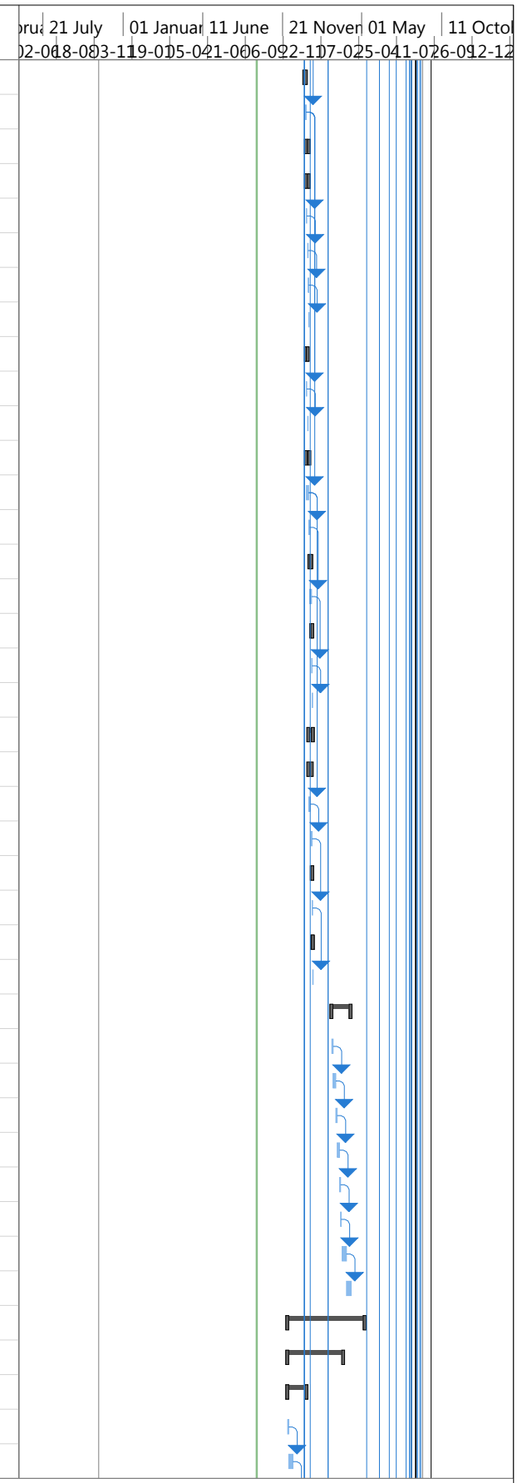

Project: Project1
Date: Tue 29-09-20

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress


ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
722		Lean Concrete	3 days	Mon 14-12-20	Wed 16-12-20	Mon 14-12-20	Wed 16-12-20	$570.00
723		Installation of Formwork to Pad Footings	5 days	Thu 17-12-20	Wed 23-12-20	Thu 17-12-20	Wed 23-12-20	$1,600.00
724		Installation of Reinforcement Bars to Pad Footings&Stumps	5 days	Thu 24-12-20	Wed 30-12-20	Thu 24-12-20	Wed 30-12-20	$2,560.50
725		Concreting Works of Pad Footings	3 days	Thu 31-12-20	Mon 04-01-21	Thu 31-12-20	Mon 04-01-21	$4,750.00
726		Installation of Stumps F/works	1 day	Tue 05-01-21	Tue 05-01-21	Tue 05-01-21	Tue 05-01-21	$650.00
727		Concreting Works for Stumps	1 day	Wed 06-01-21	Wed 06-01-21	Wed 06-01-21	Wed 06-01-21	$405.00
728		Backfilling&Compaction	2 days	Thu 07-01-21	Fri 08-01-21	Thu 07-01-21	Fri 08-01-21	$0.00
729		**Ground Beam Structures**	**18 days**	**Mon 11-01-21**	**Wed 03-02-21**	**Mon 11-01-21**	**Wed 03-02-21**	**$10,107.00**
730		Excavation of Ground Beam	3 days	Mon 11-01-21	Wed 13-01-21	Mon 11-01-21	Wed 13-01-21	$72.00
731		Lean Concrete	2 days	Thu 14-01-21	Fri 15-01-21	Thu 14-01-21	Fri 15-01-21	$285.00
732		Installation of Ground Beam F/works	4 days	Mon 18-01-21	Thu 21-01-21	Mon 18-01-21	Thu 21-01-21	$3,650.00
733		Installation of Ground Beam Rebars	4 days	Fri 22-01-21	Wed 27-01-21	Fri 22-01-21	Wed 27-01-21	$2,500.00
734		Concreting Works for Ground Beams	3 days	Thu 28-01-21	Mon 01-02-21	Thu 28-01-21	Mon 01-02-21	$3,600.00
735		Backfilling and Compaction	2 days	Tue 02-02-21	Wed 03-02-21	Tue 02-02-21	Wed 03-02-21	$0.00
736		**Ground Slab**	**9 days**	**Thu 04-02-21**	**Tue 16-02-21**	**Thu 04-02-21**	**Tue 16-02-21**	**$9,129.00**
737		Excavation of Ground Slab	2 days	Thu 04-02-21	Fri 05-02-21	Thu 04-02-21	Fri 05-02-21	$104.00
738		Anti Termite Treatment	1 day	Mon 08-02-21	Mon 08-02-21	Mon 08-02-21	Mon 08-02-21	$425.00
739		Installation of F/works	1 day	Tue 09-02-21	Tue 09-02-21	Tue 09-02-21	Tue 09-02-21	$425.00
740		Damp Proof Membrane	1 day	Wed 10-02-21	Wed 10-02-21	Wed 10-02-21	Wed 10-02-21	$315.00
741		Lean Concrete	1 day	Thu 11-02-21	Thu 11-02-21	Thu 11-02-21	Thu 11-02-21	$660.00
742		Installation of Re-bars	2 days	Fri 12-02-21	Mon 15-02-21	Fri 12-02-21	Mon 15-02-21	$3,150.00
743		Concreting of Ground Slab	1 day	Tue 16-02-21	Tue 16-02-21	Tue 16-02-21	Tue 16-02-21	$4,050.00
744		**Apron Slab & Ramp**	**5 days**	**Wed 17-02-21**	**Tue 23-02-21**	**Wed 17-02-21**	**Tue 23-02-21**	**$4,303.00**
745		Excavation for Apron Slab	1 day	Wed 17-02-21	Wed 17-02-21	Wed 17-02-21	Wed 17-02-21	$32.00
746		Installation of F/works	1 day	Thu 18-02-21	Thu 18-02-21	Thu 18-02-21	Thu 18-02-21	$0.00
747		Lean Concrete	1 day	Fri 19-02-21	Fri 19-02-21	Fri 19-02-21	Fri 19-02-21	$0.00
748		Installation of Re-bars	1 day	Mon 22-02-21	Mon 22-02-21	Mon 22-02-21	Mon 22-02-21	$989.00
749		Concreting of Apron Slab& Ramp	1 day	Tue 23-02-21	Tue 23-02-21	Tue 23-02-21	Tue 23-02-21	$3,282.00
750		**Columns**	**7 days**	**Wed 24-02-21**	**Thu 04-03-21**	**Wed 24-02-21**	**Thu 04-03-21**	**$5,577.00**
751		Installation of Formworks	3 days	Wed 24-02-21	Fri 26-02-21	Wed 24-02-21	Fri 26-02-21	$1,950.00
752		Installation of Reinforcement Bars	3 days	Mon 01-03-21	Wed 03-03-21	Mon 01-03-21	Wed 03-03-21	$2,277.00
753		Concreting Works	1 day	Thu 04-03-21	Thu 04-03-21	Thu 04-03-21	Thu 04-03-21	$1,350.00
754		**Roof Beams & Hoods**	**8 days**	**Fri 05-03-21**	**Tue 16-03-21**	**Fri 05-03-21**	**Tue 16-03-21**	**$7,490.00**
755		Installation of F/works for Roof Beams	3 days	Fri 05-03-21	Tue 09-03-21	Fri 05-03-21	Tue 09-03-21	$2,550.00
756		Installation of Rebars for Roof Beams	3 days	Wed 10-03-21	Fri 12-03-21	Wed 10-03-21	Fri 12-03-21	$2,790.00
757		Concreting Works for Roof Beams	2 days	Mon 15-03-21	Tue 16-03-21	Mon 15-03-21	Tue 16-03-21	$2,150.00
758		**RC Gutter**	**6 days**	**Wed 17-03-21**	**Wed 24-03-21**	**Wed 17-03-21**	**Wed 24-03-21**	**$2,520.00**
759		Installation of F/works	2 days	Wed 17-03-21	Thu 18-03-21	Wed 17-03-21	Thu 18-03-21	$900.00
760		Installation of Rebars	2 days	Fri 19-03-21	Mon 22-03-21	Fri 19-03-21	Mon 22-03-21	$720.00
761		Concreting of RC Gutter	2 days	Tue 23-03-21	Wed 24-03-21	Tue 23-03-21	Wed 24-03-21	$900.00
762		**Installation of Roofing System**	**9 days**	**Thu 25-03-21**	**Tue 06-04-21**	**Thu 25-03-21**	**Tue 06-04-21**	**$7,166.00**

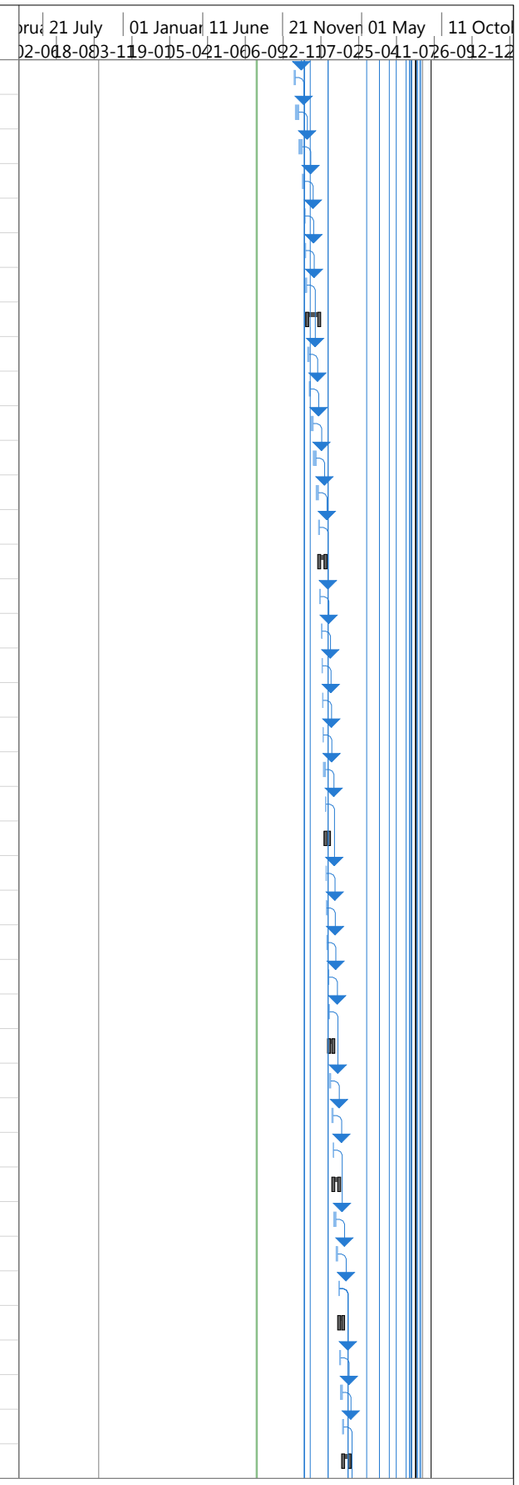

Project: Project1
Date: Tue 29-09-20

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone


ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
763		Installation of Roof Trusses, Rafters, Battens, Purlins and all necessary Structural Items	4 days	Thu 25-03-21	Tue 30-03-21	Thu 25-03-21	Tue 30-03-21	$1,550.00
764		Intallation of Roof Covering; including Aluminium Foil Insulation, Chicken Wire Mesh, Facia Board, Gutter and other necessary finishes.	4 days	Wed 31-03-21	Mon 05-04-21	Wed 31-03-21	Mon 05-04-21	$4,750.00
765		Rainwater Downpipes (RWDP)	1 day	Tue 06-04-21	Tue 06-04-21	Tue 06-04-21	Tue 06-04-21	$866.00
766		**Architectural Works**	**38 days**	**Wed 17-03-21**	**Fri 07-05-21**	**Wed 17-03-21**	**Fri 07-05-21**	**$26,368.15**
767		**External Wall**	**7 days**	**Wed 17-03-21**	**Thu 25-03-21**	**Wed 17-03-21**	**Thu 25-03-21**	**$4,770.00**
768		External Wall (Half Brick Wall including all sundries)	7 days	Wed 17-03-21	Thu 25-03-21	Wed 17-03-21	Thu 25-03-21	$4,770.00
769		**External Doors & Windows**	**6 days**	**Fri 26-03-21**	**Fri 02-04-21**	**Fri 26-03-21**	**Fri 02-04-21**	**$4,625.00**
770		**External Doors**	**3 days**	**Fri 26-03-21**	**Tue 30-03-21**	**Fri 26-03-21**	**Tue 30-03-21**	**$4,125.00**
771		Motorized Door including all Accessories	3 days	Fri 26-03-21	Tue 30-03-21	Fri 26-03-21	Tue 30-03-21	$4,125.00
772		**External Windows**	**3 days**	**Wed 31-03-21**	**Fri 02-04-21**	**Wed 31-03-21**	**Fri 02-04-21**	**$500.00**
773		Intallation of Aluminium Window Frames and Panels	3 days	Wed 31-03-21	Fri 02-04-21	Wed 31-03-21	Fri 02-04-21	$500.00
774		**Internal Wall**	**7 days**	**Wed 17-03-21**	**Thu 25-03-21**	**Wed 17-03-21**	**Thu 25-03-21**	**$1,359.15**
775		Internal Wall (Half Brick Including All sundries)	7 days	Wed 17-03-21	Thu 25-03-21	Wed 17-03-21	Thu 25-03-21	$1,359.15
776		**Internal Wall Finishes**	**14 days**	**Fri 26-03-21**	**Wed 14-04-21**	**Fri 26-03-21**	**Wed 14-04-21**	**$5,340.00**
777		Plastering of Walls&Columns	7 days	Fri 26-03-21	Mon 05-04-21	Fri 26-03-21	Mon 05-04-21	$2,848.00
778		Internal Wall Painting Finishes	7 days	Tue 06-04-21	Wed 14-04-21	Tue 06-04-21	Wed 14-04-21	$2,492.00
779		**Internal Floor Finishes**	**4 days**	**Thu 15-04-21**	**Tue 20-04-21**	**Thu 15-04-21**	**Tue 20-04-21**	**$1,068.00**
780		Cement Screed	2 days	Thu 15-04-21	Fri 16-04-21	Thu 15-04-21	Fri 16-04-21	$1,008.00
781		Internal Floor Grating	2 days	Mon 19-04-21	Tue 20-04-21	Mon 19-04-21	Tue 20-04-21	$60.00
782		**Internal Ceiling Finishes**	**3 days**	**Wed 21-04-21**	**Fri 23-04-21**	**Wed 21-04-21**	**Fri 23-04-21**	**$3,095.00**
783		Aluminium Ceiling Strip Finishes	3 days	Wed 21-04-21	Fri 23-04-21	Wed 21-04-21	Fri 23-04-21	$3,095.00
784		**External Wall**	**7 days**	**Tue 27-04-21**	**Wed 05-05-21**	**Tue 27-04-21**	**Wed 05-05-21**	**$4,458.00**
785		External Plastering to External Wall	4 days	Tue 27-04-21	Fri 30-04-21	Tue 27-04-21	Fri 30-04-21	$2,400.00
786		External Wall Painting Finishes	3 days	Mon 03-05-21	Wed 05-05-21	Mon 03-05-21	Wed 05-05-21	$2,058.00
787		**External Floor Finishes**	**3 days**	**Mon 19-04-21**	**Wed 21-04-21**	**Mon 19-04-21**	**Wed 21-04-21**	**$288.00**
788		Cement Screed Finishes	3 days	Mon 19-04-21	Wed 21-04-21	Mon 19-04-21	Wed 21-04-21	$288.00
789		**External Ceiling Finishes**	**2 days**	**Thu 06-05-21**	**Fri 07-05-21**	**Thu 06-05-21**	**Fri 07-05-21**	**$1,365.00**
790		External Ceiling Finishes	2 days	Thu 06-05-21	Fri 07-05-21	Thu 06-05-21	Fri 07-05-21	$1,365.00
791		**RUMAH SAMPAH**	**20 days**	**Thu 01-04-21**	**Wed 28-04-21**	**Thu 01-04-21**	**Wed 28-04-21**	**$13,950.00**
792		Construction of Rumah Sampah	20 days	Thu 01-04-21	Wed 28-04-21	Thu 01-04-21	Wed 28-04-21	$13,950.00
793		**BANGUNAN PENCAWANG SESB**	**90 days**	**Wed 15-07-20**	**Tue 17-11-20**	**Wed 15-07-20**	**Tue 17-11-20**	**$27,900.00**
794		Construction of Bangunan Pencawang SESB by SESB	90 days	Wed 15-07-20	Tue 17-11-20	Wed 15-07-20	Tue 17-11-20	$27,900.00
795		**MECHANICAL WORKS**	**283 days**	**Fri 31-07-20**	**Tue 31-08-21**	**Fri 31-07-20**	**Tue 31-08-21**	**$425,791.20**
796		**Internal Cold Water Plumbing**	**280 days**	**Fri 31-07-20**	**Thu 26-08-21**	**Fri 31-07-20**	**Thu 26-08-21**	**$106,020.00**
797		**Internal Cold Water Plumbing Services for Balai Bomba**	**63 days**	**Thu 20-05-21**	**Mon 16-08-21**	**Thu 20-05-21**	**Mon 16-08-21**	**$75,330.00**
798		To supply and install HDPE pipe from suction pump to storage water tank	3 days	Thu 20-05-21	Mon 24-05-21	Thu 20-05-21	Mon 24-05-21	$2,325.00
799		Pumping System	3 days	Wed 09-06-21	Fri 11-06-21	Wed 09-06-21	Fri 11-06-21	$26,505.00
800		Suction Water Tank	3 days	Mon 14-06-21	Wed 16-06-21	Mon 14-06-21	Wed 16-06-21	$16,740.00
801		Elevated Water Tank	7 days	Thu 17-06-21	Fri 25-06-21	Thu 17-06-21	Fri 25-06-21	$8,370.00
802		To supply and install HDPE pipe to main distributor dropper	10 days	Thu 20-05-21	Wed 02-06-21	Thu 20-05-21	Wed 02-06-21	$2,790.00
803		To supply and install HDPE pipes to all sanitary Fittings	5 days	Tue 10-08-21	Mon 16-08-21	Tue 10-08-21	Mon 16-08-21	$18,600.00

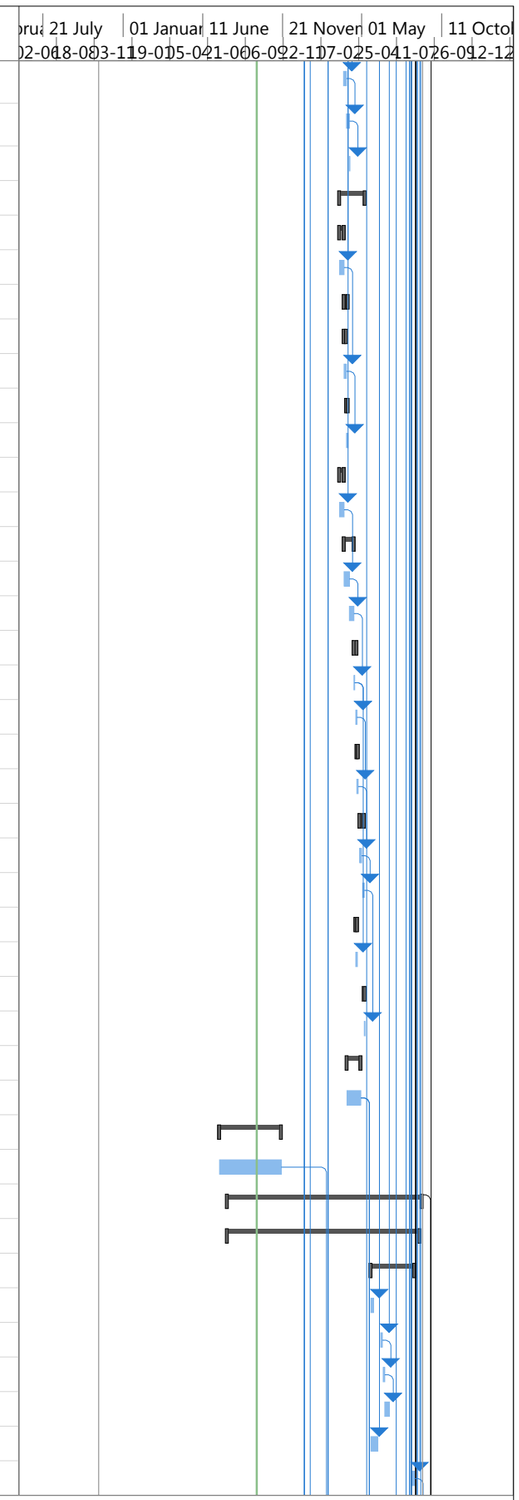

Project: Project1
Date: Tue 29-09-20

Task | Project Summary | Manual Task | Start-only | Deadline
Split | Inactive Task | Duration-only | Finish-only | Progress
Milestone | Inactive Milestone | Manual Summary Rollup | External Tasks | Manual Progress
Summary | Inactive Summary | Manual Summary | External Milestone


ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
804		**Internal Cold Water Plumbing Services for Rumah Sampah**	**3 days**	**Thu 29-04-21**	**Mon 03-05-21**	**Thu 29-04-21**	**Mon 03-05-21**	**$3,720.00**
805		To supply and install cold water plumbing system to Rumah Sampah	3 days	Thu 29-04-21	Mon 03-05-21	Thu 29-04-21	Mon 03-05-21	$3,720.00
806		**Internal Cold Water Plumbing Services for Menara Latihan**	**7 days**	**Thu 12-08-21**	**Fri 20-08-21**	**Thu 12-08-21**	**Fri 20-08-21**	**$1,860.00**
807		To supply and install cold water plumbing system to Menara Latihan	7 days	Thu 12-08-21	Fri 20-08-21	Thu 12-08-21	Fri 20-08-21	$1,860.00
808		**Other Items**	**280 days**	**Fri 31-07-20**	**Thu 26-08-21**	**Fri 31-07-20**	**Thu 26-08-21**	**$25,110.00**
809		Flushing of Cold Water System	2 days	Mon 23-08-21	Tue 24-08-21	Mon 23-08-21	Tue 24-08-21	$1,860.00
810		Preparation, Submission of Shop Drawings, Catalogue, Samples etc.	1 day	Fri 31-07-20	Sat 01-08-20	Fri 31-07-20	Sat 01-08-20	$1,860.00
811		Submission of Operation Manual and As Built	1 day	Fri 30-04-21	Fri 30-04-21	Fri 30-04-21	Fri 30-04-21	$1,860.00
812		Testing & Commisioning	2 days	Wed 25-08-21	Thu 26-08-21	Wed 25-08-21	Thu 26-08-21	$7,440.00
813		Painting of Complete System, Identification, name plates etc	2 days	Mon 03-05-21	Tue 04-05-21	Mon 03-05-21	Tue 04-05-21	$930.00
814		Privide Manufacturer's Warranty	1 day	Fri 30-04-21	Sat 01-05-21	Fri 30-04-21	Sat 01-05-21	$1,860.00
815		Carry out Schedule Maintenance during DLP	1 day	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	$9,300.00
816		**Internal Sanitary plumbing Services**	**154 days**	**Fri 18-12-20**	**Wed 21-07-21**	**Fri 18-12-20**	**Wed 21-07-21**	**$67,518.00**
817		Construction of Internal Building Inpection Chamber (IC A & B)	7 days	Tue 13-07-21	Wed 21-07-21	Tue 13-07-21	Wed 21-07-21	$8,370.00
818		Construction of Internal Building Inpection Chamber (IC C at Rumah Sampah)	3 days	Thu 29-04-21	Mon 03-05-21	Thu 29-04-21	Mon 03-05-21	$4,185.00
819		100mm dia UPVC discharge pipes connect to adjacent manholes	7 days	Thu 04-02-21	Fri 12-02-21	Thu 04-02-21	Fri 12-02-21	$4,650.00
820		Supply and Install 225mm dia VCP Pipes to C&S Manholes	10 days	Thu 04-02-21	Wed 17-02-21	Thu 04-02-21	Wed 17-02-21	$8,835.00
821		0.75mm upvc pipes (underground floor traps to gully traps)	3 days	Fri 18-12-20	Tue 22-12-20	Fri 18-12-20	Tue 22-12-20	$5,208.00
822		100mm UPVC Brown pipes (on ground WC and Urinal discharged to adjacent IC	3 days	Fri 18-12-20	Tue 22-12-20	Fri 18-12-20	Tue 22-12-20	$5,208.00
823		0.75mm upvc pipes (undergroundground sink and wash basin to gully traps)	1 day	Fri 18-12-20	Fri 18-12-20	Fri 18-12-20	Fri 18-12-20	$5,952.00
824		100mm and 75mm vertical soil pipes for aboveground work	7 days	Wed 30-12-20	Thu 07-01-21	Wed 30-12-20	Thu 07-01-21	$9,300.00
825		**Supply and Install horizantal 100mm dia soil and 40mm dia waste pipes for above ground works**	**15 days**	**Mon 26-04-21**	**Fri 14-05-21**	**Mon 26-04-21**	**Fri 14-05-21**	**$9,300.00**
826		Basin/Sink Tap	3 days	Mon 26-04-21	Wed 28-04-21	Mon 26-04-21	Wed 28-04-21	$1,860.00
827		Water Closet	3 days	Thu 29-04-21	Mon 03-05-21	Thu 29-04-21	Mon 03-05-21	$1,860.00
828		Shower	3 days	Tue 04-05-21	Thu 06-05-21	Tue 04-05-21	Thu 06-05-21	$1,860.00
829		Urinal	3 days	Fri 07-05-21	Tue 11-05-21	Fri 07-05-21	Tue 11-05-21	$1,860.00
830		Floor Traps & Other Fittings	3 days	Wed 12-05-21	Fri 14-05-21	Wed 12-05-21	Fri 14-05-21	$1,860.00
831		**Other Items**	**15 days**	**Mon 17-05-21**	**Fri 04-06-21**	**Mon 17-05-21**	**Fri 04-06-21**	**$6,510.00**
832		**Testing & Commissioning**	**15 days**	**Mon 17-05-21**	**Fri 04-06-21**	**Mon 17-05-21**	**Fri 04-06-21**	**$6,510.00**
833		Submission of Test Result before Final Testing	1 day	Mon 17-05-21	Mon 17-05-21	Mon 17-05-21	Mon 17-05-21	$4,650.00
834		Leak Test, Flow Test	7 days	Tue 18-05-21	Wed 26-05-21	Tue 18-05-21	Wed 26-05-21	$930.00
835		Training Employer Personnel	7 days	Thu 27-05-21	Fri 04-06-21	Thu 27-05-21	Fri 04-06-21	$930.00
836		**Air Conditioning and Mechanical Services**	**149 days**	**Mon 01-02-21**	**Thu 26-08-21**	**Mon 01-02-21**	**Thu 26-08-21**	**$76,390.20**
837		**Balai Bomba**	**22 days**	**Tue 20-07-21**	**Wed 18-08-21**	**Tue 20-07-21**	**Wed 18-08-21**	**$51,745.20**
838		To supply and Install Ceiling Inverter Type Air Cooled Split Unit	15 days	Tue 20-07-21	Mon 09-08-21	Tue 20-07-21	Mon 09-08-21	$24,105.60
839		To Supply and Install Wall Inverter Type Air Cooled Type Split Unit	7 days	Tue 10-08-21	Wed 18-08-21	Tue 10-08-21	Wed 18-08-21	$16,386.60
840		To Supply and Install Exhaust Fan (Propeller Type with Automatic Shutter)	5 days	Tue 20-07-21	Mon 26-07-21	Tue 20-07-21	Mon 26-07-21	$2,883.00
841		To Supply and Install Exhaust Fan (Ceiling Type)	3 days	Tue 27-07-21	Thu 29-07-21	Tue 27-07-21	Thu 29-07-21	$4,650.00
842		Kitchen Range Hood	2 days	Fri 30-07-21	Mon 02-08-21	Fri 30-07-21	Mon 02-08-21	$3,720.00
843		**Menara Latihan**	**9 days**	**Thu 05-08-21**	**Tue 17-08-21**	**Thu 05-08-21**	**Tue 17-08-21**	**$5,580.00**
844		Smoke Exhaust Hood	3 days	Thu 05-08-21	Mon 09-08-21	Thu 05-08-21	Mon 09-08-21	$2,790.00

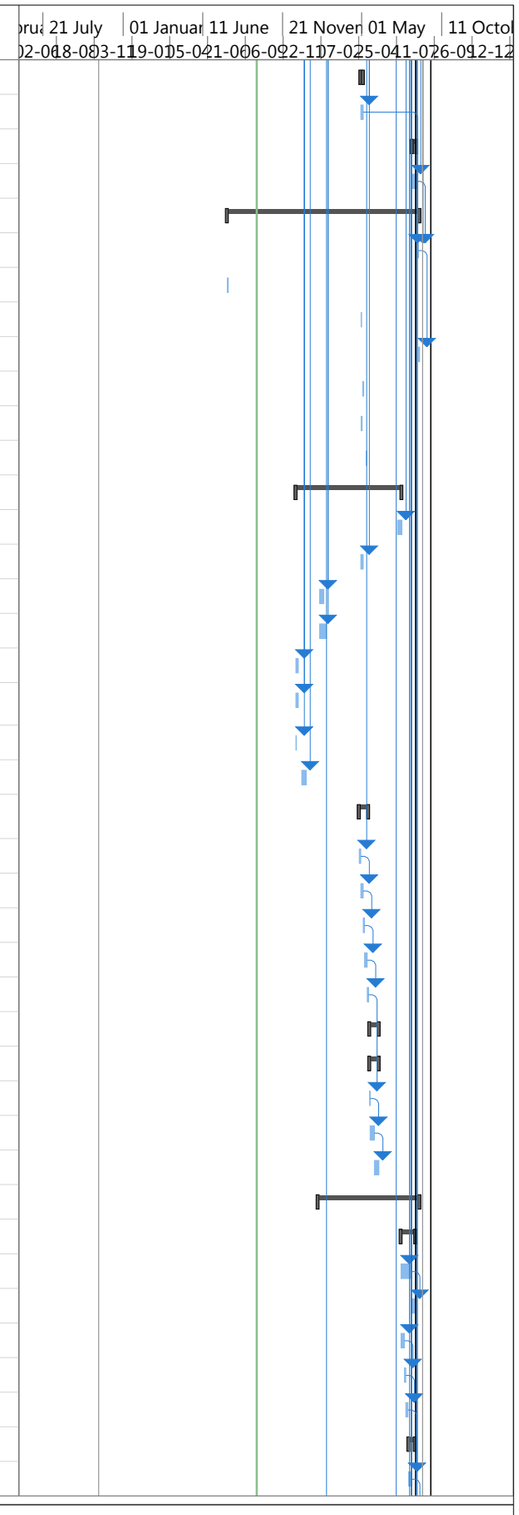

Project: Project1
Date: Tue 29-09-20

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone


ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
845		Smoke Exhaust Fan	3 days	Tue 10-08-21	Thu 12-08-21	Tue 10-08-21	Thu 12-08-21	$2,790.00
846		GI Duct c/w External Grill	3 days	Fri 13-08-21	Tue 17-08-21	Fri 13-08-21	Tue 17-08-21	$0.00
847		**Other Items**	**149 days**	**Mon 01-02-21**	**Thu 26-08-21**	**Mon 01-02-21**	**Thu 26-08-21**	**$19,065.00**
848		**Testing & Commissioning**	**149 days**	**Mon 01-02-21**	**Thu 26-08-21**	**Mon 01-02-21**	**Thu 26-08-21**	**$19,065.00**
849		Submission to SO before Final Test	1 day	Wed 18-08-21	Wed 18-08-21	Wed 18-08-21	Wed 18-08-21	$465.00
850		All Equipment Test	3 days	Thu 19-08-21	Mon 23-08-21	Thu 19-08-21	Mon 23-08-21	$4,650.00
851		Training of Employer's Personnel	3 days	Tue 24-08-21	Thu 26-08-21	Tue 24-08-21	Thu 26-08-21	$930.00
852		Submission of Shop Drawings, Catalogue, Brochures, Samples etc	1 day	Mon 01-02-21	Mon 01-02-21	Mon 01-02-21	Mon 01-02-21	$1,860.00
853		Submission of Operation Manual and As Built Drawings	1 day	Tue 24-08-21	Tue 24-08-21	Tue 24-08-21	Tue 24-08-21	$1,860.00
854		Carry out Schedule Maintenance during DLP	1 day	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	$9,300.00
855		**Fire Protection Services**	**132 days**	**Mon 01-03-21**	**Tue 31-08-21**	**Mon 01-03-21**	**Tue 31-08-21**	**$27,063.00**
856		Portable Fire Extinguisher for all Buildings	3 days	Mon 26-07-21	Wed 28-07-21	Mon 26-07-21	Wed 28-07-21	$5,859.00
857		Dry riser System	14 days	Thu 05-08-21	Tue 24-08-21	Thu 05-08-21	Tue 24-08-21	$11,160.00
858		Drain Outlet Pipe to Kolah Air	7 days	Thu 05-08-21	Fri 13-08-21	Thu 05-08-21	Fri 13-08-21	$4,650.00
859		**Other Item**	**132 days**	**Mon 01-03-21**	**Tue 31-08-21**	**Mon 01-03-21**	**Tue 31-08-21**	**$5,394.00**
860		**Testing & Commissioning**	**132 days**	**Mon 01-03-21**	**Tue 31-08-21**	**Mon 01-03-21**	**Tue 31-08-21**	**$5,394.00**
861		Submission of Test Result Before Final Testing	1 day	Wed 25-08-21	Wed 25-08-21	Wed 25-08-21	Wed 25-08-21	$930.00
862		All Equipment Test	2 days	Thu 26-08-21	Fri 27-08-21	Thu 26-08-21	Fri 27-08-21	$930.00
863		Training for Employer's Personnel	2 days	Mon 30-08-21	Tue 31-08-21	Mon 30-08-21	Tue 31-08-21	$930.00
864		Submission of Shop Drawings, Catalogue, Brochures, Samples etc	1 day	Mon 01-03-21	Mon 01-03-21	Mon 01-03-21	Mon 01-03-21	$930.00
865		Submission of Operation Manual and As Built	1 day	Mon 30-08-21	Mon 30-08-21	Mon 30-08-21	Mon 30-08-21	$930.00
866		Schedule Maintenance During DLP	1 day	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	$744.00
867		**Motorized Roller Shutter**	**119 days**	**Mon 15-03-21**	**Thu 26-08-21**	**Mon 15-03-21**	**Thu 26-08-21**	**$148,800.00**
868		To Supply and Install 4 Nos of Motorized Roller Shutter	20 days	Mon 26-07-21	Fri 20-08-21	Mon 26-07-21	Fri 20-08-21	$130,200.00
869		**Other Items**	**119 days**	**Mon 15-03-21**	**Thu 26-08-21**	**Mon 15-03-21**	**Thu 26-08-21**	**$18,600.00**
870		**Testing & Commissioning**	**119 days**	**Mon 15-03-21**	**Thu 26-08-21**	**Mon 15-03-21**	**Thu 26-08-21**	**$18,600.00**
871		Submission of Test Result Before Final Testing	1 day	Mon 23-08-21	Mon 23-08-21	Mon 23-08-21	Mon 23-08-21	$2,790.00
872		All Equipment Test	1 day	Tue 24-08-21	Tue 24-08-21	Tue 24-08-21	Tue 24-08-21	$930.00
873		Training for Employer's Personnel	1 day	Wed 25-08-21	Wed 25-08-21	Wed 25-08-21	Wed 25-08-21	$1,860.00
874		Submission of Shop Drawings, Catalogue, Brochures, Samples etc	1 day	Mon 15-03-21	Mon 15-03-21	Mon 15-03-21	Mon 15-03-21	$930.00
875		Submission of Operation Manual and As Built	1 day	Thu 26-08-21	Thu 26-08-21	Thu 26-08-21	Thu 26-08-21	$930.00
876		Schedule Maintenance During DLP	1 day	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	$11,160.00
877		**ELECTRICAL SERVICES**	**139 days**	**Thu 18-02-21**	**Tue 31-08-21**	**Thu 18-02-21**	**Tue 31-08-21**	**$1,051,513.80**
878		**Electrical Services for Internal Works**	**76 days**	**Mon 10-05-21**	**Mon 23-08-21**	**Mon 10-05-21**	**Mon 23-08-21**	**$357,966.30**
879		Electrical Works	30 days	Wed 23-06-21	Tue 03-08-21	Wed 23-06-21	Tue 03-08-21	$318,441.30
880		**Other Works**	**76 days**	**Mon 10-05-21**	**Mon 23-08-21**	**Mon 10-05-21**	**Mon 23-08-21**	**$39,525.00**
881		Galvanized Trunking	7 days	Wed 04-08-21	Thu 12-08-21	Wed 04-08-21	Thu 12-08-21	$13,950.00
882		Fire Barrier Materials for Floor Slab and Firewall	7 days	Wed 04-08-21	Thu 12-08-21	Wed 04-08-21	Thu 12-08-21	$3,255.00
883		Pre Testing	3 days	Fri 13-08-21	Tue 17-08-21	Fri 13-08-21	Tue 17-08-21	$9,300.00
884		Testing & Commissioning	3 days	Wed 18-08-21	Fri 20-08-21	Wed 18-08-21	Fri 20-08-21	$1,860.00
885		CPR Chart at Bilik Servis	1 day	Mon 23-08-21	Mon 23-08-21	Mon 23-08-21	Mon 23-08-21	$465.00

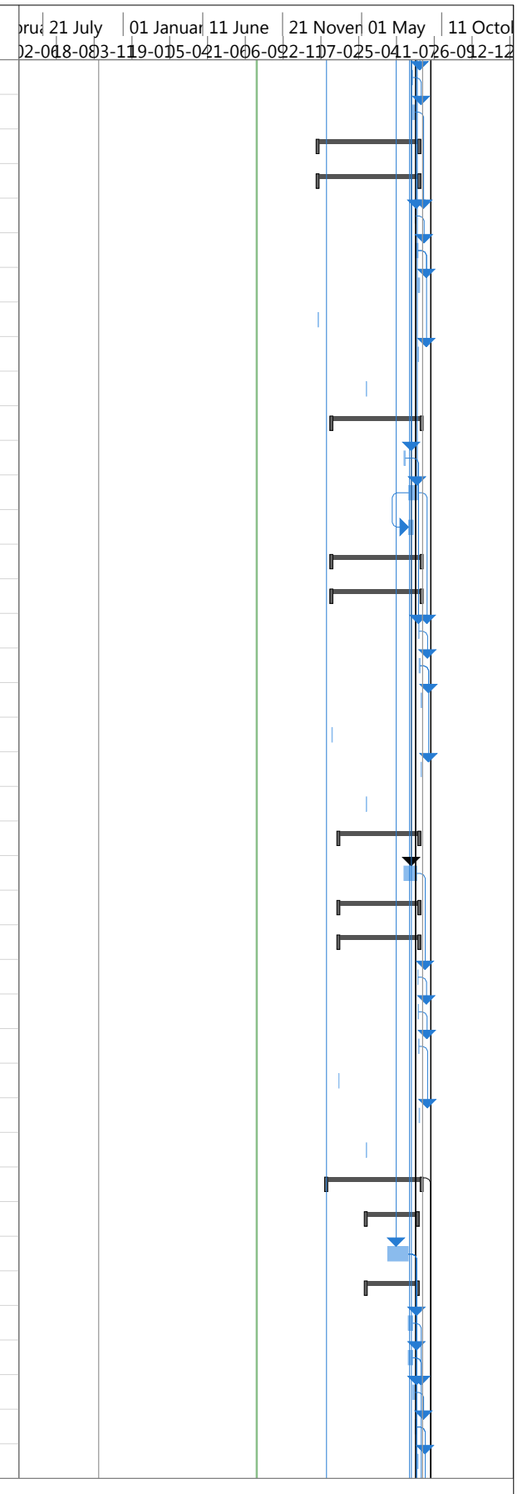

Project: Project1
Date: Tue 29-09-20

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	


ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
886		Electrical Schematic Chart at Bilik Servis	1 day	Mon 23-08-21	Mon 23-08-21	Mon 23-08-21	Mon 23-08-21	$1,395.00
887		LV incoming Cable	2 days	Fri 13-08-21	Mon 16-08-21	Fri 13-08-21	Mon 16-08-21	$4,650.00
888		River Sand at Bilik Servis	2 days	Tue 17-08-21	Wed 18-08-21	Tue 17-08-21	Wed 18-08-21	$1,860.00
889		Service & Maintenace during DLP	1 day	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	$2,790.00
890		**Telephone Services for Internal works**	**82 days**	**Mon 10-05-21**	**Tue 31-08-21**	**Mon 10-05-21**	**Tue 31-08-21**	**$81,049.50**
891		Telephone Works	14 days	Tue 20-07-21	Fri 06-08-21	Tue 20-07-21	Fri 06-08-21	$21,669.00
892		**Other Work**	**74 days**	**Mon 10-05-21**	**Thu 19-08-21**	**Mon 10-05-21**	**Thu 19-08-21**	**$10,695.50**
893		Galvanized Trunking	3 days	Mon 09-08-21	Wed 11-08-21	Mon 09-08-21	Wed 11-08-21	$1,860.00
894		Fire Barrier Materials in Riser	3 days	Thu 12-08-21	Mon 16-08-21	Thu 12-08-21	Mon 16-08-21	$930.50
895		Pre-Testing	2 days	Tue 17-08-21	Wed 18-08-21	Tue 17-08-21	Wed 18-08-21	$2,790.00
896		Testing & Commissioning	1 day	Thu 19-08-21	Thu 19-08-21	Thu 19-08-21	Thu 19-08-21	$1,860.00
897		Painting and Labelling	2 days	Tue 17-08-21	Wed 18-08-21	Tue 17-08-21	Wed 18-08-21	$1,395.00
898		Services and Maintenance During DLP	1 day	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	$1,860.00
899		**Information Communication Technology System**	**17 days**	**Mon 09-08-21**	**Tue 31-08-21**	**Mon 09-08-21**	**Tue 31-08-21**	**$48,685.00**
900		**ICT Main Equipment**	**17 days**	**Mon 09-08-21**	**Tue 31-08-21**	**Mon 09-08-21**	**Tue 31-08-21**	**$48,685.00**
901		Backbone Fibre	7 days	Mon 09-08-21	Tue 17-08-21	Mon 09-08-21	Tue 17-08-21	$7,440.00
902		Horizantal Cabling	5 days	Wed 18-08-21	Tue 24-08-21	Wed 18-08-21	Tue 24-08-21	$17,065.00
903		Network Switch	5 days	Wed 25-08-21	Tue 31-08-21	Wed 25-08-21	Tue 31-08-21	$24,180.00
904		**Lightning Protection System**	**78 days**	**Mon 10-05-21**	**Wed 25-08-21**	**Mon 10-05-21**	**Wed 25-08-21**	**$68,401.50**
905		Lightning Protection System	14 days	Mon 26-07-21	Thu 12-08-21	Mon 26-07-21	Thu 12-08-21	$62,821.50
906		**Other Works**	**78 days**	**Mon 10-05-21**	**Wed 25-08-21**	**Mon 10-05-21**	**Wed 25-08-21**	**$5,580.00**
907		Galvanized Trunking/Cable Tray	3 days	Fri 13-08-21	Tue 17-08-21	Fri 13-08-21	Tue 17-08-21	$930.00
908		Fire Barrier Material Through Floor	3 days	Wed 18-08-21	Fri 20-08-21	Wed 18-08-21	Fri 20-08-21	$465.00
909		Pre Testing	2 days	Mon 23-08-21	Tue 24-08-21	Mon 23-08-21	Tue 24-08-21	$1,395.00
910		Testing & Commissioning	1 day	Wed 25-08-21	Wed 25-08-21	Wed 25-08-21	Wed 25-08-21	$465.00
911		Painting and Labelling	1 day	Mon 23-08-21	Mon 23-08-21	Mon 23-08-21	Mon 23-08-21	$930.00
912		Service and Maintenace during DLP	1 day	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	$1,395.00
913		**Extra Low Voltage System**	**78 days**	**Mon 10-05-21**	**Wed 25-08-21**	**Mon 10-05-21**	**Wed 25-08-21**	**$66,867.00**
914		Public Address System (Main Equipment)	3 days	Wed 04-08-21	Fri 06-08-21	Wed 04-08-21	Fri 06-08-21	$25,110.00
915		Public Address System (Internal Works)	5 days	Mon 09-08-21	Fri 13-08-21	Mon 09-08-21	Fri 13-08-21	$17,391.00
916		MATV System	7 days	Wed 04-08-21	Thu 12-08-21	Wed 04-08-21	Thu 12-08-21	$17,391.00
917		**Other Works**	**78 days**	**Mon 10-05-21**	**Wed 25-08-21**	**Mon 10-05-21**	**Wed 25-08-21**	**$6,975.00**
918		Galvanized Trunking/Cable Tray	3 days	Fri 13-08-21	Tue 17-08-21	Fri 13-08-21	Tue 17-08-21	$1,395.00
919		Fire Barrier Material Through Riser	2 days	Wed 18-08-21	Thu 19-08-21	Wed 18-08-21	Thu 19-08-21	$930.00
920		Pre Testing	2 days	Fri 20-08-21	Mon 23-08-21	Fri 20-08-21	Mon 23-08-21	$1,860.00
921		Testing & Commissioning	2 days	Tue 24-08-21	Wed 25-08-21	Tue 24-08-21	Wed 25-08-21	$465.00
922		Painting and Labelling	1 day	Fri 20-08-21	Fri 20-08-21	Fri 20-08-21	Fri 20-08-21	$465.00
923		Service and Maintenace during DLP	1 day	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	$1,860.00
924		**Generating System**	**43 days**	**Tue 02-03-21**	**Thu 29-04-21**	**Tue 02-03-21**	**Thu 29-04-21**	**$74,400.00**
925		To Supply 25KVA 50Hz 415V Sound Proof All Weather 3 Phase Generator Set	7 days	Thu 01-04-21	Fri 09-04-21	Thu 01-04-21	Fri 09-04-21	$37,200.00
926		Built In AMF Control Board Panel	3 days	Mon 12-04-21	Wed 14-04-21	Mon 12-04-21	Wed 14-04-21	$23,250.00

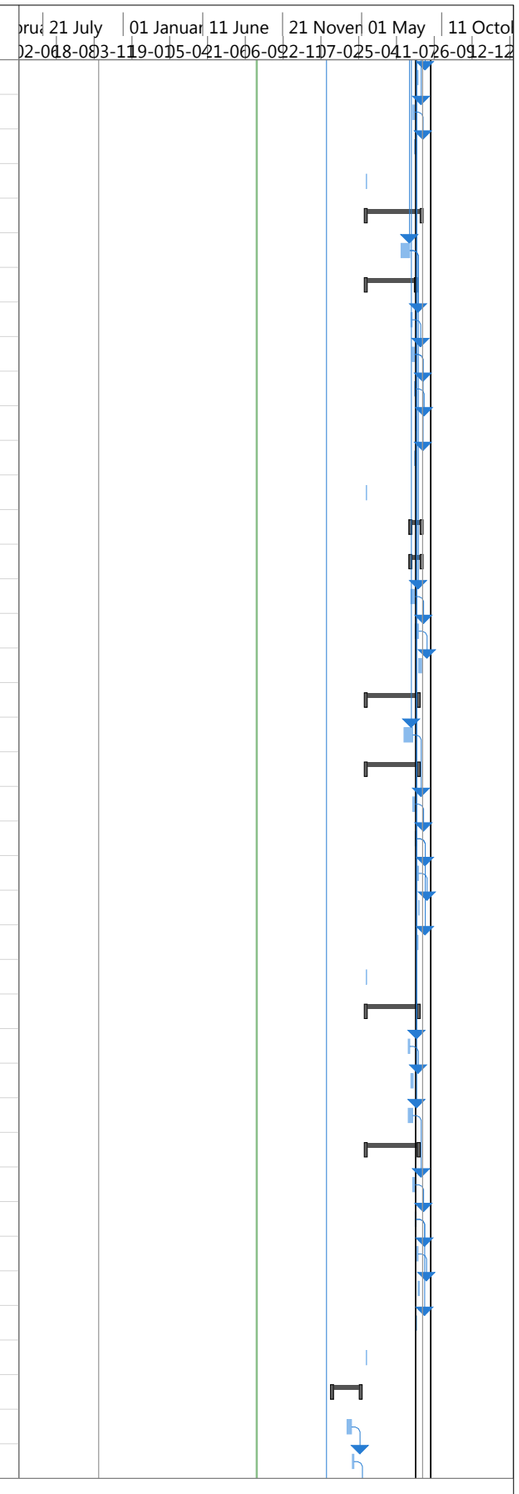

Project: Project1
Date: Tue 29-09-20

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
927		Electrical Submain Cabling From AMF to Generator	3 days	Thu 15-04-21	Mon 19-04-21	Thu 15-04-21	Mon 19-04-21	$1,860.00
928		Factory Testing for Genset	1 day	Tue 02-03-21	Tue 02-03-21	Tue 02-03-21	Tue 02-03-21	$9,300.00
929		Submission For Authority Approval	1 day	Wed 10-03-21	Wed 10-03-21	Wed 10-03-21	Wed 10-03-21	$930.00
930		MCCB Box at Ruang Jentera	7 days	Tue 20-04-21	Wed 28-04-21	Tue 20-04-21	Wed 28-04-21	$930.00
931		Testing & Commissioning	1 day	Thu 29-04-21	Thu 29-04-21	Thu 29-04-21	Thu 29-04-21	$930.00
932		**Electrical Services for Main Equipments and External Works**	**55 days**	**Thu 18-02-21**	**Wed 05-05-21**	**Thu 18-02-21**	**Wed 05-05-21**	**$248,728.50**
933		**Electrical Main Equipments and Infra Works**	**55 days**	**Thu 18-02-21**	**Wed 05-05-21**	**Thu 18-02-21**	**Wed 05-05-21**	**$248,728.50**
934		Electrical Main Switch and Submain Cable	25 days	Thu 18-02-21	Wed 24-03-21	Thu 18-02-21	Wed 24-03-21	$130,200.00
935		External Lighting and Cabling Works	25 days	Thu 01-04-21	Wed 05-05-21	Thu 01-04-21	Wed 05-05-21	$118,528.50
936		**Telephone Service For Main Equipment and External Works**	**51 days**	**Mon 01-03-21**	**Mon 10-05-21**	**Mon 01-03-21**	**Mon 10-05-21**	**$93,000.00**
937		External Telephone and Infra Works	30 days	Mon 01-03-21	Fri 09-04-21	Mon 01-03-21	Fri 09-04-21	$83,700.00
938		**Other Works**	**21 days**	**Mon 12-04-21**	**Mon 10-05-21**	**Mon 12-04-21**	**Mon 10-05-21**	**$9,300.00**
939		Galvanized Trunking/Cable Tray	3 days	Mon 12-04-21	Wed 14-04-21	Mon 12-04-21	Wed 14-04-21	$2,790.00
940		Fire Barrier Material Through Riser Room	2 days	Thu 15-04-21	Fri 16-04-21	Thu 15-04-21	Fri 16-04-21	$930.00
941		Pre Testing	1 day	Mon 19-04-21	Mon 19-04-21	Mon 19-04-21	Mon 19-04-21	$1,860.00
942		Testing & Commissioning	2 days	Tue 20-04-21	Wed 21-04-21	Tue 20-04-21	Wed 21-04-21	$1,395.00
943		Painting and Labelling	2 days	Thu 22-04-21	Fri 23-04-21	Thu 22-04-21	Fri 23-04-21	$930.00
944		Service and Maintenace during DLP	1 day	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	$1,395.00
945		**General Work for Electrical Service**	**10 days**	**Mon 26-04-21**	**Fri 07-05-21**	**Mon 26-04-21**	**Fri 07-05-21**	**$61,101.00**
946		To Provide Switchroom with peripherals, labels and Signages	1 day	Mon 26-04-21	Mon 26-04-21	Mon 26-04-21	Mon 26-04-21	$5,766.00
947		Circuit Numbering System and Schematic Diagram for all DSB and MSB	1 day	Fri 30-04-21	Fri 30-04-21	Fri 30-04-21	Fri 30-04-21	$2,790.00
948		Shop Drawings	1 day	Mon 03-05-21	Mon 03-05-21	Mon 03-05-21	Mon 03-05-21	$4,650.00
949		As-Built Drawings, Catalogue and Operation Manual	1 day	Wed 05-05-21	Wed 05-05-21	Wed 05-05-21	Wed 05-05-21	$4,650.00
950		Liason with Local Authority	1 day	Thu 06-05-21	Thu 06-05-21	Thu 06-05-21	Thu 06-05-21	$1,860.00
951		Practical Training and maintenance of the operators	7 days	Tue 27-04-21	Wed 05-05-21	Tue 27-04-21	Wed 05-05-21	$3,255.00
952		Sample Board, Sample workmanship	1 day	Tue 27-04-21	Tue 27-04-21	Tue 27-04-21	Tue 27-04-21	$930.00
953		Breaking and Hacking and Make Good of Brickwalls, floor, slab and other civil works	1 day	Fri 30-04-21	Fri 30-04-21	Fri 30-04-21	Fri 30-04-21	$4,650.00
954		Allow Compliance to Specifications and Drawings.	1 day	Fri 07-05-21	Fri 07-05-21	Fri 07-05-21	Fri 07-05-21	$32,550.00
955		**WANG PERUNTUKAN SEMENTARA**	**65 days**	**Fri 01-01-21**	**Thu 01-04-21**	**Fri 01-01-21**	**Thu 01-04-21**	**$520,000.00**
956		Contribution to Local & Utility Authority	1 day	Mon 01-03-21	Mon 01-03-21	Mon 01-03-21	Mon 01-03-21	$295,000.00
957		Loose Furniture	1 day	Fri 01-01-21	Fri 01-01-21	Fri 01-01-21	Fri 01-01-21	$75,000.00
958		Lanskap	1 day	Wed 03-03-21	Wed 03-03-21	Wed 03-03-21	Wed 03-03-21	$20,000.00
959		Papan Tanda Bangunan	1 day	Thu 01-04-21	Thu 01-04-21	Thu 01-04-21	Thu 01-04-21	$50,000.00
960		Off Site Work	1 day	Thu 01-04-21	Thu 01-04-21	Thu 01-04-21	Thu 01-04-21	$80,000.00
961		PROJECT FINISH	0 days	Wed 01-09-21	Wed 01-09-21	Wed 01-09-21	Wed 01-09-21	$0.00

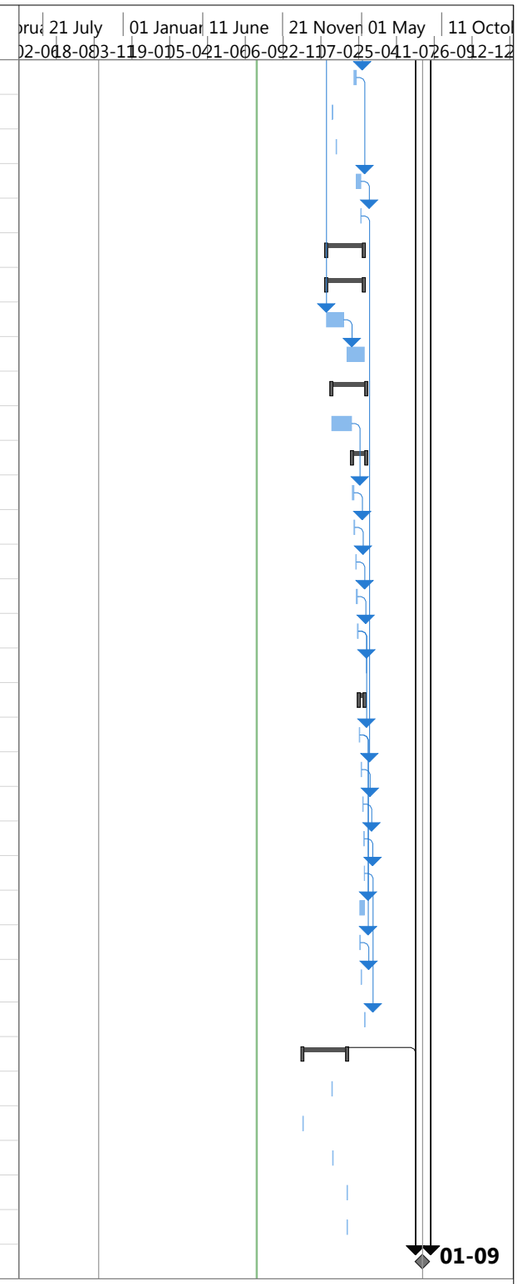

Project: Project1
Date: Tue 29-09-20

Task	Project Summary	Manual Task	Start-only	Deadline			
Split	Inactive Task	Duration-only	Finish-only	Progress			
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress			
Summary	Inactive Summary	Manual Summary	External Milestone				
