
ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
1		**CADANGAN PEMBINAAN PROJEK BALAI BOMBA DAN PENYELAMAT BEAUFORT, SABAH**	**390 days**	**Tue 12-11-19**	**Wed 01-09-21**	**Tue 12-11-19**	**Wed 01-09-21**	**$6,305,978.26**
2		PROJECT START	0 days	Tue 12-11-19	Tue 12-11-19	Tue 12-11-19	Tue 12-11-19	$0.00
3		**PRELIMINARIES**	**308 days**	**Tue 12-11-19**	**Mon 10-05-21**	**Tue 12-11-19**	**Mon 10-05-21**	**$303,180.00**
4		**Provisions In Condition of Contract PWD Form 203 (Rev.1/2010)**	**308 days**	**Tue 12-11-19**	**Mon 10-05-21**	**Tue 12-11-19**	**Mon 10-05-21**	**$303,180.00**
317		**SITE PREPARATION, EARTHWORKS AND ASSOCIATED WORKS**	**309 days**	**Wed 11-12-19**	**Wed 09-06-21**	**Wed 11-12-19**	**Wed 09-06-21**	**$1,817,866.00**
318		Site Clearing	25 days	Wed 11-12-19	Tue 14-01-20	Wed 11-12-19	Tue 14-01-20	$35,812.00
319		Temporary Access Complete with Washbay	7 days	Wed 15-01-20	Thu 23-01-20	Wed 15-01-20	Thu 23-01-20	$14,500.00
320		Earthwork: Cut and Fill to Formation Level	30 days	Fri 24-01-20	Thu 05-03-20	Fri 24-01-20	Thu 05-03-20	$69,750.00
321		Temporary Earth Drain	14 days	Fri 06-03-20	Fri 17-07-20	Fri 06-03-20	Fri 17-07-20	$19,475.00
322		**Geotechnical Work**	**57 days**	**Fri 06-03-20**	**Wed 16-09-20**	**Fri 06-03-20**	**Wed 16-09-20**	**$318,461.00**
323		**PVD & Drainage Blanket**	**26 days**	**Fri 06-03-20**	**Tue 04-08-20**	**Fri 06-03-20**	**Tue 04-08-20**	**$171,061.00**
324		Plant & Equipment	3 days	Fri 06-03-20	Tue 10-03-20	Fri 06-03-20	Tue 10-03-20	$15,000.00
325		Setting out for Prefabricated Vertical Drain	2 days	Wed 11-03-20	Thu 12-03-20	Wed 11-03-20	Thu 12-03-20	$6,241.00
326		Supply and Install Pre-Fabricated Vertical Drain	14 days	Fri 13-03-20	Fri 24-07-20	Fri 13-03-20	Fri 24-07-20	$99,840.00
327		Construction of 500mm Drainage Blanket	7 days	Mon 27-07-20	Tue 04-08-20	Mon 27-07-20	Tue 04-08-20	$49,980.00
328		**Surcharging**	**31 days**	**Wed 05-08-20**	**Wed 16-09-20**	**Wed 05-08-20**	**Wed 16-09-20**	**$147,400.00**
329		Supply , lay, spread and compact of suitable materials as surcharge fill	3 days	Wed 05-08-20	Fri 07-08-20	Wed 05-08-20	Fri 07-08-20	$35,250.00
330		Excavate and remove surcharge materials as directed	14 days	Mon 10-08-20	Thu 27-08-20	Mon 10-08-20	Thu 27-08-20	$21,150.00
331		Supply and lay approved geotextile between drainage blanket and suitable fill	7 days	Fri 28-08-20	Mon 07-09-20	Fri 28-08-20	Mon 07-09-20	$42,000.00
332		Supply and lay approved geotextile between drainage blanket and surcharge fill	7 days	Tue 08-09-20	Wed 16-09-20	Tue 08-09-20	Wed 16-09-20	$49,000.00
333		**Marching Field & Roadworks**	**190 days**	**Thu 17-09-20**	**Wed 09-06-21**	**Thu 17-09-20**	**Wed 09-06-21**	**$617,514.00**
334		Preparation of Subgrade Layer	39 days	Thu 17-09-20	Tue 10-11-20	Thu 17-09-20	Tue 10-11-20	$30,064.00
335		Contruction/Laying of Road Base	40 days	Wed 11-11-20	Tue 05-01-21	Wed 11-11-20	Tue 05-01-21	$222,040.00
336		Installation of Road Kerb	30 days	Wed 06-01-21	Tue 16-02-21	Wed 06-01-21	Tue 16-02-21	$24,270.00
337		Testing; FDT, CBR, MDT	7 days	Wed 17-02-21	Thu 25-02-21	Wed 17-02-21	Thu 25-02-21	$2,500.00
338		Asphalt Finishes Layer	30 days	Fri 26-02-21	Thu 08-04-21	Fri 26-02-21	Thu 08-04-21	$307,440.00
339		Road Marking	30 days	Fri 09-04-21	Thu 20-05-21	Fri 09-04-21	Thu 20-05-21	$29,400.00
340		Road Signboard	14 days	Fri 21-05-21	Wed 09-06-21	Fri 21-05-21	Wed 09-06-21	$1,800.00
341		**Sistem Saliran Permukaan**	**160 days**	**Thu 17-09-20**	**Wed 28-04-21**	**Thu 17-09-20**	**Wed 28-04-21**	**$330,280.00**
342		Reinforced Concrete Drain	60 days	Thu 17-09-20	Wed 09-12-20	Thu 17-09-20	Wed 09-12-20	$198,620.00
343		Culvert Construction	30 days	Thu 10-12-20	Wed 20-01-21	Thu 10-12-20	Wed 20-01-21	$95,000.00
344		Sump	30 days	Thu 21-01-21	Wed 03-03-21	Thu 21-01-21	Wed 03-03-21	$16,500.00
345		MS Grating for Sump and Grating	20 days	Thu 04-03-21	Wed 31-03-21	Thu 04-03-21	Wed 31-03-21	$16,660.00
346		Work to Existing Drain	20 days	Thu 01-04-21	Wed 28-04-21	Thu 01-04-21	Wed 28-04-21	$3,500.00
347		**Sistem Retikulasi Air**	**116 days**	**Thu 10-12-20**	**Thu 20-05-21**	**Thu 10-12-20**	**Thu 20-05-21**	**$75,177.00**
348		Excavation and Laying of 150mm MSSL Pipes including bedding and surrounding	39 days	Thu 10-12-20	Tue 02-02-21	Thu 10-12-20	Tue 02-02-21	$30,488.00
349		Pillar Hydrant & Bulk Meter	20 days	Wed 03-02-21	Tue 02-03-21	Wed 03-02-21	Tue 02-03-21	$7,500.00
350		Valve Chambers including Accessories and Equipment	20 days	Wed 03-03-21	Tue 30-03-21	Wed 03-03-21	Tue 30-03-21	$3,750.00
351		Balancing Tank	30 days	Wed 31-03-21	Tue 11-05-21	Wed 31-03-21	Tue 11-05-21	$22,500.00

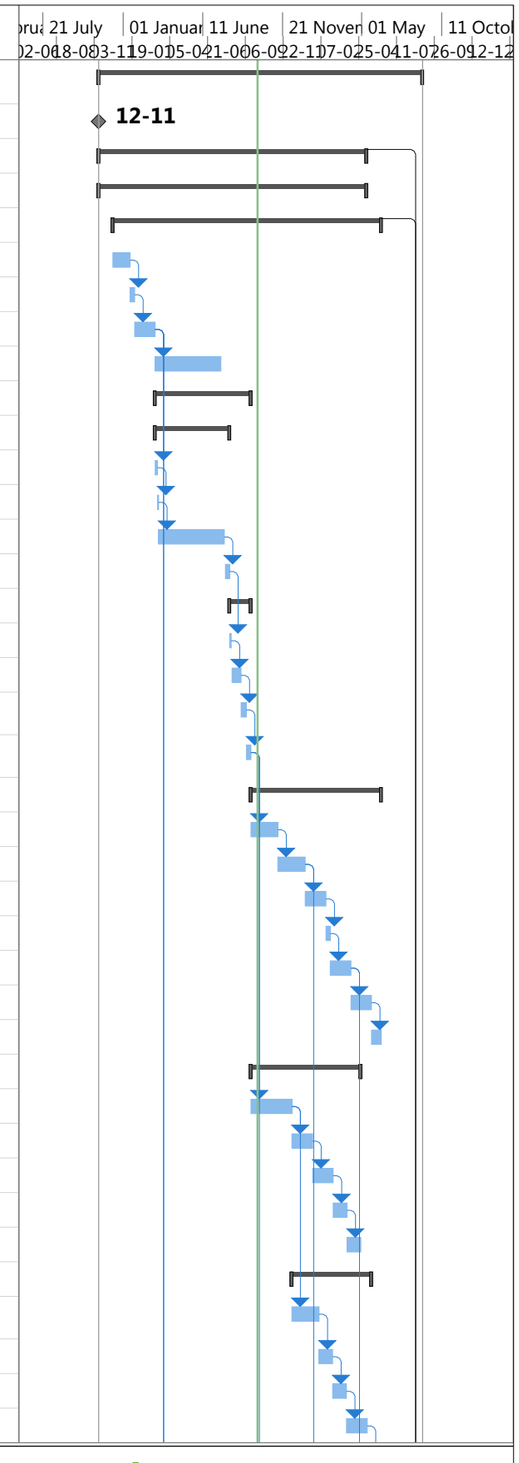

Project: Project1
Date: Thu 01-10-20


Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone

Disediakan oleh :

Disahkan oleh :

Disemak oleh :

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
352		Tightness Test, Flushing and Dissenfecting Test	7 days	Wed 12-05-21	Thu 20-05-21	Wed 12-05-21	Thu 20-05-21	$10,939.00
353		**Sistem Saliran Kumbahan**	**137 days**	**Thu 17-09-20**	**Fri 26-03-21**	**Thu 17-09-20**	**Fri 26-03-21**	**$50,760.00**
354		Excavation of Pipe Trenches, Laying of Bedding and Laying of 150mm UPVC Pipe, jointingand other accessories.	60 days	Thu 17-09-20	Wed 09-12-20	Thu 17-09-20	Wed 09-12-20	$13,160.00
355		Construction of Manholes	40 days	Thu 10-12-20	Wed 03-02-21	Thu 10-12-20	Wed 03-02-21	$7,600.00
356		Construction of Septic Tank	30 days	Thu 04-02-21	Wed 17-03-21	Thu 04-02-21	Wed 17-03-21	$25,000.00
357		Testing	7 days	Thu 18-03-21	Fri 26-03-21	Thu 18-03-21	Fri 26-03-21	$5,000.00
358		**Fencing, Decorative Fencing and Gates**	**107 days**	**Wed 06-01-21**	**Thu 03-06-21**	**Wed 06-01-21**	**Thu 03-06-21**	**$286,137.00**
359		Construction of Sliding and Double Swing Gate including RC Colums	13 days	Wed 06-01-21	Fri 22-01-21	Wed 06-01-21	Fri 22-01-21	$30,500.00
360		Boundary Fencing	60 days	Mon 25-01-21	Fri 16-04-21	Mon 25-01-21	Fri 16-04-21	$158,406.00
361		**Flag Pole**	**14 days**	**Mon 19-04-21**	**Thu 06-05-21**	**Mon 19-04-21**	**Thu 06-05-21**	**$18,600.00**
362		Flag Pole	14 days	Mon 19-04-21	Thu 06-05-21	Mon 19-04-21	Thu 06-05-21	$18,600.00
363		**Kolah Air**	**14 days**	**Fri 07-05-21**	**Wed 26-05-21**	**Fri 07-05-21**	**Wed 26-05-21**	**$17,607.00**
364		Kolah Air	14 days	Fri 07-05-21	Wed 26-05-21	Fri 07-05-21	Wed 26-05-21	$17,607.00
365		**Turfing**	**40 days**	**Fri 09-04-21**	**Thu 03-06-21**	**Fri 09-04-21**	**Thu 03-06-21**	**$61,024.00**
366		Turfing Work	40 days	Fri 09-04-21	Thu 03-06-21	Fri 09-04-21	Thu 03-06-21	$61,024.00
367		**PILING WORKS**	**113 days**	**Fri 20-12-19**	**Thu 17-09-20**	**Fri 20-12-19**	**Thu 17-09-20**	**$141,905.91**
368		Submission of Pile Catalogue, Plant, Equipment and Pile Set Criteria	1 day	Fri 20-12-19	Fri 20-12-19	Fri 20-12-19	Fri 20-12-19	$0.00
369		Mobilization of Plant & Equipment	3 days	Fri 06-03-20	Tue 10-03-20	Fri 06-03-20	Tue 10-03-20	$23,250.00
370		Initial Pile Driving for MLT	1 day	Wed 11-03-20	Wed 11-03-20	Wed 11-03-20	Wed 11-03-20	$0.00
371		MLT Pile Testing (1 Nos)	7 days	Thu 12-03-20	Tue 14-07-20	Thu 12-03-20	Tue 14-07-20	$18,600.00
372		Submission of Pile Testing Report	2 days	Wed 15-07-20	Thu 16-07-20	Wed 15-07-20	Thu 16-07-20	$0.00
373		**Supply and Delivery of Piles**	**8 days**	**Fri 17-07-20**	**Tue 28-07-20**	**Fri 17-07-20**	**Tue 28-07-20**	**$62,058.90**
374		Menara Latihan	2 days	Fri 17-07-20	Mon 20-07-20	Fri 17-07-20	Mon 20-07-20	$19,065.00
375		Entrance Signage	2 days	Tue 21-07-20	Wed 22-07-20	Tue 21-07-20	Wed 22-07-20	$4,361.70
376		Entrance Culvert	2 days	Thu 23-07-20	Fri 24-07-20	Thu 23-07-20	Fri 24-07-20	$18,693.00
377		Drainage	2 days	Mon 27-07-20	Tue 28-07-20	Mon 27-07-20	Tue 28-07-20	$19,939.20
378		**Pile Driving & Jointing**	**37 days**	**Wed 29-07-20**	**Thu 17-09-20**	**Wed 29-07-20**	**Thu 17-09-20**	**$37,997.01**
379		**Menara Latihan (50 Pile Points)**	**12 days**	**Wed 29-07-20**	**Thu 13-08-20**	**Wed 29-07-20**	**Thu 13-08-20**	**$8,742.00**
380		Pile Points Setting Out	1 day	Wed 29-07-20	Wed 29-07-20	Wed 29-07-20	Wed 29-07-20	$0.00
381		Pile Driving& Jointing	5 days	Thu 30-07-20	Wed 05-08-20	Thu 30-07-20	Wed 05-08-20	$7,347.00
382		Excavation of Pile caps	3 days	Thu 06-08-20	Mon 10-08-20	Thu 06-08-20	Mon 10-08-20	$0.00
383		Cut off Pile Head	3 days	Tue 11-08-20	Thu 13-08-20	Tue 11-08-20	Thu 13-08-20	$1,395.00
384		**Entrance Signage (7 Pile Points)**	**12 days**	**Thu 30-07-20**	**Fri 14-08-20**	**Thu 30-07-20**	**Fri 14-08-20**	**$1,647.03**
385		Pile Points Setting Out	1 day	Thu 30-07-20	Thu 30-07-20	Thu 30-07-20	Thu 30-07-20	$0.00
386		Pile Driving& Jointing	3 days	Thu 06-08-20	Mon 10-08-20	Thu 06-08-20	Mon 10-08-20	$1,451.73
387		Excavation of Pile caps	2 days	Tue 11-08-20	Wed 12-08-20	Tue 11-08-20	Wed 12-08-20	$0.00
388		Cut off Pile Head	2 days	Thu 13-08-20	Fri 14-08-20	Thu 13-08-20	Fri 14-08-20	$195.30
389		**Entrance Culvert (30 Pile Points)**	**22 days**	**Fri 31-07-20**	**Mon 31-08-20**	**Fri 31-07-20**	**Mon 31-08-20**	**$7,058.70**
390		Pile Points Setting Out	1 day	Fri 31-07-20	Fri 31-07-20	Fri 31-07-20	Fri 31-07-20	$0.00

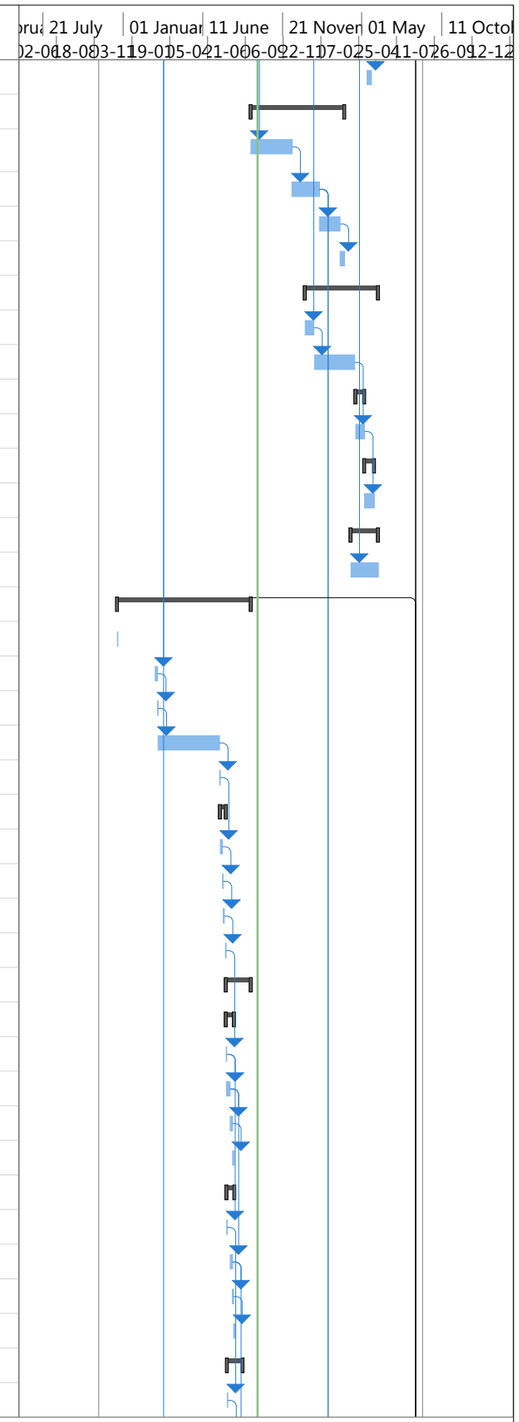

Project: Project1
Date: Thu 01-10-20


Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone

Disediakan oleh :

Disahkan oleh :

Disemak oleh :

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
391		Pile Driving& Jointing	6 days	Tue 11-08-20	Tue 18-08-20	Tue 11-08-20	Tue 18-08-20	$6,221.70
392		Excavation of Pile caps	4 days	Wed 19-08-20	Mon 24-08-20	Wed 19-08-20	Mon 24-08-20	$0.00
393		Cut off Pile Head	5 days	Tue 25-08-20	Mon 31-08-20	Tue 25-08-20	Mon 31-08-20	$837.00
394		**Drainage (32 Pile Points)**	**26 days**	**Mon 03-08-20**	**Mon 07-09-20**	**Mon 03-08-20**	**Mon 07-09-20**	**$7,529.28**
395		Pile Points Setting Out	1 day	Mon 03-08-20	Mon 03-08-20	Mon 03-08-20	Mon 03-08-20	$0.00
396		Pile Driving& Jointing	6 days	Wed 19-08-20	Wed 26-08-20	Wed 19-08-20	Wed 26-08-20	$6,636.48
397		Excavation of Pile caps	4 days	Tue 25-08-20	Fri 28-08-20	Tue 25-08-20	Fri 28-08-20	$0.00
398		Cut off Pile Head	5 days	Tue 01-09-20	Mon 07-09-20	Tue 01-09-20	Mon 07-09-20	$892.80
399		**Piling As Built Drawings**	**8 days**	**Tue 08-09-20**	**Thu 17-09-20**	**Tue 08-09-20**	**Thu 17-09-20**	**$13,020.00**
400		PDA Test (1 No)	1 day	Tue 08-09-20	Tue 08-09-20	Tue 08-09-20	Tue 08-09-20	$1,860.00
401		Preparation and Endorsement of Piling As Built Survey	7 days	Tue 08-09-20	Wed 16-09-20	Tue 08-09-20	Wed 16-09-20	$0.00
402		Submission of Piling Record	3 days	Tue 08-09-20	Thu 10-09-20	Tue 08-09-20	Thu 10-09-20	$1,860.00
403		Submission of piling As Built Survey	1 day	Thu 17-09-20	Thu 17-09-20	Thu 17-09-20	Thu 17-09-20	$9,300.00
404		**BUILDING WORKS**	**307 days**	**Fri 06-03-20**	**Wed 01-09-21**	**Fri 06-03-20**	**Wed 01-09-21**	**$2,045,721.35**
405		**BANGUNAN BALAI BOMBA**	**297 days**	**Fri 06-03-20**	**Wed 18-08-21**	**Fri 06-03-20**	**Wed 18-08-21**	**$1,488,465.70**
406		**Structural Works**	**193 days**	**Fri 06-03-20**	**Thu 25-03-21**	**Fri 06-03-20**	**Thu 25-03-21**	**$718,874.90**
407		**Pad Footings and RC Stump**	**61 days**	**Fri 06-03-20**	**Tue 22-09-20**	**Fri 06-03-20**	**Tue 22-09-20**	**$198,081.60**
408		Building Setting out& Survey	3 days	Fri 06-03-20	Tue 10-03-20	Fri 06-03-20	Tue 10-03-20	$0.00
409		Excavation of Pad Footings	7 days	Wed 11-03-20	Mon 13-07-20	Wed 11-03-20	Mon 13-07-20	$8,076.00
410		Lean Concrete	4 days	Tue 14-07-20	Fri 17-07-20	Tue 14-07-20	Fri 17-07-20	$2,202.00
411		Installation of Formwork to Pad Footings	14 days	Mon 20-07-20	Thu 06-08-20	Mon 20-07-20	Thu 06-08-20	$15,750.00
412		Installation of Reinforcement Bars to Pad Footings & Stumps	10 days	Fri 07-08-20	Thu 20-08-20	Fri 07-08-20	Thu 20-08-20	$54,393.60
413		Concreting Works of Pad Footings	7 days	Fri 21-08-20	Mon 31-08-20	Fri 21-08-20	Mon 31-08-20	$110,334.00
414		Installation of Stumps F/works	5 days	Tue 01-09-20	Mon 07-09-20	Tue 01-09-20	Mon 07-09-20	$3,700.00
415		Concreting Works for Stumps	4 days	Tue 08-09-20	Fri 11-09-20	Tue 08-09-20	Fri 11-09-20	$3,626.00
416		Backfilling& Compaction	7 days	Mon 14-09-20	Tue 22-09-20	Mon 14-09-20	Tue 22-09-20	$0.00
417		**Ground Beam Structures**	**47 days**	**Wed 23-09-20**	**Thu 26-11-20**	**Wed 23-09-20**	**Thu 26-11-20**	**$99,444.00**
418		Excavation of Ground Beam	4 days	Wed 23-09-20	Mon 28-09-20	Wed 23-09-20	Mon 28-09-20	$696.00
419		Lean Concrete	7 days	Tue 29-09-20	Wed 07-10-20	Tue 29-09-20	Wed 07-10-20	$672.00
420		Installation of Ground Beam F/works	14 days	Thu 08-10-20	Tue 27-10-20	Thu 08-10-20	Tue 27-10-20	$20,950.00
421		Installation of Ground Beam Rebars	10 days	Wed 28-10-20	Tue 10-11-20	Wed 28-10-20	Tue 10-11-20	$51,744.00
422		Concreting Works for Ground Beams	7 days	Wed 11-11-20	Thu 19-11-20	Wed 11-11-20	Thu 19-11-20	$25,382.00
423		Backfilling and Compaction	5 days	Fri 20-11-20	Thu 26-11-20	Fri 20-11-20	Thu 26-11-20	$0.00
424		**Ground Slab**	**18 days**	**Fri 27-11-20**	**Tue 22-12-20**	**Fri 27-11-20**	**Tue 22-12-20**	**$82,635.70**
425		Excavation of Ground Slab	2 days	Fri 27-11-20	Mon 30-11-20	Fri 27-11-20	Mon 30-11-20	$864.00
426		Anti Termite Treatment	2 days	Tue 01-12-20	Wed 02-12-20	Tue 01-12-20	Wed 02-12-20	$2,980.00
427		Installation of F/works	3 days	Thu 03-12-20	Mon 07-12-20	Thu 03-12-20	Mon 07-12-20	$1,552.00
428		Damp Proof Membrane	2 days	Tue 08-12-20	Wed 09-12-20	Tue 08-12-20	Wed 09-12-20	$3,105.00
429		Lean Concrete	1 day	Thu 10-12-20	Thu 10-12-20	Thu 10-12-20	Thu 10-12-20	$2,454.70
430		Installation of Re-bars	5 days	Fri 11-12-20	Thu 17-12-20	Fri 11-12-20	Thu 17-12-20	$29,204.00

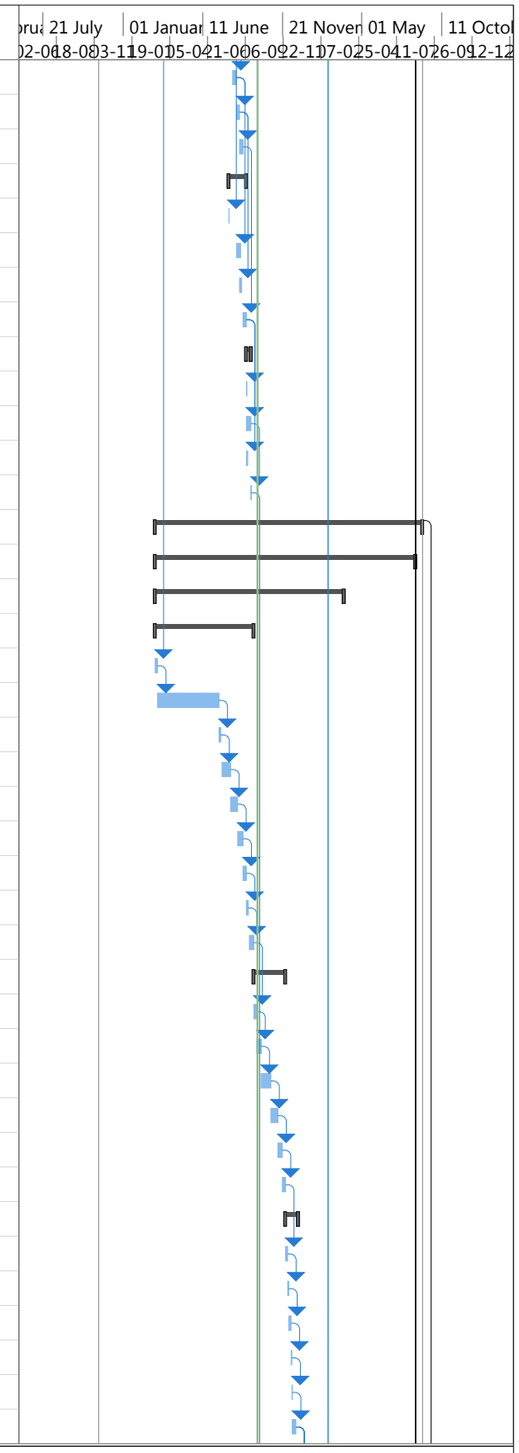

Project: Project1
Date: Thu 01-10-20


Task	Project Summary	Manual Task	Start-only	Deadline	
Split	Inactive Task	Duration-only	Finish-only	Progress	
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress	
Summary	Inactive Summary	Manual Summary	External Milestone		

Disediakan oleh :

Disahkan oleh :

Disemak oleh :

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
431		Concreting of Ground Slab	3 days	Fri 18-12-20	Tue 22-12-20	Fri 18-12-20	Tue 22-12-20	$42,476.00
432		**Apron Slab**	**13 days**	**Wed 23-12-20**	**Fri 08-01-21**	**Wed 23-12-20**	**Fri 08-01-21**	**$6,791.00**
433		Excavation for Apron Slab	3 days	Wed 23-12-20	Fri 25-12-20	Wed 23-12-20	Fri 25-12-20	$104.00
434		Installation of F/works	3 days	Mon 28-12-20	Wed 30-12-20	Mon 28-12-20	Wed 30-12-20	$0.00
435		Lean Concrete	2 days	Thu 31-12-20	Fri 01-01-21	Thu 31-12-20	Fri 01-01-21	$450.00
436		Installation of Re-bars	3 days	Mon 04-01-21	Wed 06-01-21	Mon 04-01-21	Wed 06-01-21	$1,575.00
437		Concreting of Apron Slab	2 days	Thu 07-01-21	Fri 08-01-21	Thu 07-01-21	Fri 08-01-21	$4,662.00
438		**Ramp Slab**	**6 days**	**Mon 11-01-21**	**Mon 18-01-21**	**Mon 11-01-21**	**Mon 18-01-21**	**$3,968.00**
439		Installation of F/works	3 days	Mon 11-01-21	Wed 13-01-21	Mon 11-01-21	Wed 13-01-21	$50.00
440		Installation of Re-bars	2 days	Thu 14-01-21	Fri 15-01-21	Thu 14-01-21	Fri 15-01-21	$546.00
441		Concreting of Ramp Slab	1 day	Mon 18-01-21	Mon 18-01-21	Mon 18-01-21	Mon 18-01-21	$3,372.00
442		**Ground Floor - 1st Floor Columns**	**13 days**	**Wed 23-12-20**	**Fri 08-01-21**	**Wed 23-12-20**	**Fri 08-01-21**	**$53,756.20**
443		Installation of Formworks	5 days	Wed 23-12-20	Tue 29-12-20	Wed 23-12-20	Tue 29-12-20	$14,850.00
444		Installation of Reinforcement Bars	5 days	Wed 30-12-20	Tue 05-01-21	Wed 30-12-20	Tue 05-01-21	$23,107.20
445		Concreting Works	3 days	Wed 06-01-21	Fri 08-01-21	Wed 06-01-21	Fri 08-01-21	$15,799.00
446		**1st Floor Beam & Slab**	**22 days**	**Mon 11-01-21**	**Tue 09-02-21**	**Mon 11-01-21**	**Tue 09-02-21**	**$84,145.00**
447		Installation of F/works for Beam & Slab	10 days	Mon 11-01-21	Fri 22-01-21	Mon 11-01-21	Fri 22-01-21	$17,708.00
448		Installation of Rebars for Beam & Slab	7 days	Mon 25-01-21	Tue 02-02-21	Mon 25-01-21	Tue 02-02-21	$18,781.00
449		Concreting Works for Beam & Slab	5 days	Wed 03-02-21	Tue 09-02-21	Wed 03-02-21	Tue 09-02-21	$47,656.00
450		**RC Staircase**	**32 days**	**Wed 10-02-21**	**Thu 25-03-21**	**Wed 10-02-21**	**Thu 25-03-21**	**$21,551.60**
451		Installation of F/works	5 days	Wed 10-02-21	Tue 16-02-21	Wed 10-02-21	Tue 16-02-21	$3,063.00
452		Instalation of Rebars	5 days	Wed 17-02-21	Tue 23-02-21	Wed 17-02-21	Tue 23-02-21	$3,302.40
453		Concreting Works	2 days	Wed 24-02-21	Thu 25-02-21	Wed 24-02-21	Thu 25-02-21	$4,092.20
454		Staircase Finishing Work including Railling work	20 days	Fri 26-02-21	Thu 25-03-21	Fri 26-02-21	Thu 25-03-21	$11,094.00
455		**1st Floor to Roof Beam Columns**	**13 days**	**Wed 10-02-21**	**Fri 26-02-21**	**Wed 10-02-21**	**Fri 26-02-21**	**$53,756.20**
456		Installation of Formworks	5 days	Wed 10-02-21	Tue 16-02-21	Wed 10-02-21	Tue 16-02-21	$14,850.00
457		Installation of Rebars	5 days	Wed 17-02-21	Tue 23-02-21	Wed 17-02-21	Tue 23-02-21	$23,107.20
458		Concreting Works	3 days	Wed 24-02-21	Fri 26-02-21	Wed 24-02-21	Fri 26-02-21	$15,799.00
459		**RC Roof Beams, RC Flat Roof and Hoods**	**18 days**	**Mon 01-03-21**	**Wed 24-03-21**	**Mon 01-03-21**	**Wed 24-03-21**	**$114,745.60**
460		Installation of F/works	7 days	Mon 01-03-21	Tue 09-03-21	Mon 01-03-21	Tue 09-03-21	$31,700.00
461		Installation of Rebars	7 days	Wed 10-03-21	Thu 18-03-21	Wed 10-03-21	Thu 18-03-21	$40,569.60
462		Concreting Works	4 days	Fri 19-03-21	Wed 24-03-21	Fri 19-03-21	Wed 24-03-21	$42,476.00
463		**Installation of Roofing System**	**27 days**	**Thu 25-03-21**	**Fri 30-04-21**	**Thu 25-03-21**	**Fri 30-04-21**	**$153,530.00**
464		Installation of Roof Trusses, Rafters, Battens, Purlins and all necessary Structural Items	10 days	Thu 25-03-21	Wed 07-04-21	Thu 25-03-21	Wed 07-04-21	$63,200.00
465		Intallation of Roof Covering; including Aluminium Foil Insulation, Chicken Wire Mesh, Facia Board, Gutter and other necessary finishes.	10 days	Thu 08-04-21	Wed 21-04-21	Thu 08-04-21	Wed 21-04-21	$85,370.00
466		Rainwater Downpipes (RWDP)	7 days	Thu 22-04-21	Fri 30-04-21	Thu 22-04-21	Fri 30-04-21	$4,960.00
467		**Architectural Works**	**105 days**	**Thu 25-03-21**	**Wed 18-08-21**	**Thu 25-03-21**	**Wed 18-08-21**	**$616,060.80**
468		**External Wall**	**22 days**	**Thu 25-03-21**	**Fri 23-04-21**	**Thu 25-03-21**	**Fri 23-04-21**	**$57,569.20**
469		Stiffeners	7 days	Thu 25-03-21	Fri 02-04-21	Thu 25-03-21	Fri 02-04-21	$7,179.20

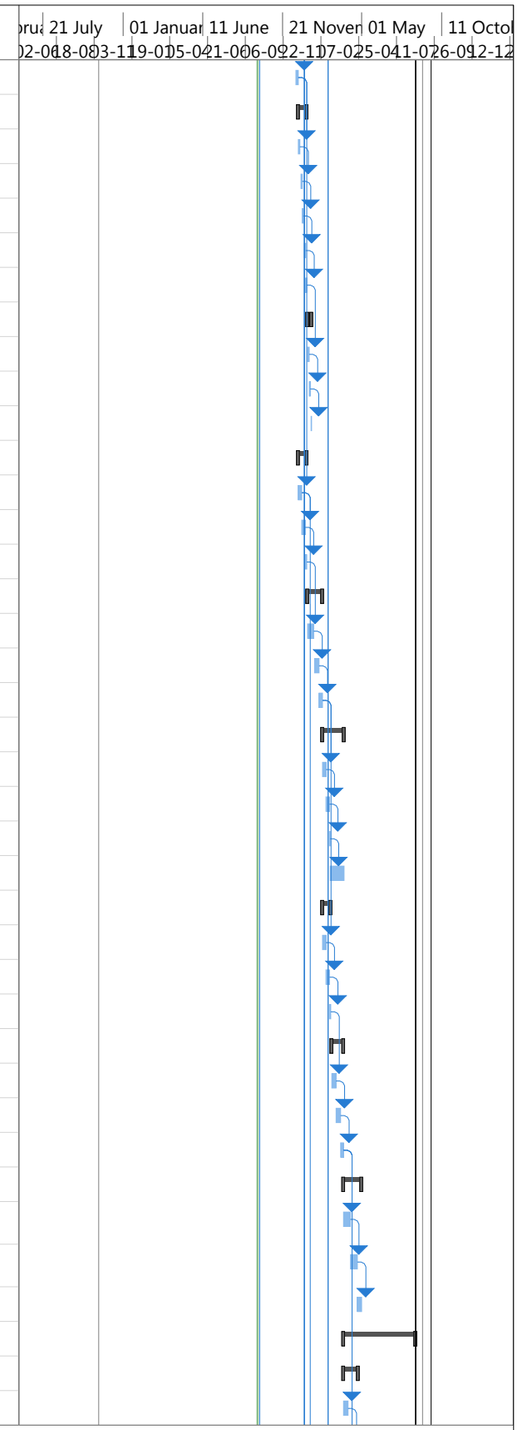

Project: Project1
Date: Thu 01-10-20


Task	Project Summary	Manual Task	Start-only	Deadline	
Split	Inactive Task	Duration-only	Finish-only	Progress	
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress	
Summary	Inactive Summary	Manual Summary	External Milestone		

Disediakan oleh :

Disahkan oleh :

Disemak oleh :

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
470		External Wall (1 Brick, Half Brick Including Parapet Wall including all sundries)	15 days	Mon 05-04-21	Fri 23-04-21	Mon 05-04-21	Fri 23-04-21	$50,390.00
471		**External Doors & Windows**	**31 days**	**Mon 26-04-21**	**Mon 07-06-21**	**Mon 26-04-21**	**Mon 07-06-21**	**$60,716.00**
472		**External Doors**	**28 days**	**Mon 26-04-21**	**Wed 02-06-21**	**Mon 26-04-21**	**Wed 02-06-21**	**$11,731.00**
473		Lintols	3 days	Mon 26-04-21	Wed 28-04-21	Mon 26-04-21	Wed 28-04-21	$260.00
474		Door Frames	7 days	Thu 29-04-21	Fri 07-05-21	Thu 29-04-21	Fri 07-05-21	$550.00
475		Door Panels	7 days	Mon 10-05-21	Tue 18-05-21	Mon 10-05-21	Tue 18-05-21	$1,920.00
476		Ironmongeries including Door Finishes	5 days	Wed 19-05-21	Tue 25-05-21	Wed 19-05-21	Tue 25-05-21	$3,823.00
477		Automatic Roller Shutter	4 days	Wed 26-05-21	Mon 31-05-21	Wed 26-05-21	Mon 31-05-21	$4,300.00
478		Aluminium Sliding Doors & Gate	2 days	Tue 01-06-21	Wed 02-06-21	Tue 01-06-21	Wed 02-06-21	$878.00
479		**External Windows**	**28 days**	**Thu 29-04-21**	**Mon 07-06-21**	**Thu 29-04-21**	**Mon 07-06-21**	**$48,985.00**
480		Lintols	7 days	Thu 29-04-21	Fri 07-05-21	Thu 29-04-21	Fri 07-05-21	$2,420.00
481		Intallation of Aluminium Window Frames and Panels	21 days	Mon 10-05-21	Mon 07-06-21	Mon 10-05-21	Mon 07-06-21	$46,565.00
482		**Internal Walls& Partition**	**40 days**	**Thu 25-03-21**	**Wed 19-05-21**	**Thu 25-03-21**	**Wed 19-05-21**	**$75,057.00**
483		Installation of Brickwall (1Brick & Half Brick including Mild Steel Railing, Toilet Cubicle System c/w Sundries)	40 days	Thu 25-03-21	Wed 19-05-21	Thu 25-03-21	Wed 19-05-21	$75,057.00
484		**Internal Doors & Windows**	**29 days**	**Thu 20-05-21**	**Tue 29-06-21**	**Thu 20-05-21**	**Tue 29-06-21**	**$48,794.00**
485		**Internal Doors**	**29 days**	**Thu 20-05-21**	**Tue 29-06-21**	**Thu 20-05-21**	**Tue 29-06-21**	**$40,560.00**
486		Lintols and Heelstone	5 days	Thu 20-05-21	Wed 26-05-21	Thu 20-05-21	Wed 26-05-21	$880.00
487		Door Frames	7 days	Thu 27-05-21	Fri 04-06-21	Thu 27-05-21	Fri 04-06-21	$3,960.00
488		Door Panels	7 days	Mon 07-06-21	Tue 15-06-21	Mon 07-06-21	Tue 15-06-21	$18,700.00
489		Ironmongeries including Door Finishes	10 days	Wed 16-06-21	Tue 29-06-21	Wed 16-06-21	Tue 29-06-21	$17,020.00
490		**Internal Windows**	**12 days**	**Thu 20-05-21**	**Fri 04-06-21**	**Thu 20-05-21**	**Fri 04-06-21**	**$8,234.00**
491		Lintols	5 days	Thu 20-05-21	Wed 26-05-21	Thu 20-05-21	Wed 26-05-21	$560.00
492		Installation of Window Frames and Panels	7 days	Thu 27-05-21	Fri 04-06-21	Thu 27-05-21	Fri 04-06-21	$7,674.00
493		**Internal Wall Finishes**	**24 days**	**Thu 20-05-21**	**Tue 22-06-21**	**Thu 20-05-21**	**Tue 22-06-21**	**$59,045.00**
494		Plastering of Walls & Columns	14 days	Thu 20-05-21	Tue 08-06-21	Thu 20-05-21	Tue 08-06-21	$24,272.00
495		Wall Tiles	3 days	Wed 09-06-21	Fri 11-06-21	Wed 09-06-21	Fri 11-06-21	$9,825.00
496		Internal Wall Painting Finishes	7 days	Mon 14-06-21	Tue 22-06-21	Mon 14-06-21	Tue 22-06-21	$24,948.00
497		**Internal Floor Finishes**	**22 days**	**Wed 09-06-21**	**Thu 08-07-21**	**Wed 09-06-21**	**Thu 08-07-21**	**$103,024.00**
498		Cement Screed	7 days	Wed 09-06-21	Thu 17-06-21	Wed 09-06-21	Thu 17-06-21	$33,912.00
499		Waterproofing	2 days	Fri 18-06-21	Mon 21-06-21	Fri 18-06-21	Mon 21-06-21	$3,803.00
500		Floor Tiles Finishes including skirting	7 days	Tue 22-06-21	Wed 30-06-21	Tue 22-06-21	Wed 30-06-21	$41,169.00
501		Carpet Tiles including skirting	7 days	Tue 22-06-21	Wed 30-06-21	Tue 22-06-21	Wed 30-06-21	$11,325.00
502		Epoxy Floring	3 days	Thu 01-07-21	Mon 05-07-21	Thu 01-07-21	Mon 05-07-21	$10,725.00
503		Artificial Turfing	1 day	Tue 06-07-21	Tue 06-07-21	Tue 06-07-21	Tue 06-07-21	$1,890.00
504		PreCast Concrete Drain Cover	3 days	Tue 06-07-21	Thu 08-07-21	Tue 06-07-21	Thu 08-07-21	$200.00
505		**Internal Ceiling Finishes**	**19 days**	**Wed 23-06-21**	**Mon 19-07-21**	**Wed 23-06-21**	**Mon 19-07-21**	**$71,838.00**
506		Installation of Aluminium Strip Including all Fittings	7 days	Wed 23-06-21	Thu 01-07-21	Wed 23-06-21	Thu 01-07-21	$29,250.00
507		Installation of Ceiling Board	7 days	Fri 02-07-21	Mon 12-07-21	Fri 02-07-21	Mon 12-07-21	$35,490.00
508		Painting of Intrenal Ceiling	5 days	Tue 13-07-21	Mon 19-07-21	Tue 13-07-21	Mon 19-07-21	$7,098.00

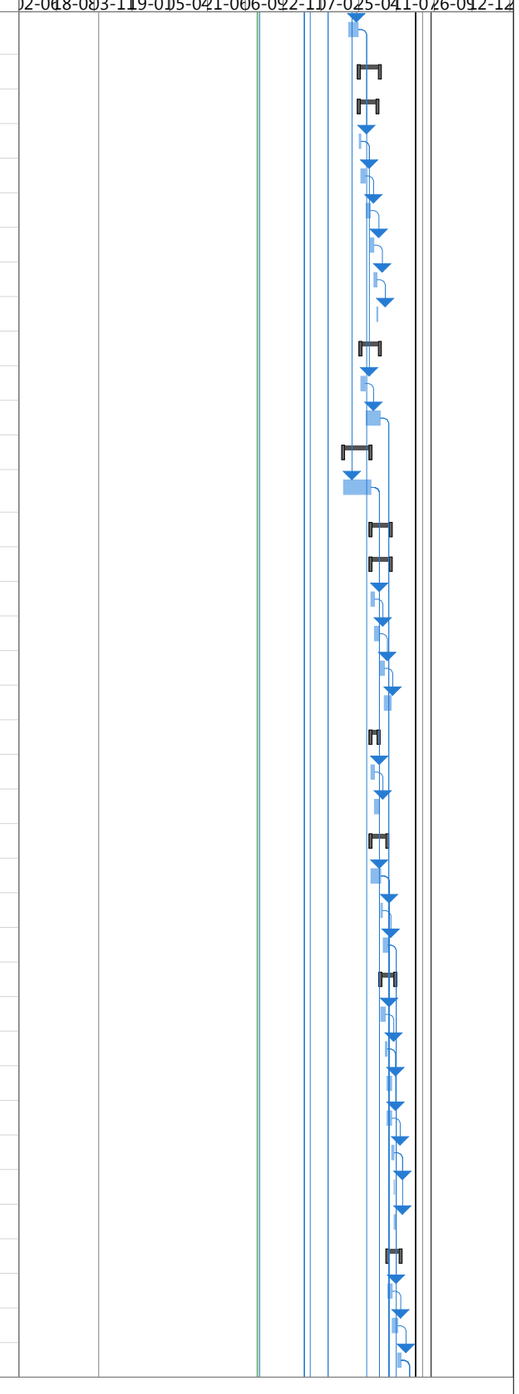

Project: Project1
Date: Thu 01-10-20


Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	

Disediakan oleh :

Disahkan oleh :

Disemak oleh :

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
509		**External Finishes**	**34 days**	**Tue 08-06-21**	**Fri 23-07-21**	**Tue 08-06-21**	**Fri 23-07-21**	**$116,882.00**
510		**External Wall**	**20 days**	**Tue 08-06-21**	**Mon 05-07-21**	**Tue 08-06-21**	**Mon 05-07-21**	**$71,140.00**
511		External Plastering to Wall, Columns, Hoods, Beam & Cavity Wall	10 days	Tue 08-06-21	Mon 21-06-21	Tue 08-06-21	Mon 21-06-21	$25,828.00
512		Waterproofong at Top of Hood	5 days	Tue 08-06-21	Mon 14-06-21	Tue 08-06-21	Mon 14-06-21	$21,930.00
513		External Wall Painting Finishes	10 days	Tue 22-06-21	Mon 05-07-21	Tue 22-06-21	Mon 05-07-21	$23,382.00
514		**External Floor Finishes**	**9 days**	**Tue 06-07-21**	**Fri 16-07-21**	**Tue 06-07-21**	**Fri 16-07-21**	**$7,792.00**
515		Cement Screed Finishes	5 days	Tue 06-07-21	Mon 12-07-21	Tue 06-07-21	Mon 12-07-21	$2,748.00
516		External Floor Tiling Finishes	4 days	Tue 13-07-21	Fri 16-07-21	Tue 13-07-21	Fri 16-07-21	$5,044.00
517		**External Ceiling Finishes**	**14 days**	**Tue 06-07-21**	**Fri 23-07-21**	**Tue 06-07-21**	**Fri 23-07-21**	**$37,950.00**
518		Installation of External Ceiling Finishes	14 days	Tue 06-07-21	Fri 23-07-21	Tue 06-07-21	Fri 23-07-21	$37,950.00
519		**Installation of Sanitary Appliances**	**15 days**	**Tue 20-07-21**	**Mon 09-08-21**	**Tue 20-07-21**	**Mon 09-08-21**	**$12,900.00**
520		WC, Cistern, Shower, Taps, Stop Cock, Wash Basins, Sink, Bidet, Handicap Rail, All Accessories and Testing Required	15 days	Tue 20-07-21	Mon 09-08-21	Tue 20-07-21	Mon 09-08-21	$12,900.00
521		**Other Builder's Work**	**22 days**	**Tue 20-07-21**	**Wed 18-08-21**	**Tue 20-07-21**	**Wed 18-08-21**	**$10,235.60**
522		Mass concrete at WC Base	7 days	Tue 20-07-21	Wed 28-07-21	Tue 20-07-21	Wed 28-07-21	$550.00
523		Counter Top & Bench	7 days	Tue 10-08-21	Wed 18-08-21	Tue 10-08-21	Wed 18-08-21	$2,100.00
524		Sliding Pole	7 days	Tue 10-08-21	Wed 18-08-21	Tue 10-08-21	Wed 18-08-21	$7,585.60
525		**MENARA LATIHAN**	**249 days**	**Fri 18-09-20**	**Wed 01-09-21**	**Fri 18-09-20**	**Wed 01-09-21**	**$362,700.00**
526		**Structural Works**	**240 days**	**Fri 18-09-20**	**Thu 19-08-21**	**Fri 18-09-20**	**Thu 19-08-21**	**$245,247.00**
527		**Pile Caps and RC Stump**	**27 days**	**Fri 18-09-20**	**Mon 26-10-20**	**Fri 18-09-20**	**Mon 26-10-20**	**$15,502.34**
528		Excavation of Pile Caps	7 days	Fri 18-09-20	Mon 28-09-20	Fri 18-09-20	Mon 28-09-20	$252.00
529		Lean Concrete	4 days	Tue 29-09-20	Fri 02-10-20	Tue 29-09-20	Fri 02-10-20	$78.00
530		Installation of Formwork	5 days	Mon 05-10-20	Fri 09-10-20	Mon 05-10-20	Fri 09-10-20	$1,950.00
531		Installation of Rebars for Pile Caps and Stump	5 days	Mon 12-10-20	Fri 16-10-20	Mon 12-10-20	Fri 16-10-20	$4,852.34
532		Concreting Works of Pile Caps	2 days	Mon 19-10-20	Tue 20-10-20	Mon 19-10-20	Tue 20-10-20	$6,734.00
533		Installation of Stumps F/work	2 days	Wed 21-10-20	Thu 22-10-20	Wed 21-10-20	Thu 22-10-20	$600.00
534		Concreting Works for Stumps	1 day	Fri 23-10-20	Fri 23-10-20	Fri 23-10-20	Fri 23-10-20	$1,036.00
535		Backfilling& Compaction	1 day	Mon 26-10-20	Mon 26-10-20	Mon 26-10-20	Mon 26-10-20	$0.00
536		**Ground Beam Structures**	**17 days**	**Tue 27-10-20**	**Wed 18-11-20**	**Tue 27-10-20**	**Wed 18-11-20**	**$11,468.00**
537		Excavation of Ground Beam	2 days	Tue 27-10-20	Wed 28-10-20	Tue 27-10-20	Wed 28-10-20	$96.00
538		Lean Concrete	2 days	Thu 29-10-20	Fri 30-10-20	Thu 29-10-20	Fri 30-10-20	$96.00
539		Installation of F/works for Ground Beam	5 days	Mon 02-11-20	Fri 06-11-20	Mon 02-11-20	Fri 06-11-20	$3,450.00
540		Installation of G. Beam Rebars	5 days	Mon 09-11-20	Fri 13-11-20	Mon 09-11-20	Fri 13-11-20	$4,200.00
541		Concreting Works for Ground Beams	2 days	Mon 16-11-20	Tue 17-11-20	Mon 16-11-20	Tue 17-11-20	$3,626.00
542		Backfilling and Compaction	1 day	Wed 18-11-20	Wed 18-11-20	Wed 18-11-20	Wed 18-11-20	$0.00
543		**Ground Slab**	**7 days**	**Thu 19-11-20**	**Fri 27-11-20**	**Thu 19-11-20**	**Fri 27-11-20**	**$8,994.80**
544		Excavation for Ground Slab	1 day	Thu 19-11-20	Thu 19-11-20	Thu 19-11-20	Thu 19-11-20	$72.00
545		Anti Termite Treatment	1 day	Fri 20-11-20	Fri 20-11-20	Fri 20-11-20	Fri 20-11-20	$260.00
546		Installation of F/works	1 day	Mon 23-11-20	Mon 23-11-20	Mon 23-11-20	Mon 23-11-20	$500.00
547		Damp Proof Membrane	1 day	Tue 24-11-20	Tue 24-11-20	Tue 24-11-20	Tue 24-11-20	$260.00

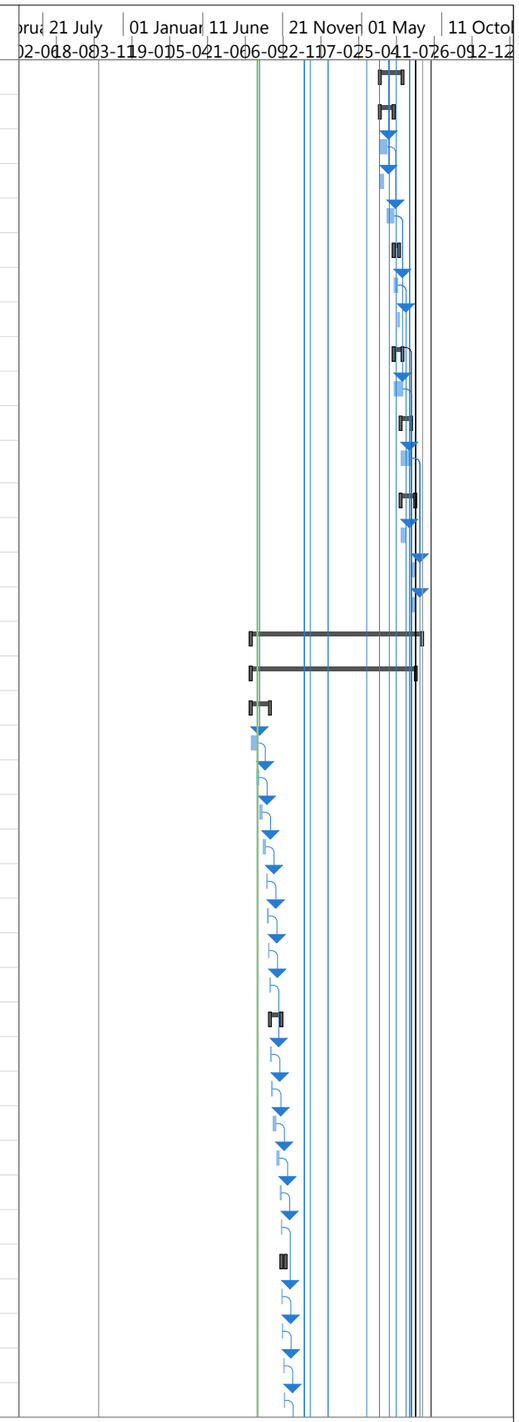

Project: Project1
Date: Thu 01-10-20


Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	

Disediakan oleh :

Disahkan oleh :

Disemak oleh :

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
548		Installation of Re-bars	2 days	Wed 25-11-20	Thu 26-11-20	Wed 25-11-20	Thu 26-11-20	$4,276.80
549		Concreting of Ground Slab	1 day	Fri 27-11-20	Fri 27-11-20	Fri 27-11-20	Fri 27-11-20	$3,626.00
550		**Frame**	**144 days**	**Mon 30-11-20**	**Thu 17-06-21**	**Mon 30-11-20**	**Thu 17-06-21**	**$122,211.86**
551		**Ground Floor - 1st Floor Columns**	**8 days**	**Mon 30-11-20**	**Wed 09-12-20**	**Mon 30-11-20**	**Wed 09-12-20**	**$8,965.83**
552		Installation of Formworks and Rebars	7 days	Mon 30-11-20	Tue 08-12-20	Mon 30-11-20	Tue 08-12-20	$4,735.53
553		Concreting Works	1 day	Wed 09-12-20	Wed 09-12-20	Wed 09-12-20	Wed 09-12-20	$4,230.30
554		**1st Floor R.C Beam & Floor Slab**	**8 days**	**Thu 10-12-20**	**Mon 21-12-20**	**Thu 10-12-20**	**Mon 21-12-20**	**$8,858.32**
555		Installation of F/works & Rebars	7 days	Thu 10-12-20	Fri 18-12-20	Thu 10-12-20	Fri 18-12-20	$6,268.32
556		Concreting Works	1 day	Mon 21-12-20	Mon 21-12-20	Mon 21-12-20	Mon 21-12-20	$2,590.00
557		**RC Staircase (GF -1st FL)**	**8 days**	**Tue 22-12-20**	**Thu 31-12-20**	**Tue 22-12-20**	**Thu 31-12-20**	**$3,262.93**
558		Installation of F/works & Re-Bars	7 days	Tue 22-12-20	Wed 30-12-20	Tue 22-12-20	Wed 30-12-20	$2,296.00
559		Concreting of RC Staircase	1 day	Thu 31-12-20	Thu 31-12-20	Thu 31-12-20	Thu 31-12-20	$966.93
560		**1st Floor - 2nd Floor Columns**	**8 days**	**Fri 01-01-21**	**Tue 12-01-21**	**Fri 01-01-21**	**Tue 12-01-21**	**$8,965.83**
561		Installation of Formworks and Rebars	7 days	Fri 01-01-21	Mon 11-01-21	Fri 01-01-21	Mon 11-01-21	$4,735.53
562		Concreting Works	1 day	Tue 12-01-21	Tue 12-01-21	Tue 12-01-21	Tue 12-01-21	$4,230.30
563		**2nd Floor R.C Beam & Slab**	**8 days**	**Wed 13-01-21**	**Fri 22-01-21**	**Wed 13-01-21**	**Fri 22-01-21**	**$8,858.32**
564		Installation of F/works & Rebars	7 days	Wed 13-01-21	Thu 21-01-21	Wed 13-01-21	Thu 21-01-21	$6,268.32
565		Concreting Works	1 day	Fri 22-01-21	Fri 22-01-21	Fri 22-01-21	Fri 22-01-21	$2,590.00
566		**RC Staircase (1st -2nd FL)**	**8 days**	**Mon 25-01-21**	**Wed 03-02-21**	**Mon 25-01-21**	**Wed 03-02-21**	**$3,262.93**
567		Installation of F/works & Re-Bars	7 days	Mon 25-01-21	Tue 02-02-21	Mon 25-01-21	Tue 02-02-21	$2,296.00
568		Concreting of RC Staircase	1 day	Wed 03-02-21	Wed 03-02-21	Wed 03-02-21	Wed 03-02-21	$966.93
569		**2nd Floor - 3rd Floor Columns**	**8 days**	**Thu 04-02-21**	**Mon 15-02-21**	**Thu 04-02-21**	**Mon 15-02-21**	**$8,965.53**
570		Installation of Formworks and Rebars	7 days	Thu 04-02-21	Fri 12-02-21	Thu 04-02-21	Fri 12-02-21	$4,735.53
571		Concreting Works	1 day	Mon 15-02-21	Mon 15-02-21	Mon 15-02-21	Mon 15-02-21	$4,230.00
572		**3rd Floor R.C Beam & Slab**	**8 days**	**Tue 16-02-21**	**Thu 25-02-21**	**Tue 16-02-21**	**Thu 25-02-21**	**$8,858.32**
573		Installation of F/works & Rebars	7 days	Tue 16-02-21	Wed 24-02-21	Tue 16-02-21	Wed 24-02-21	$6,268.32
574		Concreting Works	1 day	Thu 25-02-21	Thu 25-02-21	Thu 25-02-21	Thu 25-02-21	$2,590.00
575		**RC Staircase (2nd -3rd FL)**	**8 days**	**Fri 26-02-21**	**Tue 09-03-21**	**Fri 26-02-21**	**Tue 09-03-21**	**$3,262.93**
576		Installation of F/works & Re-Bars	7 days	Fri 26-02-21	Mon 08-03-21	Fri 26-02-21	Mon 08-03-21	$2,296.00
577		Concreting of RC Staircase	1 day	Tue 09-03-21	Tue 09-03-21	Tue 09-03-21	Tue 09-03-21	$966.93
578		**3rd Floor - 4th Floor Columns**	**8 days**	**Wed 10-03-21**	**Fri 19-03-21**	**Wed 10-03-21**	**Fri 19-03-21**	**$8,965.83**
579		Installation of Formworks and Rebars	7 days	Wed 10-03-21	Thu 18-03-21	Wed 10-03-21	Thu 18-03-21	$4,735.53
580		Concreting Works	1 day	Fri 19-03-21	Fri 19-03-21	Fri 19-03-21	Fri 19-03-21	$4,230.30
581		**4th Floor RC Beam & Slab**	**8 days**	**Mon 22-03-21**	**Wed 31-03-21**	**Mon 22-03-21**	**Wed 31-03-21**	**$8,858.32**
582		Installation of Formworks and Rebars	7 days	Mon 22-03-21	Tue 30-03-21	Mon 22-03-21	Tue 30-03-21	$6,268.32
583		Concreting Works	1 day	Wed 31-03-21	Wed 31-03-21	Wed 31-03-21	Wed 31-03-21	$2,590.00
584		**RC Staircase (3rd - 4th FL)**	**8 days**	**Thu 01-04-21**	**Mon 12-04-21**	**Thu 01-04-21**	**Mon 12-04-21**	**$3,262.93**
585		Installation of Formworks and Rebars	7 days	Thu 01-04-21	Fri 09-04-21	Thu 01-04-21	Fri 09-04-21	$2,296.00
586		Concreting Works	1 day	Mon 12-04-21	Mon 12-04-21	Mon 12-04-21	Mon 12-04-21	$966.93
587		**4th Floor - 5th Floor Columns**	**8 days**	**Tue 13-04-21**	**Thu 22-04-21**	**Tue 13-04-21**	**Thu 22-04-21**	**$8,965.83**

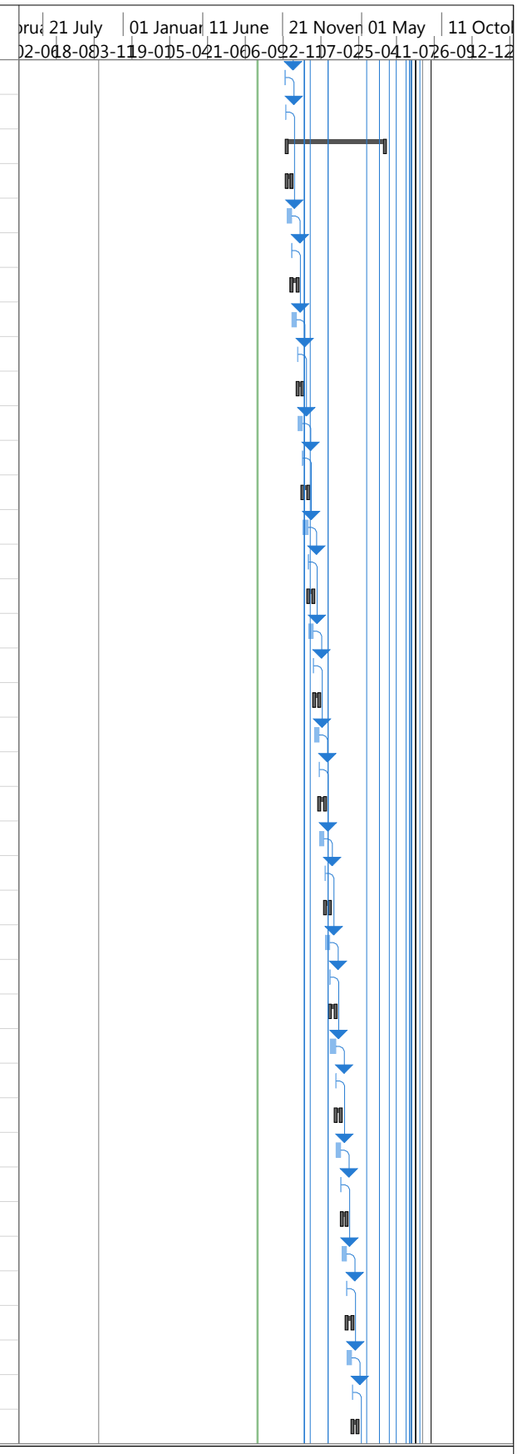

Project: Project1
Date: Thu 01-10-20


Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone

Disediakan oleh :

Disahkan oleh :

Disemak oleh :

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
588		Installation of Formworks and Rebars	7 days	Tue 13-04-21	Wed 21-04-21	Tue 13-04-21	Wed 21-04-21	$4,735.53
589		Concreting Works	1 day	Thu 22-04-21	Thu 22-04-21	Thu 22-04-21	Thu 22-04-21	$4,230.30
590		**5th Floor R.C Beam & Slab**	**8 days**	**Fri 23-04-21**	**Tue 04-05-21**	**Fri 23-04-21**	**Tue 04-05-21**	**$8,858.32**
591		Installation of F/works & Rebars	7 days	Fri 23-04-21	Mon 03-05-21	Fri 23-04-21	Mon 03-05-21	$6,268.32
592		Concreting Works	1 day	Tue 04-05-21	Tue 04-05-21	Tue 04-05-21	Tue 04-05-21	$2,590.00
593		**RC Staircase (4th -5th Level)**	**8 days**	**Wed 05-05-21**	**Fri 14-05-21**	**Wed 05-05-21**	**Fri 14-05-21**	**$3,262.93**
594		Installation of F/works & Rebars	7 days	Wed 05-05-21	Thu 13-05-21	Wed 05-05-21	Thu 13-05-21	$2,296.00
595		Concreting Works	1 day	Fri 14-05-21	Fri 14-05-21	Fri 14-05-21	Fri 14-05-21	$966.93
596		**5th Floor - Roof Level Columns**	**8 days**	**Mon 17-05-21**	**Wed 26-05-21**	**Mon 17-05-21**	**Wed 26-05-21**	**$8,965.83**
597		Installation of Formworks and Rebars	7 days	Mon 17-05-21	Tue 25-05-21	Mon 17-05-21	Tue 25-05-21	$4,735.53
598		Concreting Works	1 day	Wed 26-05-21	Wed 26-05-21	Wed 26-05-21	Wed 26-05-21	$4,230.30
599		**Roof R.C Beam & Slab**	**8 days**	**Thu 27-05-21**	**Mon 07-06-21**	**Thu 27-05-21**	**Mon 07-06-21**	**$4,548.00**
600		Installation of F/works & Rebars	7 days	Thu 27-05-21	Fri 04-06-21	Thu 27-05-21	Fri 04-06-21	$2,994.00
601		Concreting Works	1 day	Mon 07-06-21	Mon 07-06-21	Mon 07-06-21	Mon 07-06-21	$1,554.00
602		**RC Staircase (5th -Roof Level)**	**8 days**	**Tue 08-06-21**	**Thu 17-06-21**	**Tue 08-06-21**	**Thu 17-06-21**	**$3,262.93**
603		Installation of F/works & Re-Bars	7 days	Tue 08-06-21	Wed 16-06-21	Tue 08-06-21	Wed 16-06-21	$2,296.00
604		Concreting of RC Staircase	1 day	Thu 17-06-21	Thu 17-06-21	Thu 17-06-21	Thu 17-06-21	$966.93
605		**Walls**	**14 days**	**Fri 18-06-21**	**Wed 07-07-21**	**Fri 18-06-21**	**Wed 07-07-21**	**$12,250.00**
606		Installation of Half Brick Wall including Waterproofing and Sundries	14 days	Fri 18-06-21	Wed 07-07-21	Fri 18-06-21	Wed 07-07-21	$12,250.00
607		**External Doors and Windows**	**17 days**	**Thu 08-07-21**	**Fri 30-07-21**	**Thu 08-07-21**	**Fri 30-07-21**	**$18,390.00**
608		Lintols	7 days	Thu 08-07-21	Fri 16-07-21	Thu 08-07-21	Fri 16-07-21	$500.00
609		Installation of Door Frames, Panels, Accessories, Ironmongeries and Finishing	10 days	Mon 19-07-21	Fri 30-07-21	Mon 19-07-21	Fri 30-07-21	$17,890.00
610		**Internal Finishes**	**45 days**	**Fri 18-06-21**	**Thu 19-08-21**	**Fri 18-06-21**	**Thu 19-08-21**	**$28,208.00**
611		**Internal Wall Finishes**	**24 days**	**Thu 08-07-21**	**Tue 10-08-21**	**Thu 08-07-21**	**Tue 10-08-21**	**$7,344.00**
612		Wall Plastering	14 days	Thu 08-07-21	Tue 27-07-21	Thu 08-07-21	Tue 27-07-21	$3,888.00
613		Wall Painting Finishes	10 days	Wed 28-07-21	Tue 10-08-21	Wed 28-07-21	Tue 10-08-21	$3,456.00
614		**Internal Floor Finishes**	**2 days**	**Wed 11-08-21**	**Thu 12-08-21**	**Wed 11-08-21**	**Thu 12-08-21**	**$352.00**
615		Cement Screed	2 days	Wed 11-08-21	Thu 12-08-21	Wed 11-08-21	Thu 12-08-21	$352.00
616		**Internal Ceiling Finishes**	**4 days**	**Fri 13-08-21**	**Wed 18-08-21**	**Fri 13-08-21**	**Wed 18-08-21**	**$616.00**
617		Ceiling Plastering Finishes	2 days	Fri 13-08-21	Mon 16-08-21	Fri 13-08-21	Mon 16-08-21	$308.00
618		Painting of Internal Ceiling	2 days	Tue 17-08-21	Wed 18-08-21	Tue 17-08-21	Wed 18-08-21	$308.00
619		**Staircase Finishes**	**45 days**	**Fri 18-06-21**	**Thu 19-08-21**	**Fri 18-06-21**	**Thu 19-08-21**	**$19,896.00**
620		Plastering Work and Painting Finishes to Staircase	30 days	Fri 18-06-21	Thu 29-07-21	Fri 18-06-21	Thu 29-07-21	$4,970.00
621		Mild Steel Railing	15 days	Fri 30-07-21	Thu 19-08-21	Fri 30-07-21	Thu 19-08-21	$14,926.00
622		**External Finishes**	**20 days**	**Thu 08-07-21**	**Wed 04-08-21**	**Thu 08-07-21**	**Wed 04-08-21**	**$28,222.00**
623		**External Wall Finishes**	**14 days**	**Thu 08-07-21**	**Tue 27-07-21**	**Thu 08-07-21**	**Tue 27-07-21**	**$24,273.00**
624		Wall Plastering, Waterproofing and WallPainting Finishes	14 days	Thu 08-07-21	Tue 27-07-21	Thu 08-07-21	Tue 27-07-21	$24,273.00
625		External Floor Finishes : Cement Screed	3 days	Wed 28-07-21	Fri 30-07-21	Wed 28-07-21	Fri 30-07-21	$1,872.00
626		External Ceiling Finishes: Cement Screed and Painting	3 days	Mon 02-08-21	Wed 04-08-21	Mon 02-08-21	Wed 04-08-21	$2,077.00

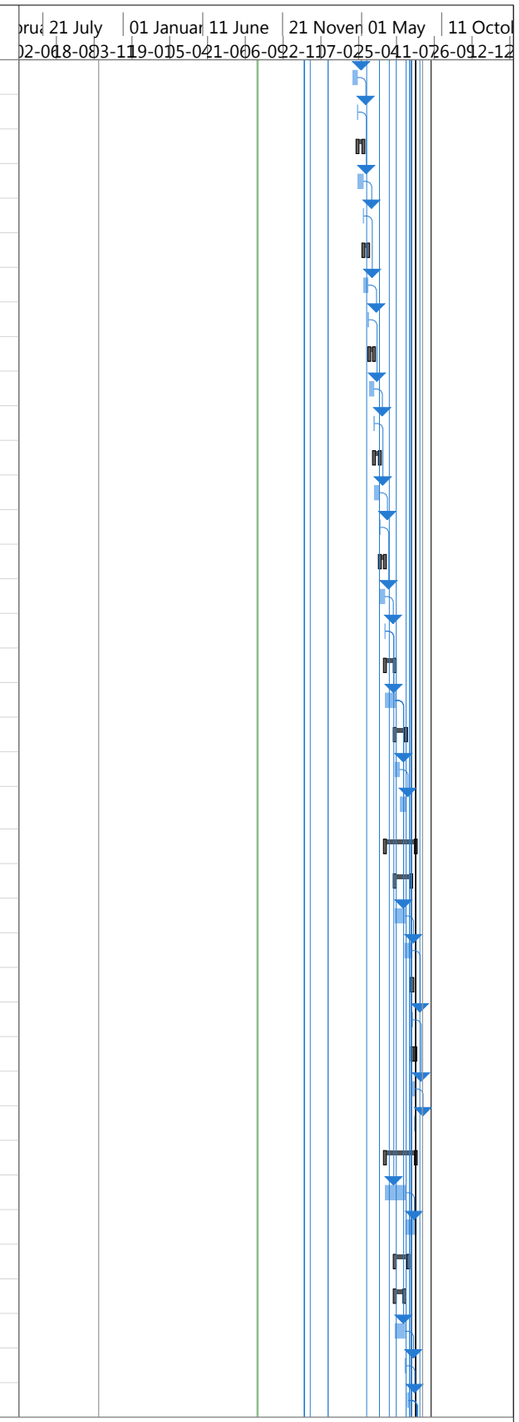

Project: Project1
Date: Thu 01-10-20


Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone

Disediakan oleh :

Disahkan oleh :

Disemak oleh :

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
627		Wall Climbing System	20 days	Thu 05-08-21	Wed 01-09-21	Thu 05-08-21	Wed 01-09-21	$109,737.00
628		Roof Builder's Work: GI Pipes to Parapet Walls, MS Door & waterproofing Work	5 days	Thu 05-08-21	Wed 11-08-21	Thu 05-08-21	Wed 11-08-21	$7,716.00
629		**RUMAH PAM**	**59 days**	**Mon 02-11-20**	**Thu 21-01-21**	**Mon 02-11-20**	**Thu 21-01-21**	**$42,408.00**
630		**Structural Works**	**48 days**	**Mon 02-11-20**	**Wed 06-01-21**	**Mon 02-11-20**	**Wed 06-01-21**	**$25,175.70**
631		**Pad Footings and RC Stump**	**14 days**	**Mon 02-11-20**	**Thu 19-11-20**	**Mon 02-11-20**	**Thu 19-11-20**	**$9,043.50**
632		Building Setting out&Survey	1 day	Mon 02-11-20	Mon 02-11-20	Mon 02-11-20	Mon 02-11-20	$0.00
633		Excavation of Pad Footings	2 days	Tue 03-11-20	Wed 04-11-20	Tue 03-11-20	Wed 04-11-20	$320.00
634		Lean Concrete	1 day	Thu 05-11-20	Thu 05-11-20	Thu 05-11-20	Thu 05-11-20	$360.00
635		Installation of Formwork to Pad Footings	3 days	Fri 06-11-20	Tue 10-11-20	Fri 06-11-20	Tue 10-11-20	$1,050.00
636		Installation of Reinforcement Bars to Pad Footings& Stumps	3 days	Wed 11-11-20	Fri 13-11-20	Wed 11-11-20	Fri 13-11-20	$2,038.50
637		Concreting Works of Pad Footings	1 day	Mon 16-11-20	Mon 16-11-20	Mon 16-11-20	Mon 16-11-20	$4,500.00
638		Installation of Stumps F/works	1 day	Tue 17-11-20	Tue 17-11-20	Tue 17-11-20	Tue 17-11-20	$550.00
639		Concreting Works for Stumps	1 day	Wed 18-11-20	Wed 18-11-20	Wed 18-11-20	Wed 18-11-20	$225.00
640		Backfilling&Compaction	1 day	Thu 19-11-20	Thu 19-11-20	Thu 19-11-20	Thu 19-11-20	$0.00
641		**Ground Beam Structures**	**11 days**	**Fri 20-11-20**	**Fri 04-12-20**	**Fri 20-11-20**	**Fri 04-12-20**	**$3,541.00**
642		Excavation of Ground Beam	2 days	Fri 20-11-20	Mon 23-11-20	Fri 20-11-20	Mon 23-11-20	$24.00
643		Lean Concrete	1 day	Tue 24-11-20	Tue 24-11-20	Tue 24-11-20	Tue 24-11-20	$75.00
644		Installation of Ground Beam F/works	3 days	Wed 25-11-20	Fri 27-11-20	Wed 25-11-20	Fri 27-11-20	$1,350.00
645		Installation of Ground Beam Rebars	3 days	Mon 30-11-20	Wed 02-12-20	Mon 30-11-20	Wed 02-12-20	$1,192.00
646		Concreting Works for Ground Beams	1 day	Thu 03-12-20	Thu 03-12-20	Thu 03-12-20	Thu 03-12-20	$900.00
647		Backfilling and Compaction	1 day	Fri 04-12-20	Fri 04-12-20	Fri 04-12-20	Fri 04-12-20	$0.00
648		**Ground Slab**	**10 days**	**Mon 07-12-20**	**Fri 18-12-20**	**Mon 07-12-20**	**Fri 18-12-20**	**$5,715.07**
649		Excavation of Ground Slab	1 day	Mon 07-12-20	Mon 07-12-20	Mon 07-12-20	Mon 07-12-20	$56.00
650		Anti Termite Treatment	1 day	Tue 08-12-20	Tue 08-12-20	Tue 08-12-20	Tue 08-12-20	$205.00
651		Installation of F/works	1 day	Wed 09-12-20	Wed 09-12-20	Wed 09-12-20	Wed 09-12-20	$210.00
652		Damp Proof Membrane	1 day	Thu 10-12-20	Thu 10-12-20	Thu 10-12-20	Thu 10-12-20	$120.00
653		Lean Concrete	1 day	Fri 11-12-20	Fri 11-12-20	Fri 11-12-20	Fri 11-12-20	$420.00
654		Installation of Re-bars	1 day	Mon 14-12-20	Mon 14-12-20	Mon 14-12-20	Mon 14-12-20	$1,174.50
655		Concreting of Ground Slab	1 day	Tue 15-12-20	Tue 15-12-20	Tue 15-12-20	Tue 15-12-20	$2,700.00
656		Plinth	3 days	Wed 16-12-20	Fri 18-12-20	Wed 16-12-20	Fri 18-12-20	$829.57
657		**Apron Slab & Ramp**	**6 days**	**Wed 16-12-20**	**Wed 23-12-20**	**Wed 16-12-20**	**Wed 23-12-20**	**$1,513.63**
658		Excavation for Apron Slab	1 day	Wed 16-12-20	Wed 16-12-20	Wed 16-12-20	Wed 16-12-20	$16.50
659		Installation of F/works	2 days	Thu 17-12-20	Fri 18-12-20	Thu 17-12-20	Fri 18-12-20	$0.00
660		Lean Concrete	1 day	Mon 21-12-20	Mon 21-12-20	Mon 21-12-20	Mon 21-12-20	$120.00
661		Installation of Re-bars	2 days	Tue 22-12-20	Wed 23-12-20	Tue 22-12-20	Wed 23-12-20	$832.13
662		Concreting of Apron Slab & Ramp	1 day	Tue 22-12-20	Tue 22-12-20	Tue 22-12-20	Tue 22-12-20	$545.00
663		**Columns**	**3 days**	**Wed 16-12-20**	**Fri 18-12-20**	**Wed 16-12-20**	**Fri 18-12-20**	**$1,311.00**
664		Installation of Formworks	1 day	Wed 16-12-20	Wed 16-12-20	Wed 16-12-20	Wed 16-12-20	$600.00
665		Installation of Reinforcement Bars	1 day	Thu 17-12-20	Thu 17-12-20	Thu 17-12-20	Thu 17-12-20	$351.00

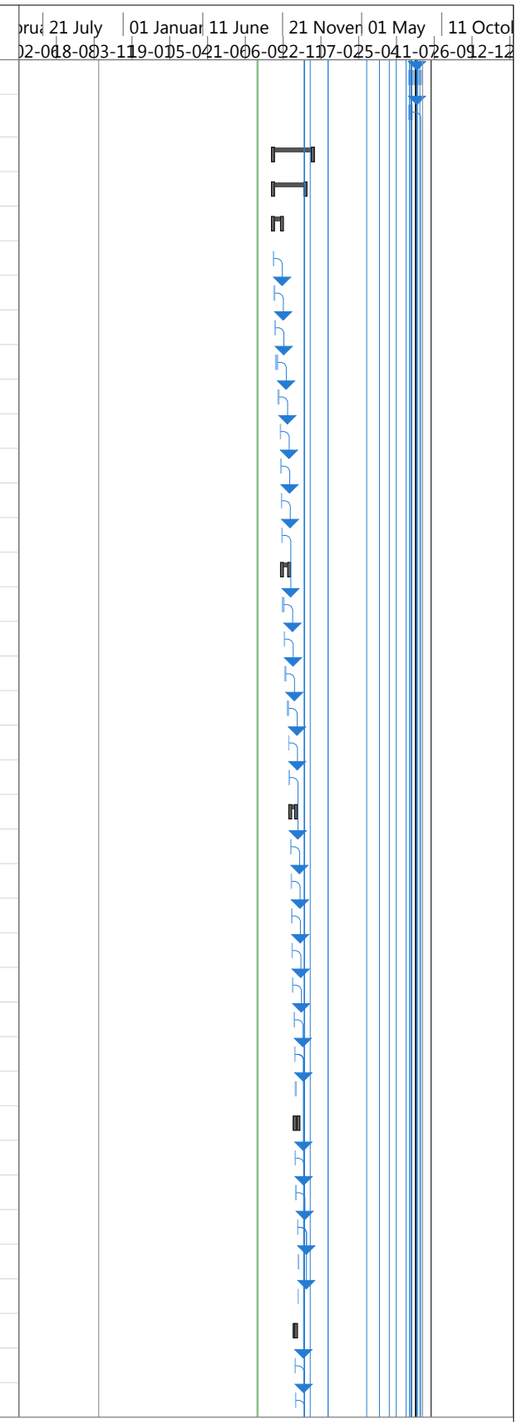

Project: Project1
Date: Thu 01-10-20


Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	

Disediakan oleh :

Disahkan oleh :

Disemak oleh :

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
666		Concreting Works	1 day	Fri 18-12-20	Fri 18-12-20	Fri 18-12-20	Fri 18-12-20	$360.00
667		**Roof Beams & Hoods**	**5 days**	**Mon 21-12-20**	**Fri 25-12-20**	**Mon 21-12-20**	**Fri 25-12-20**	**$2,991.50**
668		Installation of F/works for Roof Beams	2 days	Mon 21-12-20	Tue 22-12-20	Mon 21-12-20	Tue 22-12-20	$1,250.00
669		Installation of Rebars for Roof Beams	2 days	Wed 23-12-20	Thu 24-12-20	Wed 23-12-20	Thu 24-12-20	$391.50
670		Concreting Works for Roof Beams	1 day	Fri 25-12-20	Fri 25-12-20	Fri 25-12-20	Fri 25-12-20	$1,350.00
671		**RC Gutter**	**8 days**	**Mon 28-12-20**	**Wed 06-01-21**	**Mon 28-12-20**	**Wed 06-01-21**	**$1,060.00**
672		Installation of F/works	2 days	Mon 28-12-20	Tue 29-12-20	Mon 28-12-20	Tue 29-12-20	$250.00
673		Installation of Rebars	2 days	Wed 30-12-20	Thu 31-12-20	Wed 30-12-20	Thu 31-12-20	$252.00
674		Concreting of RC Gutter	2 days	Fri 01-01-21	Mon 04-01-21	Fri 01-01-21	Mon 04-01-21	$360.00
675		Waterproofing and Finishing of RC Gutter	2 days	Tue 05-01-21	Wed 06-01-21	Tue 05-01-21	Wed 06-01-21	$198.00
676		**Installation of Roofing System**	**8 days**	**Thu 07-01-21**	**Mon 18-01-21**	**Thu 07-01-21**	**Mon 18-01-21**	**$4,767.00**
677		Installation of Roof Trusses, Rafters, Battens, Purlins and all necessary Structural Items	3 days	Thu 07-01-21	Mon 11-01-21	Thu 07-01-21	Mon 11-01-21	$2,792.00
678		Intallation of Roof Covering; including Aluminium Foil Insulation, Chicken Wire Mesh, Facia Board, Gutter and other necessary finishes.	3 days	Tue 12-01-21	Thu 14-01-21	Tue 12-01-21	Thu 14-01-21	$1,510.00
679		Rainwater Downpipes (RWDP)	2 days	Fri 15-01-21	Mon 18-01-21	Fri 15-01-21	Mon 18-01-21	$465.00
680		**Architectural Works**	**13 days**	**Tue 05-01-21**	**Thu 21-01-21**	**Tue 05-01-21**	**Thu 21-01-21**	**$12,465.30**
681		**External Wall**	**3 days**	**Tue 05-01-21**	**Thu 07-01-21**	**Tue 05-01-21**	**Thu 07-01-21**	**$2,662.30**
682		External Wall (Half Brick Wall including all sundries)	3 days	Tue 05-01-21	Thu 07-01-21	Tue 05-01-21	Thu 07-01-21	$2,662.30
683		**External Doors & Windows**	**4 days**	**Fri 08-01-21**	**Wed 13-01-21**	**Fri 08-01-21**	**Wed 13-01-21**	**$2,110.00**
684		**External Doors**	**4 days**	**Fri 08-01-21**	**Wed 13-01-21**	**Fri 08-01-21**	**Wed 13-01-21**	**$1,265.00**
685		Lintols	1 day	Fri 08-01-21	Fri 08-01-21	Fri 08-01-21	Fri 08-01-21	$50.00
686		Door Frames	1 day	Mon 11-01-21	Mon 11-01-21	Mon 11-01-21	Mon 11-01-21	$0.00
687		Door Panels	1 day	Tue 12-01-21	Tue 12-01-21	Tue 12-01-21	Tue 12-01-21	$1,130.00
688		Ironmongeries including Door Finishes	1 day	Wed 13-01-21	Wed 13-01-21	Wed 13-01-21	Wed 13-01-21	$85.00
689		**External Windows**	**2 days**	**Fri 08-01-21**	**Mon 11-01-21**	**Fri 08-01-21**	**Mon 11-01-21**	**$845.00**
690		Lintols	1 day	Fri 08-01-21	Fri 08-01-21	Fri 08-01-21	Fri 08-01-21	$125.00
691		Intallation of Aluminium Window Frames and Panels	1 day	Mon 11-01-21	Mon 11-01-21	Mon 11-01-21	Mon 11-01-21	$720.00
692		**Internal Wall Finishes**	**5 days**	**Fri 08-01-21**	**Thu 14-01-21**	**Fri 08-01-21**	**Thu 14-01-21**	**$1,568.00**
693		Plastering of Walls& Columns	3 days	Fri 08-01-21	Tue 12-01-21	Fri 08-01-21	Tue 12-01-21	$784.00
694		Internal Wall Painting Finishes	2 days	Wed 13-01-21	Thu 14-01-21	Wed 13-01-21	Thu 14-01-21	$784.00
695		**Internal Floor Finishes**	**2 days**	**Fri 15-01-21**	**Mon 18-01-21**	**Fri 15-01-21**	**Mon 18-01-21**	**$455.00**
696		Cement Screed	2 days	Fri 15-01-21	Mon 18-01-21	Fri 15-01-21	Mon 18-01-21	$455.00
697		**Internal Ceiling Finishes**	**2 days**	**Tue 19-01-21**	**Wed 20-01-21**	**Tue 19-01-21**	**Wed 20-01-21**	**$2,850.00**
698		Plaster ceiling Finishes	1 day	Tue 19-01-21	Tue 19-01-21	Tue 19-01-21	Tue 19-01-21	$1,520.00
699		Painting of Intrenal Ceiling	1 day	Wed 20-01-21	Wed 20-01-21	Wed 20-01-21	Wed 20-01-21	$1,330.00
700		**External Finishes**	**7 days**	**Wed 13-01-21**	**Thu 21-01-21**	**Wed 13-01-21**	**Thu 21-01-21**	**$2,820.00**
701		**External Wall**	**5 days**	**Wed 13-01-21**	**Tue 19-01-21**	**Wed 13-01-21**	**Tue 19-01-21**	**$1,568.00**
702		External Plastering to External Wall	3 days	Wed 13-01-21	Fri 15-01-21	Wed 13-01-21	Fri 15-01-21	$784.00
703		External Wall Painting Finishes	2 days	Mon 18-01-21	Tue 19-01-21	Mon 18-01-21	Tue 19-01-21	$784.00
704		**External Floor Finishes**	**1 day**	**Wed 20-01-21**	**Wed 20-01-21**	**Wed 20-01-21**	**Wed 20-01-21**	**$252.00**

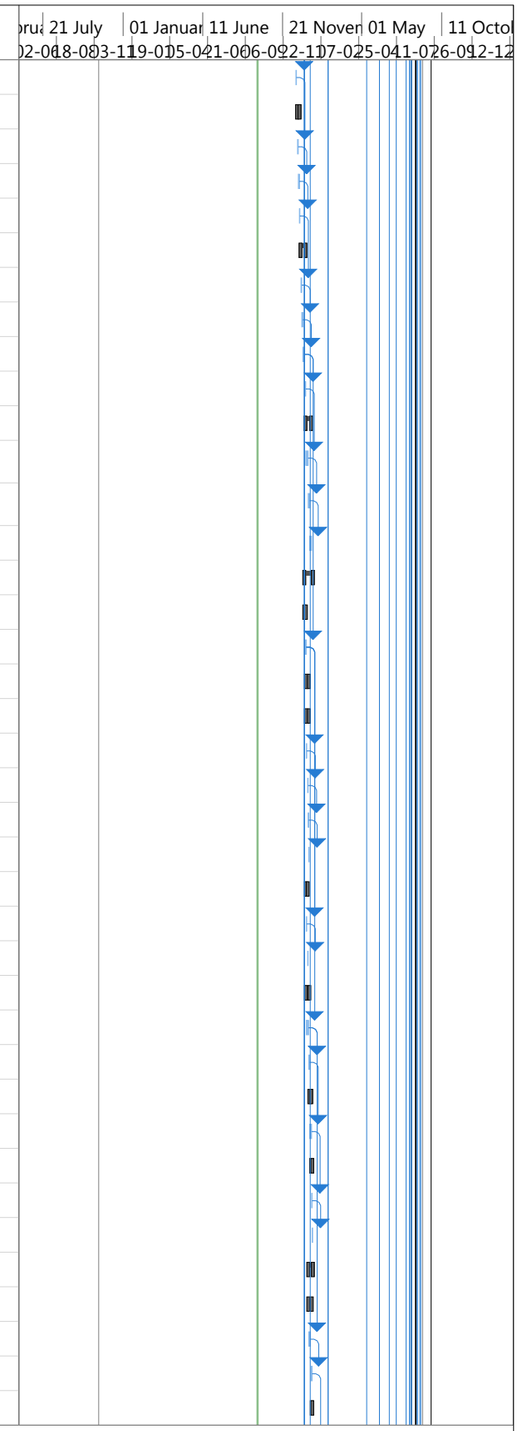

Project: Project1
Date: Thu 01-10-20


Task	Project Summary	Manual Task	Start-only	Deadline	
Split	Inactive Task	Duration-only	Finish-only	Progress	
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress	
Summary	Inactive Summary	Manual Summary	External Milestone		

Disediakan oleh :

Disahkan oleh :

Disemak oleh :

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
705		Cement Screed Finishes	1 day	Wed 20-01-21	Wed 20-01-21	Wed 20-01-21	Wed 20-01-21	$252.00
706		**External Ceiling Finishes**	**1 day**	**Thu 21-01-21**	**Thu 21-01-21**	**Thu 21-01-21**	**Thu 21-01-21**	**$1,000.00**
707		External Ceiling Finishes	1 day	Thu 21-01-21	Thu 21-01-21	Thu 21-01-21	Thu 21-01-21	$1,000.00
708		**TEMPAT LETAK KERETA BERBUMBUNG**	**29 days**	**Mon 01-03-21**	**Thu 08-04-21**	**Mon 01-03-21**	**Thu 08-04-21**	**$26,598.00**
709		Excavation of Pad Footings	3 days	Mon 01-03-21	Wed 03-03-21	Mon 01-03-21	Wed 03-03-21	$64.00
710		Installation of F/works to Pad Footings including Lean Concrete	3 days	Thu 04-03-21	Mon 08-03-21	Thu 04-03-21	Mon 08-03-21	$670.00
711		Installation of Rebars to Pad Footings & Stumps	3 days	Tue 09-03-21	Thu 11-03-21	Tue 09-03-21	Thu 11-03-21	$1,209.00
712		Concreting of Pad Footings	3 days	Fri 12-03-21	Tue 16-03-21	Fri 12-03-21	Tue 16-03-21	$1,350.00
713		Installation of F/works and Concreting of Stumps	2 days	Wed 17-03-21	Thu 18-03-21	Wed 17-03-21	Thu 18-03-21	$750.00
714		Backfill	1 day	Fri 19-03-21	Fri 19-03-21	Fri 19-03-21	Fri 19-03-21	$6.50
715		Installation of GI Posts	7 days	Mon 22-03-21	Tue 30-03-21	Mon 22-03-21	Tue 30-03-21	$4,362.00
716		Installation of Roofing System	7 days	Wed 31-03-21	Thu 08-04-21	Wed 31-03-21	Thu 08-04-21	$18,186.50
717		**STOR LOGISTIK**	**114 days**	**Tue 01-12-20**	**Fri 07-05-21**	**Tue 01-12-20**	**Fri 07-05-21**	**$83,699.65**
718		**Structural Works**	**82 days**	**Tue 01-12-20**	**Wed 24-03-21**	**Tue 01-12-20**	**Wed 24-03-21**	**$50,165.50**
719		**Pad Footings and RC Stump**	**29 days**	**Tue 01-12-20**	**Fri 08-01-21**	**Tue 01-12-20**	**Fri 08-01-21**	**$11,039.50**
720		Building Setting out&Survey	2 days	Tue 01-12-20	Wed 02-12-20	Tue 01-12-20	Wed 02-12-20	$0.00
721		Excavation of Pad Footings	7 days	Thu 03-12-20	Fri 11-12-20	Thu 03-12-20	Fri 11-12-20	$504.00
722		Lean Concrete	3 days	Mon 14-12-20	Wed 16-12-20	Mon 14-12-20	Wed 16-12-20	$570.00
723		Installation of Formwork to Pad Footings	5 days	Thu 17-12-20	Wed 23-12-20	Thu 17-12-20	Wed 23-12-20	$1,600.00
724		Installation of Reinforcement Bars to Pad Footings&Stumps	5 days	Thu 24-12-20	Wed 30-12-20	Thu 24-12-20	Wed 30-12-20	$2,560.50
725		Concreting Works of Pad Footings	3 days	Thu 31-12-20	Mon 04-01-21	Thu 31-12-20	Mon 04-01-21	$4,750.00
726		Installation of Stumps F/works	1 day	Tue 05-01-21	Tue 05-01-21	Tue 05-01-21	Tue 05-01-21	$650.00
727		Concreting Works for Stumps	1 day	Wed 06-01-21	Wed 06-01-21	Wed 06-01-21	Wed 06-01-21	$405.00
728		Backfilling&Compaction	2 days	Thu 07-01-21	Fri 08-01-21	Thu 07-01-21	Fri 08-01-21	$0.00
729		**Ground Beam Structures**	**18 days**	**Mon 11-01-21**	**Wed 03-02-21**	**Mon 11-01-21**	**Wed 03-02-21**	**$10,107.00**
730		Excavation of Ground Beam	3 days	Mon 11-01-21	Wed 13-01-21	Mon 11-01-21	Wed 13-01-21	$72.00
731		Lean Concrete	2 days	Thu 14-01-21	Fri 15-01-21	Thu 14-01-21	Fri 15-01-21	$285.00
732		Installation of Ground Beam F/works	4 days	Mon 18-01-21	Thu 21-01-21	Mon 18-01-21	Thu 21-01-21	$3,650.00
733		Installation of Ground Beam Rebars	4 days	Fri 22-01-21	Wed 27-01-21	Fri 22-01-21	Wed 27-01-21	$2,500.00
734		Concreting Works for Ground Beams	3 days	Thu 28-01-21	Mon 01-02-21	Thu 28-01-21	Mon 01-02-21	$3,600.00
735		Backfilling and Compaction	2 days	Tue 02-02-21	Wed 03-02-21	Tue 02-02-21	Wed 03-02-21	$0.00
736		**Ground Slab**	**9 days**	**Thu 04-02-21**	**Tue 16-02-21**	**Thu 04-02-21**	**Tue 16-02-21**	**$9,129.00**
737		Excavation of Ground Slab	2 days	Thu 04-02-21	Fri 05-02-21	Thu 04-02-21	Fri 05-02-21	$104.00
738		Anti Termite Treatment	1 day	Mon 08-02-21	Mon 08-02-21	Mon 08-02-21	Mon 08-02-21	$425.00
739		Installation of F/works	1 day	Tue 09-02-21	Tue 09-02-21	Tue 09-02-21	Tue 09-02-21	$425.00
740		Damp Proof Membrane	1 day	Wed 10-02-21	Wed 10-02-21	Wed 10-02-21	Wed 10-02-21	$315.00
741		Lean Concrete	1 day	Thu 11-02-21	Thu 11-02-21	Thu 11-02-21	Thu 11-02-21	$660.00
742		Installation of Re-bars	2 days	Fri 12-02-21	Mon 15-02-21	Fri 12-02-21	Mon 15-02-21	$3,150.00
743		Concreting of Ground Slab	1 day	Tue 16-02-21	Tue 16-02-21	Tue 16-02-21	Tue 16-02-21	$4,050.00
744		**Apron Slab & Ramp**	**5 days**	**Wed 17-02-21**	**Tue 23-02-21**	**Wed 17-02-21**	**Tue 23-02-21**	**$4,303.00**

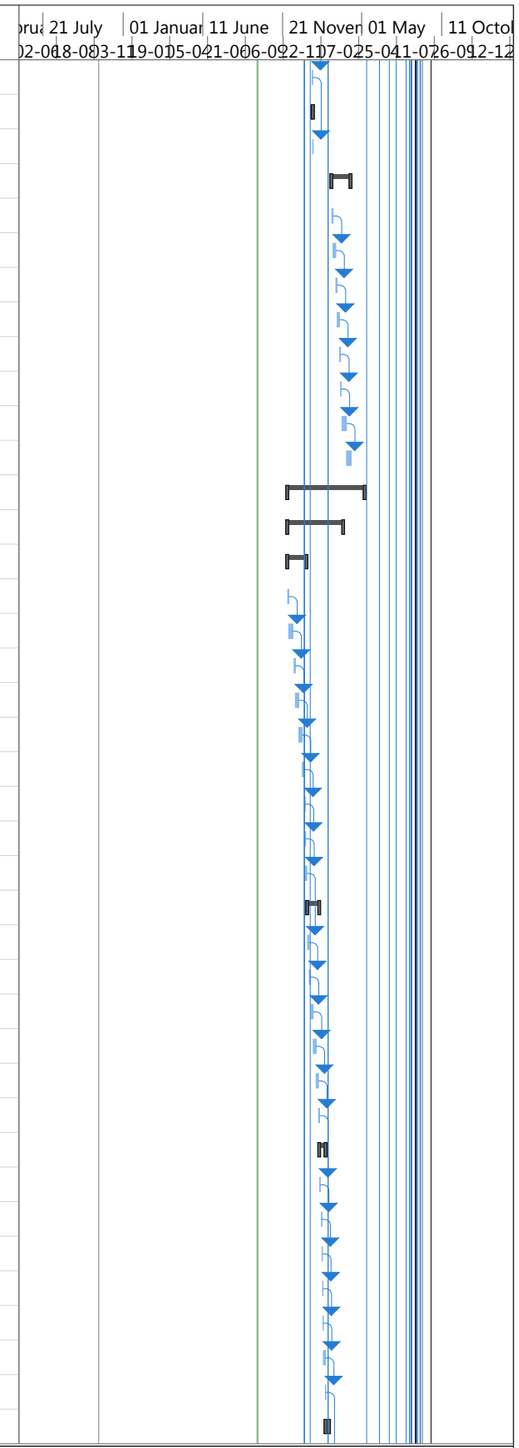

Project: Project1
Date: Thu 01-10-20


Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	

Disediakan oleh :

Disahkan oleh :

Disemak oleh :

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
745		Excavation for Apron Slab	1 day	Wed 17-02-21	Wed 17-02-21	Wed 17-02-21	Wed 17-02-21	$32.00
746		Installation of F/works	1 day	Thu 18-02-21	Thu 18-02-21	Thu 18-02-21	Thu 18-02-21	$0.00
747		Lean Concrete	1 day	Fri 19-02-21	Fri 19-02-21	Fri 19-02-21	Fri 19-02-21	$0.00
748		Installation of Re-bars	1 day	Mon 22-02-21	Mon 22-02-21	Mon 22-02-21	Mon 22-02-21	$989.00
749		Concreting of Apron Slab& Ramp	1 day	Tue 23-02-21	Tue 23-02-21	Tue 23-02-21	Tue 23-02-21	$3,282.00
750		**Columns**	**7 days**	**Wed 24-02-21**	**Thu 04-03-21**	**Wed 24-02-21**	**Thu 04-03-21**	**$5,577.00**
751		Installation of Formworks	3 days	Wed 24-02-21	Fri 26-02-21	Wed 24-02-21	Fri 26-02-21	$1,950.00
752		Installation of Reinforcement Bars	3 days	Mon 01-03-21	Wed 03-03-21	Mon 01-03-21	Wed 03-03-21	$2,277.00
753		Concreting Works	1 day	Thu 04-03-21	Thu 04-03-21	Thu 04-03-21	Thu 04-03-21	$1,350.00
754		**Roof Beams & Hoods**	**8 days**	**Fri 05-03-21**	**Tue 16-03-21**	**Fri 05-03-21**	**Tue 16-03-21**	**$7,490.00**
755		Installation of F/works for Roof Beams	3 days	Fri 05-03-21	Tue 09-03-21	Fri 05-03-21	Tue 09-03-21	$2,550.00
756		Installation of Rebars for Roof Beams	3 days	Wed 10-03-21	Fri 12-03-21	Wed 10-03-21	Fri 12-03-21	$2,790.00
757		Concreting Works for Roof Beams	2 days	Mon 15-03-21	Tue 16-03-21	Mon 15-03-21	Tue 16-03-21	$2,150.00
758		**RC Gutter**	**6 days**	**Wed 17-03-21**	**Wed 24-03-21**	**Wed 17-03-21**	**Wed 24-03-21**	**$2,520.00**
759		Installation of F/works	2 days	Wed 17-03-21	Thu 18-03-21	Wed 17-03-21	Thu 18-03-21	$900.00
760		Installation of Rebars	2 days	Fri 19-03-21	Mon 22-03-21	Fri 19-03-21	Mon 22-03-21	$720.00
761		Concreting of RC Gutter	2 days	Tue 23-03-21	Wed 24-03-21	Tue 23-03-21	Wed 24-03-21	$900.00
762		**Installation of Roofing System**	**9 days**	**Thu 25-03-21**	**Tue 06-04-21**	**Thu 25-03-21**	**Tue 06-04-21**	**$7,166.00**
763		Installation of Roof Trusses, Rafters, Battens, Purlins and all necessary Structural Items	4 days	Thu 25-03-21	Tue 30-03-21	Thu 25-03-21	Tue 30-03-21	$1,550.00
764		Intallation of Roof Covering; including Aluminium Foil Insulation, Chicken Wire Mesh, Facia Board, Gutter and other necessary finishes.	4 days	Wed 31-03-21	Mon 05-04-21	Wed 31-03-21	Mon 05-04-21	$4,750.00
765		Rainwater Downpipes (RWDP)	1 day	Tue 06-04-21	Tue 06-04-21	Tue 06-04-21	Tue 06-04-21	$866.00
766		**Architectural Works**	**38 days**	**Wed 17-03-21**	**Fri 07-05-21**	**Wed 17-03-21**	**Fri 07-05-21**	**$26,368.15**
767		**External Wall**	**7 days**	**Wed 17-03-21**	**Thu 25-03-21**	**Wed 17-03-21**	**Thu 25-03-21**	**$4,770.00**
768		External Wall (Half Brick Wall including all sundries)	7 days	Wed 17-03-21	Thu 25-03-21	Wed 17-03-21	Thu 25-03-21	$4,770.00
769		**External Doors & Windows**	**6 days**	**Fri 26-03-21**	**Fri 02-04-21**	**Fri 26-03-21**	**Fri 02-04-21**	**$4,625.00**
770		**External Doors**	**3 days**	**Fri 26-03-21**	**Tue 30-03-21**	**Fri 26-03-21**	**Tue 30-03-21**	**$4,125.00**
771		Motorized Door including all Accessories	3 days	Fri 26-03-21	Tue 30-03-21	Fri 26-03-21	Tue 30-03-21	$4,125.00
772		**External Windows**	**3 days**	**Wed 31-03-21**	**Fri 02-04-21**	**Wed 31-03-21**	**Fri 02-04-21**	**$500.00**
773		Intallation of Aluminium Window Frames and Panels	3 days	Wed 31-03-21	Fri 02-04-21	Wed 31-03-21	Fri 02-04-21	$500.00
774		**Internal Wall**	**7 days**	**Wed 17-03-21**	**Thu 25-03-21**	**Wed 17-03-21**	**Thu 25-03-21**	**$1,359.15**
775		Internal Wall (Half Brick Including All sundries)	7 days	Wed 17-03-21	Thu 25-03-21	Wed 17-03-21	Thu 25-03-21	$1,359.15
776		**Internal Wall Finishes**	**14 days**	**Fri 26-03-21**	**Wed 14-04-21**	**Fri 26-03-21**	**Wed 14-04-21**	**$5,340.00**
777		Plastering of Walls&Columns	7 days	Fri 26-03-21	Mon 05-04-21	Fri 26-03-21	Mon 05-04-21	$2,848.00
778		Internal Wall Painting Finishes	7 days	Tue 06-04-21	Wed 14-04-21	Tue 06-04-21	Wed 14-04-21	$2,492.00
779		**Internal Floor Finishes**	**4 days**	**Thu 15-04-21**	**Tue 20-04-21**	**Thu 15-04-21**	**Tue 20-04-21**	**$1,068.00**
780		Cement Screed	2 days	Thu 15-04-21	Fri 16-04-21	Thu 15-04-21	Fri 16-04-21	$1,008.00
781		Internal Floor Grating	2 days	Mon 19-04-21	Tue 20-04-21	Mon 19-04-21	Tue 20-04-21	$60.00
782		**Internal Ceiling Finishes**	**3 days**	**Wed 21-04-21**	**Fri 23-04-21**	**Wed 21-04-21**	**Fri 23-04-21**	**$3,095.00**
783		Aluminium Ceiling Strip Finishes	3 days	Wed 21-04-21	Fri 23-04-21	Wed 21-04-21	Fri 23-04-21	$3,095.00

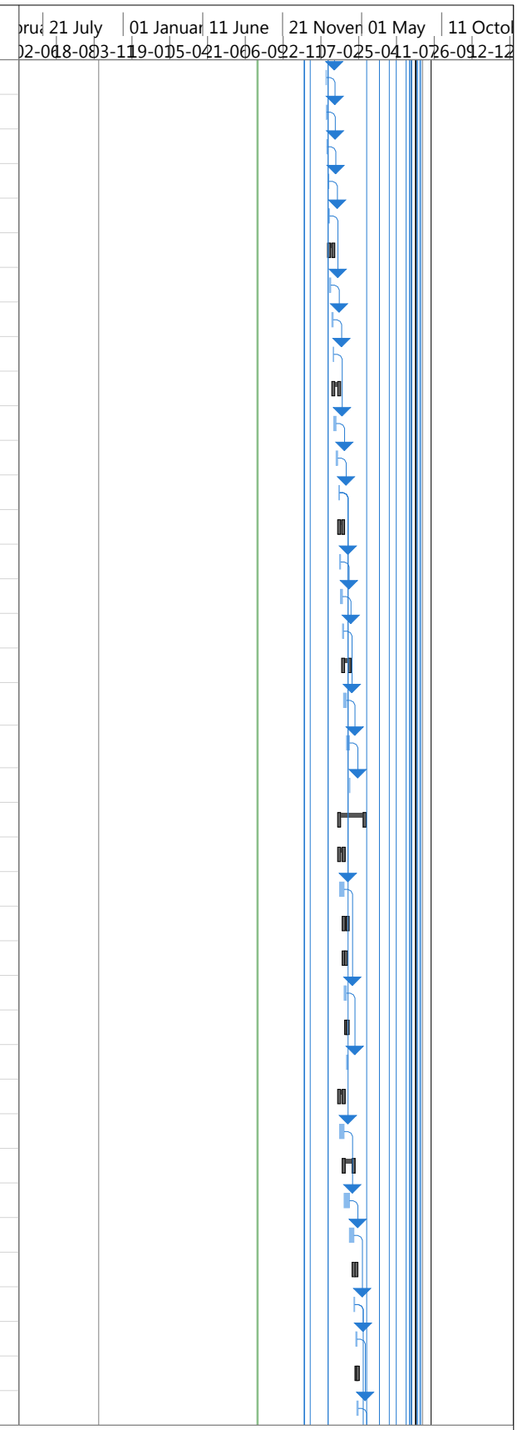

Project: Project1
Date: Thu 01-10-20


Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone

Disediakan oleh :

Disahkan oleh :

Disemak oleh :

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
784		**External Wall**	**7 days**	**Tue 27-04-21**	**Wed 05-05-21**	**Tue 27-04-21**	**Wed 05-05-21**	**$4,458.00**
785		External Plastering to External Wall	4 days	Tue 27-04-21	Fri 30-04-21	Tue 27-04-21	Fri 30-04-21	$2,400.00
786		External Wall Painting Finishes	3 days	Mon 03-05-21	Wed 05-05-21	Mon 03-05-21	Wed 05-05-21	$2,058.00
787		**External Floor Finishes**	**3 days**	**Mon 19-04-21**	**Wed 21-04-21**	**Mon 19-04-21**	**Wed 21-04-21**	**$288.00**
788		Cement Screed Finishes	3 days	Mon 19-04-21	Wed 21-04-21	Mon 19-04-21	Wed 21-04-21	$288.00
789		**External Ceiling Finishes**	**2 days**	**Thu 06-05-21**	**Fri 07-05-21**	**Thu 06-05-21**	**Fri 07-05-21**	**$1,365.00**
790		External Ceiling Finishes	2 days	Thu 06-05-21	Fri 07-05-21	Thu 06-05-21	Fri 07-05-21	$1,365.00
791		**RUMAH SAMPAH**	**20 days**	**Thu 01-04-21**	**Wed 28-04-21**	**Thu 01-04-21**	**Wed 28-04-21**	**$13,950.00**
792		Construction of Rumah Sampah	20 days	Thu 01-04-21	Wed 28-04-21	Thu 01-04-21	Wed 28-04-21	$13,950.00
793		**BANGUNAN PENCAWANG SESB**	**90 days**	**Wed 15-07-20**	**Tue 17-11-20**	**Wed 15-07-20**	**Tue 17-11-20**	**$27,900.00**
794		Construction of Bangunan Pencawang SESB by SESB	90 days	Wed 15-07-20	Tue 17-11-20	Wed 15-07-20	Tue 17-11-20	$27,900.00
795		**MECHANICAL WORKS**	**283 days**	**Fri 31-07-20**	**Tue 31-08-21**	**Fri 31-07-20**	**Tue 31-08-21**	**$425,791.20**
796		**Internal Cold Water Plumbing**	**280 days**	**Fri 31-07-20**	**Thu 26-08-21**	**Fri 31-07-20**	**Thu 26-08-21**	**$106,020.00**
797		**Internal Cold Water Plumbing Services for Balai Bomba**	**63 days**	**Thu 20-05-21**	**Mon 16-08-21**	**Thu 20-05-21**	**Mon 16-08-21**	**$75,330.00**
798		To supply and install HDPE pipe from suction pump to storage water tank	3 days	Thu 20-05-21	Mon 24-05-21	Thu 20-05-21	Mon 24-05-21	$2,325.00
799		Pumping System	3 days	Wed 09-06-21	Fri 11-06-21	Wed 09-06-21	Fri 11-06-21	$26,505.00
800		Suction Water Tank	3 days	Mon 14-06-21	Wed 16-06-21	Mon 14-06-21	Wed 16-06-21	$16,740.00
801		Elevated Water Tank	7 days	Thu 17-06-21	Fri 25-06-21	Thu 17-06-21	Fri 25-06-21	$8,370.00
802		To supply and install HDPE pipe to main distributor dropper	10 days	Thu 20-05-21	Wed 02-06-21	Thu 20-05-21	Wed 02-06-21	$2,790.00
803		To supply and install HDPE pipes to all sanitary Fittings	5 days	Tue 10-08-21	Mon 16-08-21	Tue 10-08-21	Mon 16-08-21	$18,600.00
804		**Internal Cold Water Plumbing Services for Rumah Sampah**	**3 days**	**Thu 29-04-21**	**Mon 03-05-21**	**Thu 29-04-21**	**Mon 03-05-21**	**$3,720.00**
805		To supply and install cold water plumbing system to Rumah Sampah	3 days	Thu 29-04-21	Mon 03-05-21	Thu 29-04-21	Mon 03-05-21	$3,720.00
806		**Internal Cold Water Plumbing Services for Menara Latihan**	**7 days**	**Thu 12-08-21**	**Fri 20-08-21**	**Thu 12-08-21**	**Fri 20-08-21**	**$1,860.00**
807		To supply and install cold water plumbing system to Menara Latihan	7 days	Thu 12-08-21	Fri 20-08-21	Thu 12-08-21	Fri 20-08-21	$1,860.00
808		**Other Items**	**280 days**	**Fri 31-07-20**	**Thu 26-08-21**	**Fri 31-07-20**	**Thu 26-08-21**	**$25,110.00**
809		Flushing of Cold Water System	2 days	Mon 23-08-21	Tue 24-08-21	Mon 23-08-21	Tue 24-08-21	$1,860.00
810		Preparation, Submission of Shop Drawings, Catalogue, Samples etc.	1 day	Fri 31-07-20	Sat 01-08-20	Fri 31-07-20	Sat 01-08-20	$1,860.00
811		Submission of Operation Manual and As Built	1 day	Fri 30-04-21	Fri 30-04-21	Fri 30-04-21	Fri 30-04-21	$1,860.00
812		Testing & Commisioning	2 days	Wed 25-08-21	Thu 26-08-21	Wed 25-08-21	Thu 26-08-21	$7,440.00
813		Painting of Complete System, Identification, name plates etc	2 days	Mon 03-05-21	Tue 04-05-21	Mon 03-05-21	Tue 04-05-21	$930.00
814		Privide Manufacturer's Warranty	1 day	Fri 30-04-21	Sat 01-05-21	Fri 30-04-21	Sat 01-05-21	$1,860.00
815		Carry out Schedule Maintenance during DLP	1 day	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	$9,300.00
816		**Internal Sanitary plumbing Services**	**154 days**	**Fri 18-12-20**	**Wed 21-07-21**	**Fri 18-12-20**	**Wed 21-07-21**	**$67,518.00**
817		Construction of Internal Building Inpection Chamber (IC A & B)	7 days	Tue 13-07-21	Wed 21-07-21	Tue 13-07-21	Wed 21-07-21	$8,370.00
818		Construction of Internal Building Inpection Chamber (IC C at Rumah Sampah)	3 days	Thu 29-04-21	Mon 03-05-21	Thu 29-04-21	Mon 03-05-21	$4,185.00
819		100mm dia UPVC discharge pipes connect to adjacent manholes	7 days	Thu 04-02-21	Fri 12-02-21	Thu 04-02-21	Fri 12-02-21	$4,650.00
820		Supply and Install 225mm dia VCP Pipes to C&S Manholes	10 days	Thu 04-02-21	Wed 17-02-21	Thu 04-02-21	Wed 17-02-21	$8,835.00
821		0.75mm upvc pipes (underground floor traps to gully traps)	3 days	Fri 18-12-20	Tue 22-12-20	Fri 18-12-20	Tue 22-12-20	$5,208.00
822		100mm UPVC Brown pipes (on ground WC and Urinal discharged to adjacent IC	3 days	Fri 18-12-20	Tue 22-12-20	Fri 18-12-20	Tue 22-12-20	$5,208.00

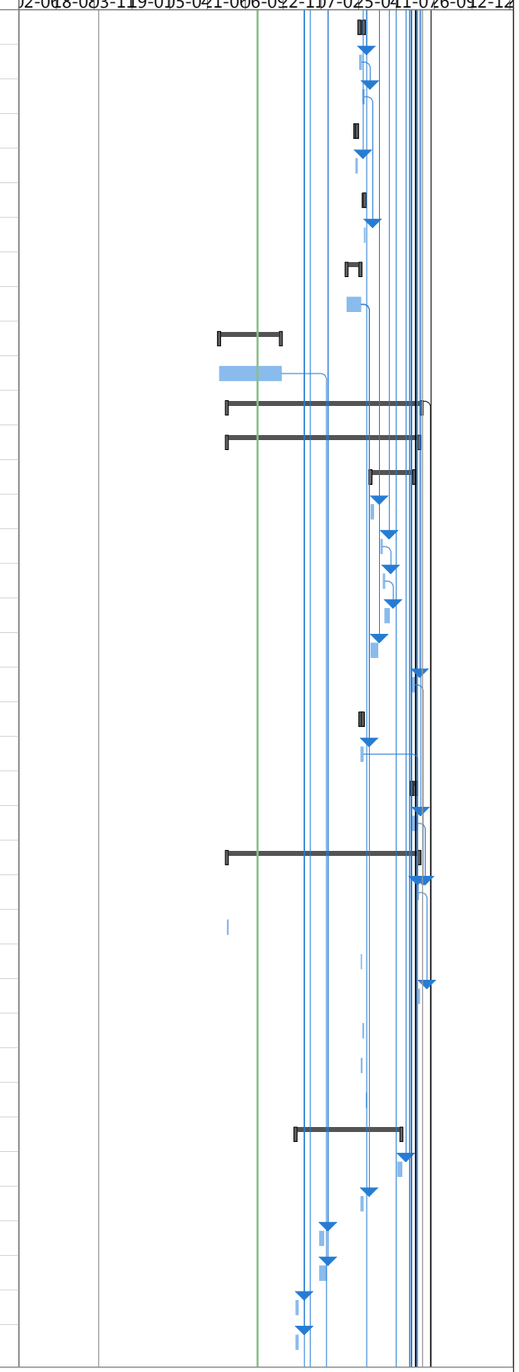

Project: Project1
Date: Thu 01-10-20


Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	

Disediakan oleh :

Disahkan oleh :

Disemak oleh :

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
823		0.75mm upvc pipes (undergroundground sink and wash basin to gully traps)	1 day	Fri 18-12-20	Fri 18-12-20	Fri 18-12-20	Fri 18-12-20	$5,952.00
824		100mm and 75mm vertical soil pipes for aboveground work	7 days	Wed 30-12-20	Thu 07-01-21	Wed 30-12-20	Thu 07-01-21	$9,300.00
825		**Supply and Install horizantal 100mm dia soil and 40mm dia waste pipes for above ground works**	**15 days**	**Mon 26-04-21**	**Fri 14-05-21**	**Mon 26-04-21**	**Fri 14-05-21**	**$9,300.00**
826		Basin/Sink Tap	3 days	Mon 26-04-21	Wed 28-04-21	Mon 26-04-21	Wed 28-04-21	$1,860.00
827		Water Closet	3 days	Thu 29-04-21	Mon 03-05-21	Thu 29-04-21	Mon 03-05-21	$1,860.00
828		Shower	3 days	Tue 04-05-21	Thu 06-05-21	Tue 04-05-21	Thu 06-05-21	$1,860.00
829		Urinal	3 days	Fri 07-05-21	Tue 11-05-21	Fri 07-05-21	Tue 11-05-21	$1,860.00
830		Floor Traps & Other Fittings	3 days	Wed 12-05-21	Fri 14-05-21	Wed 12-05-21	Fri 14-05-21	$1,860.00
831		**Other Items**	**15 days**	**Mon 17-05-21**	**Fri 04-06-21**	**Mon 17-05-21**	**Fri 04-06-21**	**$6,510.00**
832		**Testing & Commissioning**	**15 days**	**Mon 17-05-21**	**Fri 04-06-21**	**Mon 17-05-21**	**Fri 04-06-21**	**$6,510.00**
833		Submission of Test Result before Final Testing	1 day	Mon 17-05-21	Mon 17-05-21	Mon 17-05-21	Mon 17-05-21	$4,650.00
834		Leak Test, Flow Test	7 days	Tue 18-05-21	Wed 26-05-21	Tue 18-05-21	Wed 26-05-21	$930.00
835		Training Employer Personnel	7 days	Thu 27-05-21	Fri 04-06-21	Thu 27-05-21	Fri 04-06-21	$930.00
836		**Air Conditioning and Mechanical Services**	**149 days**	**Mon 01-02-21**	**Thu 26-08-21**	**Mon 01-02-21**	**Thu 26-08-21**	**$76,390.20**
837		**Balai Bomba**	**22 days**	**Tue 20-07-21**	**Wed 18-08-21**	**Tue 20-07-21**	**Wed 18-08-21**	**$51,745.20**
838		To supply and Install Ceiling Inverter Type Air Cooled Split Unit	15 days	Tue 20-07-21	Mon 09-08-21	Tue 20-07-21	Mon 09-08-21	$24,105.60
839		To Supply and Install Wall Inverter Type Air Cooled Type Split Unit	7 days	Tue 10-08-21	Wed 18-08-21	Tue 10-08-21	Wed 18-08-21	$16,386.60
840		To Supply and Install Exhaust Fan (Propeller Type with Automatic Shutter)	5 days	Tue 20-07-21	Mon 26-07-21	Tue 20-07-21	Mon 26-07-21	$2,883.00
841		To Supply and Install Exhaust Fan (Ceiling Type)	3 days	Tue 27-07-21	Thu 29-07-21	Tue 27-07-21	Thu 29-07-21	$4,650.00
842		Kitchen Range Hood	2 days	Fri 30-07-21	Mon 02-08-21	Fri 30-07-21	Mon 02-08-21	$3,720.00
843		**Menara Latihan**	**9 days**	**Thu 05-08-21**	**Tue 17-08-21**	**Thu 05-08-21**	**Tue 17-08-21**	**$5,580.00**
844		Smoke Exhaust Hood	3 days	Thu 05-08-21	Mon 09-08-21	Thu 05-08-21	Mon 09-08-21	$2,790.00
845		Smoke Exhaust Fan	3 days	Tue 10-08-21	Thu 12-08-21	Tue 10-08-21	Thu 12-08-21	$2,790.00
846		GI Duct c/w External Grill	3 days	Fri 13-08-21	Tue 17-08-21	Fri 13-08-21	Tue 17-08-21	$0.00
847		**Other Items**	**149 days**	**Mon 01-02-21**	**Thu 26-08-21**	**Mon 01-02-21**	**Thu 26-08-21**	**$19,065.00**
848		**Testing & Commissioning**	**149 days**	**Mon 01-02-21**	**Thu 26-08-21**	**Mon 01-02-21**	**Thu 26-08-21**	**$19,065.00**
849		Submission to SO before Final Test	1 day	Wed 18-08-21	Wed 18-08-21	Wed 18-08-21	Wed 18-08-21	$465.00
850		All Equipment Test	3 days	Thu 19-08-21	Mon 23-08-21	Thu 19-08-21	Mon 23-08-21	$4,650.00
851		Training of Employer's Personnel	3 days	Tue 24-08-21	Thu 26-08-21	Tue 24-08-21	Thu 26-08-21	$930.00
852		Submission of Shop Drawings, Catalogue, Brochures, Samples etc	1 day	Mon 01-02-21	Mon 01-02-21	Mon 01-02-21	Mon 01-02-21	$1,860.00
853		Submission of Operation Manual and As Built Drawings	1 day	Tue 24-08-21	Tue 24-08-21	Tue 24-08-21	Tue 24-08-21	$1,860.00
854		Carry out Schedule Maintenance during DLP	1 day	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	$9,300.00
855		**Fire Protection Services**	**132 days**	**Mon 01-03-21**	**Tue 31-08-21**	**Mon 01-03-21**	**Tue 31-08-21**	**$27,063.00**
856		Portable Fire Extinguisher for all Buildings	3 days	Mon 26-07-21	Wed 28-07-21	Mon 26-07-21	Wed 28-07-21	$5,859.00
857		Dry riser System	14 days	Thu 05-08-21	Tue 24-08-21	Thu 05-08-21	Tue 24-08-21	$11,160.00
858		Drain Outlet Pipe to Kolah Air	7 days	Thu 05-08-21	Fri 13-08-21	Thu 05-08-21	Fri 13-08-21	$4,650.00
859		**Other Item**	**132 days**	**Mon 01-03-21**	**Tue 31-08-21**	**Mon 01-03-21**	**Tue 31-08-21**	**$5,394.00**
860		**Testing & Commissioning**	**132 days**	**Mon 01-03-21**	**Tue 31-08-21**	**Mon 01-03-21**	**Tue 31-08-21**	**$5,394.00**
861		Submission of Test Result Before Final Testing	1 day	Wed 25-08-21	Wed 25-08-21	Wed 25-08-21	Wed 25-08-21	$930.00

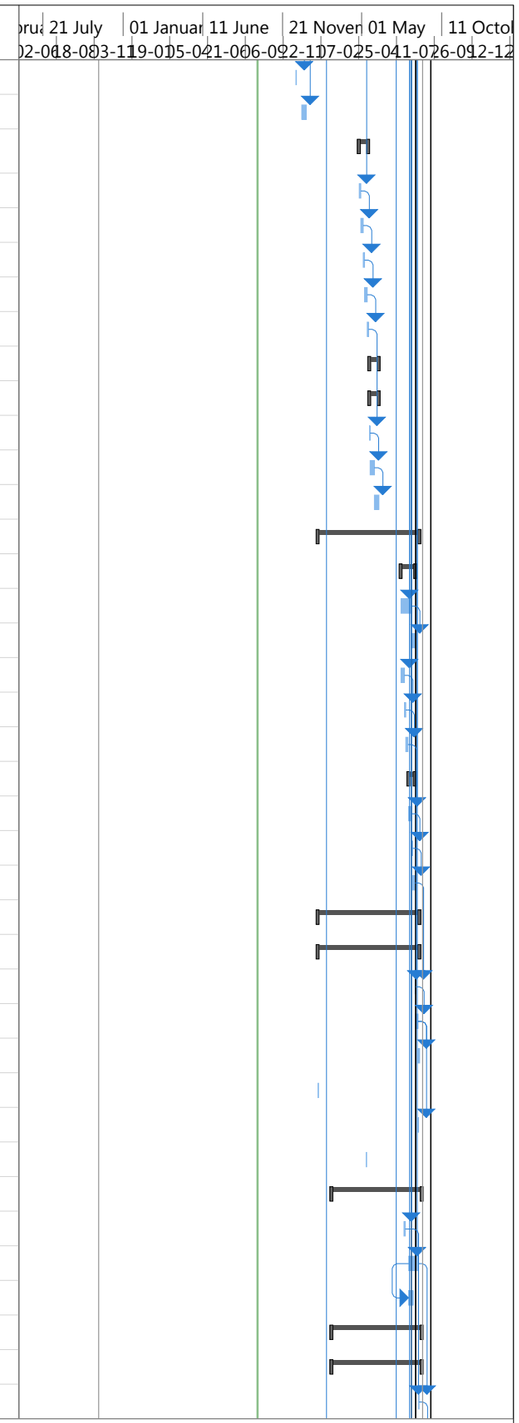

Project: Project1
Date: Thu 01-10-20


Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	

Disediakan oleh :

Disahkan oleh :

Disemak oleh :

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
862		All Equipment Test	2 days	Thu 26-08-21	Fri 27-08-21	Thu 26-08-21	Fri 27-08-21	$930.00
863		Training for Employer's Personnel	2 days	Mon 30-08-21	Tue 31-08-21	Mon 30-08-21	Tue 31-08-21	$930.00
864		Submission of Shop Drawings, Catalogue, Brochures, Samples etc	1 day	Mon 01-03-21	Mon 01-03-21	Mon 01-03-21	Mon 01-03-21	$930.00
865		Submission of Operation Manual and As Built	1 day	Mon 30-08-21	Mon 30-08-21	Mon 30-08-21	Mon 30-08-21	$930.00
866		Schedule Maintenance During DLP	1 day	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	$744.00
867		**Motorized Roller Shutter**	**119 days**	**Mon 15-03-21**	**Thu 26-08-21**	**Mon 15-03-21**	**Thu 26-08-21**	**$148,800.00**
868		To Supply and Install 4 Nos of Motorized Roller Shutter	20 days	Mon 26-07-21	Fri 20-08-21	Mon 26-07-21	Fri 20-08-21	$130,200.00
869		**Other Items**	**119 days**	**Mon 15-03-21**	**Thu 26-08-21**	**Mon 15-03-21**	**Thu 26-08-21**	**$18,600.00**
870		**Testing & Commissioning**	**119 days**	**Mon 15-03-21**	**Thu 26-08-21**	**Mon 15-03-21**	**Thu 26-08-21**	**$18,600.00**
871		Submission of Test Result Before Final Testing	1 day	Mon 23-08-21	Mon 23-08-21	Mon 23-08-21	Mon 23-08-21	$2,790.00
872		All Equipment Test	1 day	Tue 24-08-21	Tue 24-08-21	Tue 24-08-21	Tue 24-08-21	$930.00
873		Training for Employer's Personnel	1 day	Wed 25-08-21	Wed 25-08-21	Wed 25-08-21	Wed 25-08-21	$1,860.00
874		Submission of Shop Drawings, Catalogue, Brochures, Samples etc	1 day	Mon 15-03-21	Mon 15-03-21	Mon 15-03-21	Mon 15-03-21	$930.00
875		Submission of Operation Manual and As Built	1 day	Thu 26-08-21	Thu 26-08-21	Thu 26-08-21	Thu 26-08-21	$930.00
876		Schedule Maintenance During DLP	1 day	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	$11,160.00
877		**ELECTRICAL SERVICES**	**139 days**	**Thu 18-02-21**	**Tue 31-08-21**	**Thu 18-02-21**	**Tue 31-08-21**	**$1,051,513.80**
878		**Electrical Services for Internal Works**	**76 days**	**Mon 10-05-21**	**Mon 23-08-21**	**Mon 10-05-21**	**Mon 23-08-21**	**$357,966.30**
879		Electrical Works	30 days	Wed 23-06-21	Tue 03-08-21	Wed 23-06-21	Tue 03-08-21	$318,441.30
880		**Other Works**	**76 days**	**Mon 10-05-21**	**Mon 23-08-21**	**Mon 10-05-21**	**Mon 23-08-21**	**$39,525.00**
881		Galvanized Trunking	7 days	Wed 04-08-21	Thu 12-08-21	Wed 04-08-21	Thu 12-08-21	$13,950.00
882		Fire Barrier Materials for Floor Slab and Firewall	7 days	Wed 04-08-21	Thu 12-08-21	Wed 04-08-21	Thu 12-08-21	$3,255.00
883		Pre Testing	3 days	Fri 13-08-21	Tue 17-08-21	Fri 13-08-21	Tue 17-08-21	$9,300.00
884		Testing & Commissioning	3 days	Wed 18-08-21	Fri 20-08-21	Wed 18-08-21	Fri 20-08-21	$1,860.00
885		CPR Chart at Bilik Servis	1 day	Mon 23-08-21	Mon 23-08-21	Mon 23-08-21	Mon 23-08-21	$465.00
886		Electrical Schematic Chart at Bilik Servis	1 day	Mon 23-08-21	Mon 23-08-21	Mon 23-08-21	Mon 23-08-21	$1,395.00
887		LV incoming Cable	2 days	Fri 13-08-21	Mon 16-08-21	Fri 13-08-21	Mon 16-08-21	$4,650.00
888		River Sand at Bilik Servis	2 days	Tue 17-08-21	Wed 18-08-21	Tue 17-08-21	Wed 18-08-21	$1,860.00
889		Service & Maintenace during DLP	1 day	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	$2,790.00
890		**Telephone Services for Internal works**	**82 days**	**Mon 10-05-21**	**Tue 31-08-21**	**Mon 10-05-21**	**Tue 31-08-21**	**$81,049.50**
891		Telephone Works	14 days	Tue 20-07-21	Fri 06-08-21	Tue 20-07-21	Fri 06-08-21	$21,669.00
892		**Other Work**	**74 days**	**Mon 10-05-21**	**Thu 19-08-21**	**Mon 10-05-21**	**Thu 19-08-21**	**$10,695.50**
893		Galvanized Trunking	3 days	Mon 09-08-21	Wed 11-08-21	Mon 09-08-21	Wed 11-08-21	$1,860.00
894		Fire Barrier Materials in Riser	3 days	Thu 12-08-21	Mon 16-08-21	Thu 12-08-21	Mon 16-08-21	$930.50
895		Pre-Testing	2 days	Tue 17-08-21	Wed 18-08-21	Tue 17-08-21	Wed 18-08-21	$2,790.00
896		Testing & Commissioning	1 day	Thu 19-08-21	Thu 19-08-21	Thu 19-08-21	Thu 19-08-21	$1,860.00
897		Painting and Labelling	2 days	Tue 17-08-21	Wed 18-08-21	Tue 17-08-21	Wed 18-08-21	$1,395.00
898		Services and Maintenance During DLP	1 day	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	$1,860.00
899		**Information Communication Technology System**	**17 days**	**Mon 09-08-21**	**Tue 31-08-21**	**Mon 09-08-21**	**Tue 31-08-21**	**$48,685.00**
900		**ICT Main Equipment**	**17 days**	**Mon 09-08-21**	**Tue 31-08-21**	**Mon 09-08-21**	**Tue 31-08-21**	**$48,685.00**
901		Backbone Fibre	7 days	Mon 09-08-21	Tue 17-08-21	Mon 09-08-21	Tue 17-08-21	$7,440.00

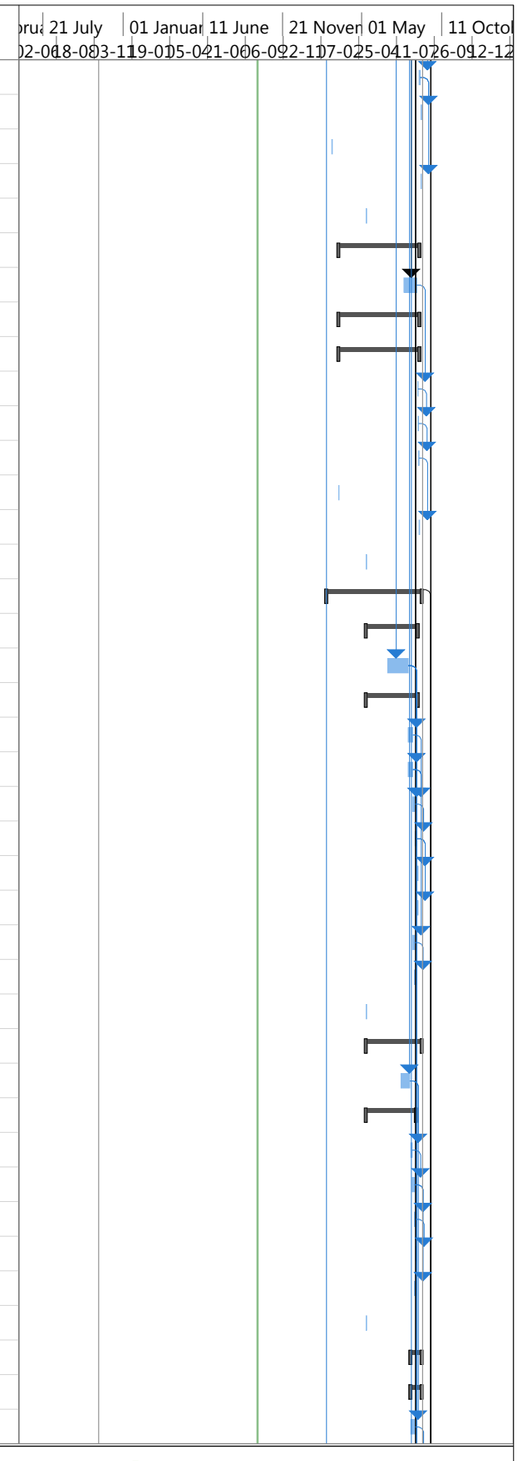

Project: Project1
Date: Thu 01-10-20


Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone

Disediakan oleh :

Disahkan oleh :

Disemak oleh :

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
902		Horizantal Cabling	5 days	Wed 18-08-21	Tue 24-08-21	Wed 18-08-21	Tue 24-08-21	$17,065.00
903		Network Switch	5 days	Wed 25-08-21	Tue 31-08-21	Wed 25-08-21	Tue 31-08-21	$24,180.00
904		**Lightning Protection System**	**78 days**	**Mon 10-05-21**	**Wed 25-08-21**	**Mon 10-05-21**	**Wed 25-08-21**	**$68,401.50**
905		Lightning Protection System	14 days	Mon 26-07-21	Thu 12-08-21	Mon 26-07-21	Thu 12-08-21	$62,821.50
906		**Other Works**	**78 days**	**Mon 10-05-21**	**Wed 25-08-21**	**Mon 10-05-21**	**Wed 25-08-21**	**$5,580.00**
907		Galvanized Trunking/Cable Tray	3 days	Fri 13-08-21	Tue 17-08-21	Fri 13-08-21	Tue 17-08-21	$930.00
908		Fire Barrier Material Through Floor	3 days	Wed 18-08-21	Fri 20-08-21	Wed 18-08-21	Fri 20-08-21	$465.00
909		Pre Testing	2 days	Mon 23-08-21	Tue 24-08-21	Mon 23-08-21	Tue 24-08-21	$1,395.00
910		Testing & Commissioning	1 day	Wed 25-08-21	Wed 25-08-21	Wed 25-08-21	Wed 25-08-21	$465.00
911		Painting and Labelling	1 day	Mon 23-08-21	Mon 23-08-21	Mon 23-08-21	Mon 23-08-21	$930.00
912		Service and Maintenace during DLP	1 day	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	$1,395.00
913		**Extra Low Voltage System**	**78 days**	**Mon 10-05-21**	**Wed 25-08-21**	**Mon 10-05-21**	**Wed 25-08-21**	**$66,867.00**
914		Public Address System (Main Equipment)	3 days	Wed 04-08-21	Fri 06-08-21	Wed 04-08-21	Fri 06-08-21	$25,110.00
915		Public Address System (Internal Works)	5 days	Mon 09-08-21	Fri 13-08-21	Mon 09-08-21	Fri 13-08-21	$17,391.00
916		MATV System	7 days	Wed 04-08-21	Thu 12-08-21	Wed 04-08-21	Thu 12-08-21	$17,391.00
917		**Other Works**	**78 days**	**Mon 10-05-21**	**Wed 25-08-21**	**Mon 10-05-21**	**Wed 25-08-21**	**$6,975.00**
918		Galvanized Trunking/Cable Tray	3 days	Fri 13-08-21	Tue 17-08-21	Fri 13-08-21	Tue 17-08-21	$1,395.00
919		Fire Barrier Material Through Riser	2 days	Wed 18-08-21	Thu 19-08-21	Wed 18-08-21	Thu 19-08-21	$930.00
920		Pre Testing	2 days	Fri 20-08-21	Mon 23-08-21	Fri 20-08-21	Mon 23-08-21	$1,860.00
921		Testing & Commissioning	2 days	Tue 24-08-21	Wed 25-08-21	Tue 24-08-21	Wed 25-08-21	$465.00
922		Painting and Labelling	1 day	Fri 20-08-21	Fri 20-08-21	Fri 20-08-21	Fri 20-08-21	$465.00
923		Service and Maintenace during DLP	1 day	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	$1,860.00
924		**Generating System**	**43 days**	**Tue 02-03-21**	**Thu 29-04-21**	**Tue 02-03-21**	**Thu 29-04-21**	**$74,400.00**
925		To Supply 25KVA 50Hz 415V Sound Proof All Weather 3 Phase Generator Set	7 days	Thu 01-04-21	Fri 09-04-21	Thu 01-04-21	Fri 09-04-21	$37,200.00
926		Built In AMF Control Board Panel	3 days	Mon 12-04-21	Wed 14-04-21	Mon 12-04-21	Wed 14-04-21	$23,250.00
927		Electrical Submain Cabling From AMF to Generator	3 days	Thu 15-04-21	Mon 19-04-21	Thu 15-04-21	Mon 19-04-21	$1,860.00
928		Factory Testing for Genset	1 day	Tue 02-03-21	Tue 02-03-21	Tue 02-03-21	Tue 02-03-21	$9,300.00
929		Submission For Authority Approval	1 day	Wed 10-03-21	Wed 10-03-21	Wed 10-03-21	Wed 10-03-21	$930.00
930		MCCB Box at Ruang Jentera	7 days	Tue 20-04-21	Wed 28-04-21	Tue 20-04-21	Wed 28-04-21	$930.00
931		Testing & Commissioning	1 day	Thu 29-04-21	Thu 29-04-21	Thu 29-04-21	Thu 29-04-21	$930.00
932		**Electrical Services for Main Equipments and External Works**	**55 days**	**Thu 18-02-21**	**Wed 05-05-21**	**Thu 18-02-21**	**Wed 05-05-21**	**$248,728.50**
933		**Electrical Main Equipments and Infra Works**	**55 days**	**Thu 18-02-21**	**Wed 05-05-21**	**Thu 18-02-21**	**Wed 05-05-21**	**$248,728.50**
934		Electrical Main Switch and Submain Cable	25 days	Thu 18-02-21	Wed 24-03-21	Thu 18-02-21	Wed 24-03-21	$130,200.00
935		External Lighting and Cabling Works	25 days	Thu 01-04-21	Wed 05-05-21	Thu 01-04-21	Wed 05-05-21	$118,528.50
936		**Telephone Service For Main Equipment and External Works**	**51 days**	**Mon 01-03-21**	**Mon 10-05-21**	**Mon 01-03-21**	**Mon 10-05-21**	**$93,000.00**
937		External Telephone and Infra Works	30 days	Mon 01-03-21	Fri 09-04-21	Mon 01-03-21	Fri 09-04-21	$83,700.00
938		**Other Works**	**21 days**	**Mon 12-04-21**	**Mon 10-05-21**	**Mon 12-04-21**	**Mon 10-05-21**	**$9,300.00**
939		Galvanized Trunking/Cable Tray	3 days	Mon 12-04-21	Wed 14-04-21	Mon 12-04-21	Wed 14-04-21	$2,790.00
940		Fire Barrier Material Through Riser Room	2 days	Thu 15-04-21	Fri 16-04-21	Thu 15-04-21	Fri 16-04-21	$930.00
941		Pre Testing	1 day	Mon 19-04-21	Mon 19-04-21	Mon 19-04-21	Mon 19-04-21	$1,860.00

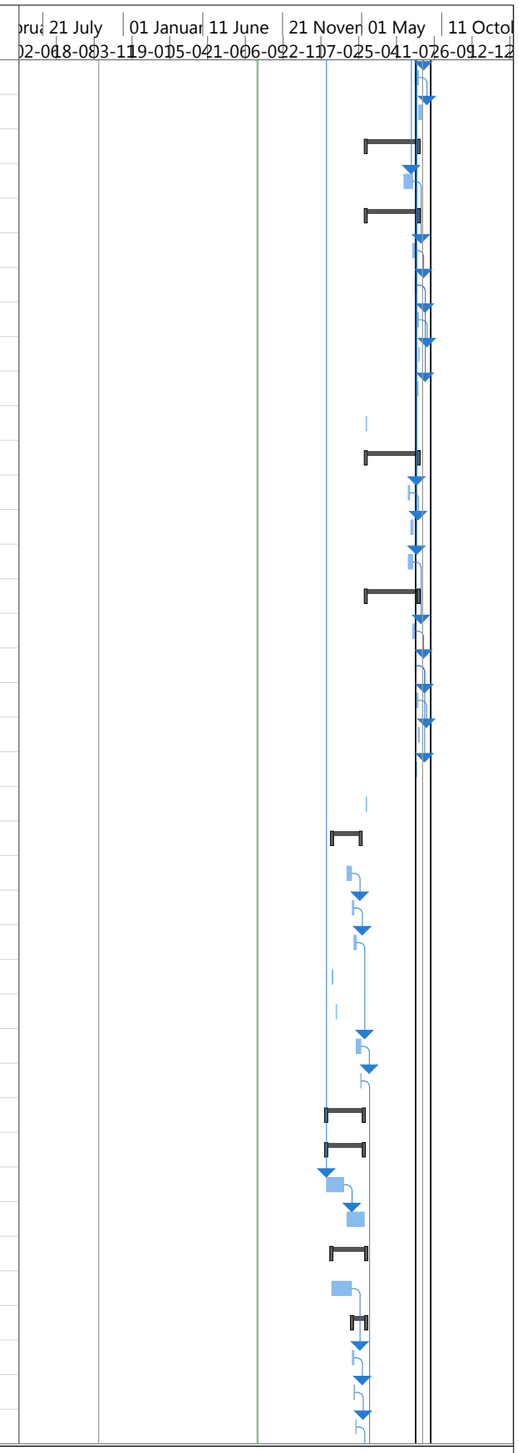

Project: Project1
Date: Thu 01-10-20


Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	

Disediakan oleh :

Disahkan oleh :

Disemak oleh :

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Cost
942		Testing & Commissioning	2 days	Tue 20-04-21	Wed 21-04-21	Tue 20-04-21	Wed 21-04-21	$1,395.00
943		Painting and Labelling	2 days	Thu 22-04-21	Fri 23-04-21	Thu 22-04-21	Fri 23-04-21	$930.00
944		Service and Maintenace during DLP	1 day	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	Mon 10-05-21	$1,395.00
945		**General Work for Electrical Service**	**10 days**	**Mon 26-04-21**	**Fri 07-05-21**	**Mon 26-04-21**	**Fri 07-05-21**	**$61,101.00**
946		To Provide Switchroom with peripherals, labels and Signages	1 day	Mon 26-04-21	Mon 26-04-21	Mon 26-04-21	Mon 26-04-21	$5,766.00
947		Circuit Numbering System and Schematic Diagram for all DSB and MSB	1 day	Fri 30-04-21	Fri 30-04-21	Fri 30-04-21	Fri 30-04-21	$2,790.00
948		Shop Drawings	1 day	Mon 03-05-21	Mon 03-05-21	Mon 03-05-21	Mon 03-05-21	$4,650.00
949		As-Built Drawings, Catalogue and Operation Manual	1 day	Wed 05-05-21	Wed 05-05-21	Wed 05-05-21	Wed 05-05-21	$4,650.00
950		Liason with Local Authority	1 day	Thu 06-05-21	Thu 06-05-21	Thu 06-05-21	Thu 06-05-21	$1,860.00
951		Practical Training and maintenance of the operators	7 days	Tue 27-04-21	Wed 05-05-21	Tue 27-04-21	Wed 05-05-21	$3,255.00
952		Sample Board, Sample workmanship	1 day	Tue 27-04-21	Tue 27-04-21	Tue 27-04-21	Tue 27-04-21	$930.00
953		Breaking and Hacking and Make Good of Brickwalls, floor, slab and other civil works	1 day	Fri 30-04-21	Fri 30-04-21	Fri 30-04-21	Fri 30-04-21	$4,650.00
954		Allow Compliance to Specifications and Drawings.	1 day	Fri 07-05-21	Fri 07-05-21	Fri 07-05-21	Fri 07-05-21	$32,550.00
955		**WANG PERUNTUKAN SEMENTARA**	**65 days**	**Fri 01-01-21**	**Thu 01-04-21**	**Fri 01-01-21**	**Thu 01-04-21**	**$520,000.00**
956		Contribution to Local & Utility Authority	1 day	Mon 01-03-21	Mon 01-03-21	Mon 01-03-21	Mon 01-03-21	$295,000.00
957		Loose Furniture	1 day	Fri 01-01-21	Fri 01-01-21	Fri 01-01-21	Fri 01-01-21	$75,000.00
958		Lanskap	1 day	Wed 03-03-21	Wed 03-03-21	Wed 03-03-21	Wed 03-03-21	$20,000.00
959		Papan Tanda Bangunan	1 day	Thu 01-04-21	Thu 01-04-21	Thu 01-04-21	Thu 01-04-21	$50,000.00
960		Off Site Work	1 day	Thu 01-04-21	Thu 01-04-21	Thu 01-04-21	Thu 01-04-21	$80,000.00
961		PROJECT FINISH	0 days	Wed 01-09-21	Wed 01-09-21	Wed 01-09-21	Wed 01-09-21	$0.00

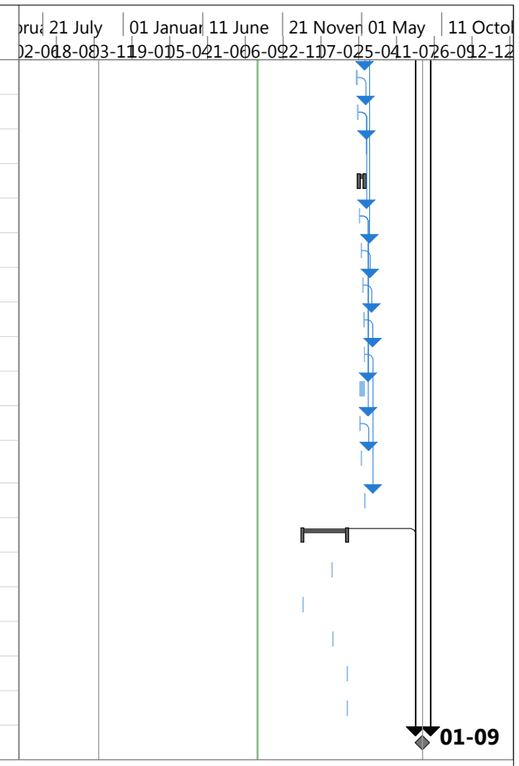

Project: Project1
Date: Thu 01-10-20

Task	Project Summary	Manual Task	Start-only	Deadline			
Split	Inactive Task	Duration-only	Finish-only	Progress			
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress			
Summary	Inactive Summary	Manual Summary	External Milestone				

Disediakan oleh :

Disahkan oleh :

Disemak oleh :
